

Law (1925) Department.
Education

Review SERIES.

G.O. No. 1518

DATED 3/9/25

[Despatch Abstract.]

Subsidy

Construction of elementary school buildings - Taluk Board, Salem -
disbursement - Sanctioned.

BACK PAPERS.

G.O.	No.	Department.	Date.	G.O.	No.	Department.	Date.

FURTHER PAPERS.

G.O.	No.	Department.	Date.	G.O.	No.	Department.	Date.



LOCAL FUND DEPARTMENT.

10: _____

17389

Received _____

192 . Registered _____

192

SUBJECT.

Requesting sanction the balance of amount Rs 1645 for Elampillai boys school building.

17389C.1 Ctu
19-6-25

ENCLOSURES.
No. _____
Spare copies _____

Ref. No. 841/Petrn of 21

Station Salem, Dated the 2nd June 1925

From

M. R. Ry. B. A. R. Kandaswamy Chettiar Avl.,
President, Taluk Board,
SALEM.

Lawton

To

The Secretary to Government,
LOCAL-SELF GOVERNMENT DEPARTMENT,
Fort St. George, MADRAS.

Through

The President,
District Board, Salem.

Sir,

In continuation of this office letter No. 841/Petrn of 21

dated 6--3--25 and with reference to G.O.No. 2014 Press dated 27th December 1924, regarding the construction of a school building at Elampillai, I have the honour to state that in G.O. 1576 dated 16th December 1919 an amount of Rs. 2000 was sanctioned for the above work. The amount could not be spent within the prescribed period, for the reason that a suitable site was not available in a favourable locality at a reasonable cost by private negotiation, hence the amount had to be surrendered in March 21 in consequence of G.O. No. 366 L. & M. dated 28th February 21.

(v)

G

of 1925

Again the surrendered amount was sanctioned in G.O. No. 2014 Press dated 27th December 1924 and thereupon, the work was commenced and the value of work done in the construction of the building up to February 25 was Rs. 650 Out of the above sum Rs. 355 was sanctioned in G.O. No.

(I) 352 dated 13-3-25 and paid for the above work. The building has been completed and is actually under occupation.

2. Under the above circumstances, I request that the Government will be pleased to sanction the balance of amount (Viz) Rs. 2000--355= 1645 in the current year. Necessary certificate is enclosed.

I have the honour to be,

Sir,

Your most obedient servant,

V.K.5-6-25.
me
5/6.

For President.
10 JUN 1925

Buildings - Elampillai - boy's School - requesting sanction - the balance of Rs 1645-0-0 -

Enclt. N. Dis 2372-25 E 8 - 625

Forwarded
17 6 25
President

16.6.25
15/6

15/6/25

To The Secretary to
Govt. L & T. Govt. Dept
Madras

2
Certificate.

Certify that the work of constructing a school building at Elampillai has been completed and that the work has been properly executed.

V.K.5-6-25.

me
5/6.

For President.
10 JUN 1925

Building - Elampillai - boy's School - requesting sanction - the balance of Rs 1645-0-0 -

C. no 2175A

Law (Est. Dep)

Memo

No 2175 A-1847-25

Building grant - construction of School building at Elampillai - Letter from the P.T.B. Saleem no 841 Petal 21 of 2.6.25

The President is requested to report the actual cost of constructing the School building at Elampillai.

AP 25/6/25
MH 30/6/25

AP 30/6/25
MH 30/6/25

V.T.P. 1.7


Lo The P.T.B. Saleem 4/7/25
R: after one month

Note

In G.O. no 2014 L.E.D. 27.12.24 the Govt have provided a grant not exceeding Rs 2000 towards the cost of the building in question. A sum of Rs 355 has already been disbursed. The balance of Rs 1645 will be paid only if the cost of the building amounts to Rs 2000 or more. The P.T.B. may be requested to report the actual cost of construction.

DESPATCHED

6 JUL 1925



AP 25/6/25
MH 30/6/25

1592
355

2372-25 E

16.6.25
19/6/25

To The Secretary to Govt. L & T. Govt Dept. Madras

DEPARTMENT.

3092A
L. C. 2148B
17/8/25

Received



Registered

192

Subject.



Requesting-disbursement--balance of subsidy-

construction of Elampillai school

Salem Taluk Board.

ENCLOSURES.

No.

Spare copies.

Ref. No. 841/Petn of 21

Station Salem, Dated the 20th July 1925.

From (Name) M.R. Ry. B.A.R. Kandasami Chettiar Ayl.,
(Designation) President, Taluk Board, Salem.

To The Secretary to the Government of Madras,

Law Education Department.
Fort St. George, MADRAS.

Sir,
Through,

The President,
District Board, SALEM.

Sir,

With reference to Government Memorandum
No. 2175 A--1 dated 4th July 1925, I have the honour to
report that the actual cost of constructing a school
building at Elampillai comes to Rs. 1591--12--0. The
completion report is enclosed for favour of perusal.

P.T.O.

I request that early orders may be passed for disbursing the balance of subsidy promised in G.O. No. 352 M.D. dated 13-3-25.

I have the honour to be,

Sir,

Your most obedient servant,

V.K.21-7-25.

NXB 3120-25-A.

Forwarded.

Salem District Board
Dated 8.25
President
9.8.25
10.8.25

To. Secretary, Govt. of Madras.
L. Gov. B. Secy.

Salem
Taluk Board
26 JUL 1925

L.F. Form No. 77. (Outer Sheet.)

1196/02/25
e.g. 35/S.T.B. of March 25

Completion Report of Works accounted for by sub-heads, and of which the total estimated cost has been exceeded by more than 5 per cent.

Taluk Salem

Name of Work Constructing an elementary school building at Selampally

Amount of Estimate, Rs. 1,615/-

Expenditure, Rs. 1,591-12-2

Difference, Rs. 23-4-0

Percentage of Excess (if any) 1.42%

Date of Commencement January 1925

Date of Completion March 1925

Forwarded to the Deputy Collector, Salem
Audit Branch, for verification and transmission to the President, Salem Taluk Board.

Station Salem

Dated 7.5.1925 Local Fund Engineer.

The figures in the columns 'As estimated' and 'As executed' have been checked and found correct, with the exception of the items altered in red ink.

Dated 29.5.1925 Audit Clerk.

Forwarded to the President, Salem Taluk Board.

Station Salem
Dated 29.5.1925 M. Chaffar Khan
Deputy Collector.
2 dt accounts

Excess expenditure sanctioned by the Board in Resolution No. ---, dated --- 192

President, --- Board.

Hoe & Co., Madras, - 28-5-1923.

Machung

noe President
15/6.

L.F. Form No. 77.—(Outer Sheet.)

Sub-heads of Estimate.	As estimated.						As executed	
	Quantity.		Rate.		Amount.		Quantity,	Rate.
	2	3	4	5	6	7	8	9
		Rs.	A. P.	Rs.	A. P.		Rs.	A. P.
Earthwork red soil encasing founda- tions	890	64	-	6	-	✓	798	64
Earthwork filling in basement	120	311	-	4	-	✓	3165	64
Concrete broken stone in mortar	430	20	-	86	-	✓	442	20
Ground moulded burnt brick in mud in foundations basement	1040	372	-	386	-	✓	1078	372
mudwalling	390	212	-	11	-	✓	286	212
brick in mortar in superstructure	0.70	4511	-	32	-	✓	174	4511
cut stone work	11	18	-	18	-	✓	-	-
Rajadance wood	94	6	-	35	-	✓	80	6
junglewood wutton	252	-26	39	-	-	✓	260	-26
				617	-			

I hereby certify that, with the exceptions noted and explained above, this work has been fully executed to that, excluding deviations explained above, it corresponds in all respects with the sanctioned plan and estimate.

Station _____
Dated _____ 192

REPORT.

Name of Work

Name of Work Constructing an elementary school building
located at 1615/- at Talasepally

Amount of estimate Rs 1,615/- at Talaceppally.

Sanctioned in S.T.B. No. 25
Explanation of differences. 20.2.25

Difference. (Excesses to be shown in red ink.)						Sanctioned in S.T.B. No. 25 Explanation of differences.	
Amount.		Quantity.	Rate.	Amount.			
7		8	9	10		11	
Rs.	A.P.		Rs.	A.P.	Rs.	A.P.	
5	-	801	-	5	1	-	due to actual measurement of work done
19 1/2	-	88 6	-	15 1/2	26	-	The eleven works were found necessary during execution and their cost may be met from the savings in the other nine heads.
400 3	-	7 1/4	-	14 3	32	-	due to actual execution.
798	-	47 8	-	18	5	-	The eleven works were found necessary during execution.
30	-	18	-	5	110	-	not executed being unnecessary.
40 10	-	5	-	110	-	-	Due to actual requirements.
67 15	-	54 5	-	-	-	-	due to actual execution of the work.

the extent of the estimate in a substantial and satisfactory manner as regards materials and workmanship, and is suitable to the purposes for which it is intended.

Accountant.

Local Fund Engineer.

COMPLETION

L.F. Form No. 77.-(Inner Sheet.)

Sub-heads of Estimate.	As estimated.			As executed.		
	Quantity.	Rate.	Amount.	Quantity.	Rate.	
1	2	3	4	5	6	
		Rs. A.P.	Rs. A.P.		Rs. A.P.	
			617 -			
Matched roofing with bamboo rafters	3560	12 13 6	457 -	3548	10 13 6	✓
Bine sheeting for valleys	-	-	-	108	- 3 -	✓
Coccurring wood pillars						
maroon battens doors	41	- 14 6	37 -	49	- 14 6	✓
with frames						
do do windows						
with frames	8	- 14 6	7 -			
levelling course of concrete	1570	7 14 -	124 -	1586	7 14 -	✓
Honey comb tile work	1370	12 4 -	168 -	744	12 4 -	✓
Plastering with lime mortar including	2160	2 14 -	63 -	1980	4 5 6	✓
whitewashing two coats	2160	- 4 6	6 -			
Plastering mud and						
covering				762	- 8 3	✓
Whitewashing two coats	390	- 4 6	1 -			
Tarring 2 coats				831	1 14 -	✓
French nails	700	- 6	22 -	700	- 6	✓
Bamboo 14' long	141	- 8 -	71 -	97	- 8 -	✓
				203	- 0 0 4 -	✓
Total			1573 -		2150	

I hereby certify that, with the exceptions noted and explained above, this work has been fully executed to that, excluding deviations explained above, it corresponds in all respects with the sanctioned plan and estimate.

Station _____
Dated _____ 192 .

REPORT.

Name of Work _____

Amount.	Difference. (Excesses to be shown in red ink.)			Explanation of differences.
	Quantity.	Rate.	Amount.	
7	8	9	10	11
		Rs. A.P.	Rs. A.P.	
			6715 -	✓
			5745 -	
			384 12 -	
			204 -	
			446 -	✓
			124 14 -	✓
			872 -	✓
			86 -	✓
			315 -	✓
			159 -	✓
			21 14 -	✓
			488 -	✓
			50 12 -	✓
			155910 -	✓
			136 -	

the extent of the estimate in a substantial and satisfactory manner as regards materials and workmanship, and and is suitable to the purposes for which it is intended.

Accountant.

Local Fund Engineer

COMPLETION

Sub-heads of Estimate.	As estimated.						As executed.	
	Quantity.	Rate.	Amount.		Quantity.	Rate.		
	1	2	3	4	5	6		
		Rs.	A. P.	Rs.	A. P.	Rs.	A. P.	
				1573	✓			
Cables such as - wiring wires etc.	}							
Artage for cables etc.		9-		17	✓	11	16	
						10	8	
						9-		
Qty Supervision		9-		25	✓			

I hereby certify that, with the exceptions noted and explained above, this work has been fully executed to that, excluding deviations explained above, it corresponds in all respects with the sanctioned plan and estimate.

Station _____

Dated _____ 192

REPORT.

Name of Work Constructing an
elementary school building
at Glampaley

		Difference. (Excesses to be shown in red ink)				Explanation of differences.
Amount.		Quantity.	Rate.	Amount.		
7		8	9	10		
Rs.	A. P.			Rs.	A. P.	
1559 10 -	✓			136 -		
15 2 -				15 2 -		due to actual expenses
28 4 -				8 4 -		in cartages incurred.
15 -						
2 -						
- - -				25 -		not charged

the extent of the estimate in a substantial and satisfactory manner as regards materials and workmanship, and and is suitable to the purposes for which it is intended.

Accountant

Local Fund Engineer.

OFFICE OF THE PRESIDENTIAL JURY BOARD
7-JUN 1926
S. A. L. E. M.

Local Fund Engineer.

(6)

Date. *ebf* Initials *ebf*

10
3.9

Law (25.9) DEPARTMENT.

Subsidiary

Constructing new? School buildings
Bd., Salem - ~~new~~ district new
ue?

” ” ” ” ” 192

C. No. 21257 From the _____, No. _____, dated _____ 192

” ” ” ” ” ” 192

” ” ” ” ” ” 192

ORDER.

Wm.

No. 1518, dated 3-9- 1925

The G.O. no. 2014 L.E. of 27.12.24
the Govt. promised a grant not exceeding
Rs 2000 towards the cost of construction
of a building for the School at Elam-
pillai. The P.T.B. Salem, reports
that the building has been completed
at a cost of Rs 1592/- A sum of
Rs 355/- has already been disbursed
under G.O. no. 352 L.E. of 13.3.25. The
Govt. sanction the payment of the
balance of Rs 1,237/- to the taluk
board in the current year.

2. The Acct.-Genl is requested to place the amount of Rs 1,237/- at the disposal of the Taluk Board as an

an early date. The P.T.B.; Salem,
is requested to place the present the
necessary bill at the Treasury for
obtaining payment or adjustment of
the account

3. The expenditure will be met
from the provision of Rs 43,200 in the
current year's budget estimate under

"31-C.C. education - Primary - Grants
to local bodies for primary education
- Grants in aid - Voted - Non-recurring -
Buildings".

AD
19/8/25
81x
22.8.25
Note

May be sent a/c. to Finance
for acceptance

AD
19/8/25
81x
22.8.25

Finance (Exp)

The draft order may be accepted

AD
28.8.25
29.8.25

Issue.
V.T.K.
1.9


7/25

P.2137 C.P.E

DESPATCHED

to 3 SEP 1925
The P.T.B. Salem (with ref
to his letter no 841 of 20.7.25)
.. P.D.B. Salem
.. P.D.E. do.
.. D.B.
.. Ex. of L.F.A.
.. Acct sent thro Finance
.. L.B.
.. Finance

100 (100), no 2175 A-2
26.8.25

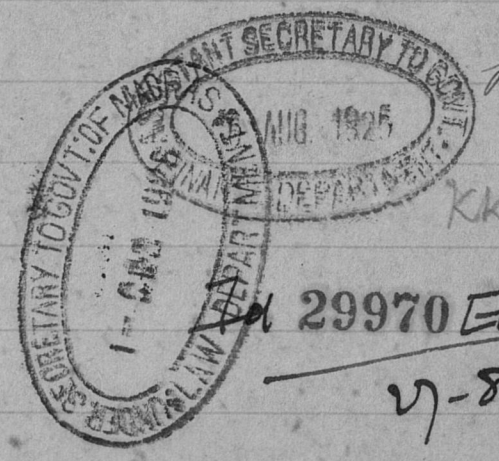

Ex G 29970 Exp. 1
1.9.25

When given for copying
When copied
When examined
When signed

192

READ AGAIN G.O. No. 192 DATED

CURRENT No.

ENCLOSURES TO G. No.

ORDER OF GOVERNMENT

LETTER OF GOVERNMENT

STATEMENT WITH DITTO

PAPERS NOT FILED OF, BEING MEANT FOR DESPATCH
IN ORIGINAL.

N.B.—
A = Copy in full.
B = Not to be copied.
P = Copy abstract only.
Q = Copy heading only.

A A A A A A A
