

(1) Number of pages _____

(2) Date of repair _____

(3) Initials of the Referencer _____

MADRAS RECORD OFFICE

Government of Madras

Public Works DEPARTMENT

G.O. No.	2256	Press
B.P. No.		Mis.
Dated	28-8-1956	18/6

Not to be folded or roughly handled

*Proceedings of the Madras Government, Public Works Department,
25th August 1876. No. 2,256.*

No. 586. Read the following endorsement of the Chief Engineer for Irrigation, dated Ootacamund, 18th August 1876, No. 152-W :—

From J. H. LATHAM, Esq., Chief Engineer and Manager, Madras Irrigation and Canal Company, to Lieutenant-Colonel J. MULLINS, R.E., Chief Engineer for Irrigation, dated Dhoor, 5th August 1876, No. 75.

June Reports.

I HAVE the honor to forward per Book Post the copies of the Upper and Lower Divisional Engineers' Reports together with my own for the month of June 1876.

MADRAS IRRIGATION AND CANAL COMPANY.

UPPER DIVISION.

Monthly Report for June 1876.

1. Until the 10th of the month, water did not rise up to the sill of the head sluices, but at 5 A.M. on that date it began to rise, and reached 11·2 above the canal sluice sill on the 11th. As the water was very muddy it was not let in until the evening of the 16th.

From the 16th to 28th water gradually fell again in the river and consequently in the canal, so that it only reached Ulloor aqueduct at 36½ miles; but on the 28th a new fresh came down, and on the 30th it reached 42½ miles.

At present it is near Jupaud.

Owing to the new work at Calinguliah No. 1, which is protected by a dam 6 feet high, it was not thought advisable to let in more than 4·8 at the head sluices.

I have no doubt that by the 8th water will reach Lockinsula.

2. The weather has been unusually free from rain. The following is the rainfall at Kurnool during the month :—

3rd June	...	...	...	...	0·50
6th "	...	...	...	...	0·27
7th "	...	...	...	...	0·03
10th "	...	...	...	...	1·36
12th "	...	...	...	...	0·74
19th "	...	...	...	...	0·12
20th "	...	...	...	...	0·41
Total in June					3·43

At Soonkesala the total was...	...	2·10
" Jupaud	...	3·50
" Velapanoor	...	6·50
" Ayaloor	...	3·62

or on the average scarcely 4 inches.

				<i>Kurnool.</i>
Rainfall during May and June 1871	...	...	...	2·53
" " " 1872	...	...	...	5·56
" " " 1873	...	...	...	6·36
" " " 1874	...	...	...	10·06
" " " 1875	...	...	...	4·64
" " " 1876	...	...	...	3·43

There are great complaints of want of rain. Many ryots are waiting in expectation of the rain long due, before they sow their dry crops. As it is their practice to sow dry crops first and after wards commence the irrigated crops, many will be delayed; but fields are being prepared for paddy and other wet crops near Kurnool.

*Proceedings of the Madras Government, Public Works Department,
25th August 1876. No. 2,256.*

3. *Repairs to the Canal on Capital Account.—Nidjood Bridge.*—The lower approach has been carried on rapidly.

Bandies can now pass over the bridge.

Dollararam Bridge.—The masonry retaining wall at foot of the upper approach is completed the parapets have been removed, and masonry rebuilt at an incline of 1 in 16 to suit a second-class crossing. The coping stones required in order to fix the teak railings and cross beams are not yet completed. The necessary revetments on both sides are finished, and the earthwork near the bridge nearly completed.

Moochomurry Bridge.—The masonry is completed. The roadway is being filled in. The upper approach is completed, except side walls and metalling. The lower approach has been taken in hand by a new contractor and will soon be finished. Foot passengers cross over the bridge as the water is now running.

Singarim Bridge.—One 15-foot arch and 1-30 and 1-32-foot arch were turned before the 30th, but, owing to the depth and velocity of water (more than 4½ feet), considerable difficulty arose in putting up the last 30-foot centring.

It is however finished, and probably all arches will be turned by the 7th July.

Repairs charged to Revenue.

4. The repairs to the head and under-sluice shutters were completed. Two new shutters for head sluices have been made in the workshop and the screws are expected from Madras soon.

The puddle which was laid on the bank for 10 chains in the Yeddaroer tank (6th mile) has been completed.

The masonry in the two new sluices at Calingulah No. 1 has been brought up to a level of 5 feet above bed or 10 feet above the sill level. The bank in front is strong and effective.

The shutters are in place; the raising gear has been commenced, and as soon as the two screws arrive from Madras they will be fitted up ready for building into the masonry.

The Sluice No. 83 at Nagatoor has been completely rebuilt according to the new muster.

Terrigopully leak has been repaired, and various minor repairs and necessary works have been completed.

5. The water-rate settlement was finished on the evening of the 13th. It was held at Kurnool, Velapanoor and Ayaloer, and occupied fifteen days, of which ten days were taken up by the actual work and five days in travelling and preparations. The abstracting and final comparison of the accounts is naturally delayed until references made to the Collector and Chief Engineer have been settled, when the final closing of the accounts will be made.

6. *Irrigation.*—No definite information as to the coming season has been obtained, but it is hoped that the present scarcity of rain may turn the minds of the ryots to the advantages held out by the using of canal water. The channels in use are all being cleared out and improved so as to supply water as may be required. The arrangements of the staff have been revised, and especially as to the bankers, who have been distributed in the manner which seems most to further the proper control of the water, as experience points out.

7. The health of the staff has been good, no serious cases of illness have occurred.

8. The staff were paid from 9th to 22nd June 1876. The delay was occasioned by the settlement work which takes up much of the time of my office staff.

(Signed)

C. H. WILKS,

Conservancy Engineer.

LOWER DIVISION.

Monthly Report for June 1876.

1. The weather has been exceptionally dry, as the enclosed table of rainfall during this month, for this and the five preceding years shows.

This was exceedingly fortunate, as a heavy shower of rain would have considerably retarded the unusually heavy silt operations.

*Proceedings of the Madras Government, Public Works Department,
25th August 1876. No. 2,256.*

2. In the 9th Section, the canal from the Rajoly head sluices (mile 145, chains 60) to Canagoodoor (mile 155, chains 29) has been thoroughly bottomed out to bed level so that so soon as the water reaches the head sluices it can be admitted into the canal.

The bottoming of the 10th Section from the head sluices at Adamapully (mile 180, chains 56) to the Punkala Vunka aqueduct (mile 183, chains 49) was completed on or about the 25th June: the remainder will be finished shortly; I hope to open these sluices on the 10th.

3. Nearly all the other earthworks are finished, and as I believe no weak banks have been neglected, and all earth above bed has been removed. The canal will be in a very efficient state so far as the earthwork is concerned.

4. This year I have been fortunate in securing earthwork labor at a far cheaper rate than previously; where 7 cubic yards per Rupee were formerly worked, 10 cubic yards were offered, and where 12 cubic yards per Rupee were worked, 16 cubic yards were offered.

5. The masonry works are in an advanced state, and will be completed before the water reaches the Lower Division. The twenty-six locks, some of which have been supplied with new cills, have been thoroughly over-hauled, and will be as thoroughly fit for navigable purposes as they were last season. Every piece of woodwork which is now composed entirely of teak is as sound as when first put together.

6. The channel works and extensions as much as needed will be completed in time for the water. The Maideoor channel cannot be so efficiently restored as I intended, as owing to the prevalence of cholera in the surrounding villages, labor cannot be procured at any price.

7. It is to be hoped that the valuable Gurrampad aqueduct will be used during the coming season. It was constructed at a great cost solely on the suggestions and petitions of the ryots of Gurrampad.

Last season when I opened it, there was not a single application for water made. The ryots gave as their reason that the land, commanded by the new works, was not made over to them. This I was informed by the Revenue authorities was not correct. If this be the case there can be no possible reason for allowing 200 acres (or more) of the most suitable soil for the growth of wet crops to lie waste this season, as it has been many years back.

8. *Irrigation.*—The final returns for the Cuddapah District demand for 1875-76 have been sent in. I enclose a condensed abstract of it. I have just received a letter from the Collector, Mr. Gribble, in which he concurs entirely with my views regarding the only claim which was disputed by the Deputy Collector at Settlement.

The early settlement and speedy closing of the accounts have given great satisfaction to the ryots. The collections, I hear, already are being made and readily paid. The postponement and deferring the collection of the water-rate is very objectionable to the ryot who has always protested against being called upon to settle his account some time after he has disposed of his crops and money, or at times when he is laying out his money in preparing his fields for the ensuing season.

9. The returns for the Kurnool District are still incomplete, owing to the numerous references which it was thought advisable to make to the Chief Engineer and Collector on many points which the Deputy Collector and myself were unable to agree upon with the existing rules.

10. The revised framed rules and placards have been posted in the villages, and wherever else required. It is to be hoped that the village authorities will apply for them, if not yet supplied, or if extra ones be required.

11. Health of staff is generally good. Dhooor still continues unhealthy, and those of my staff who live there are frequently laid up with fever. Cholera is very prevalent in some villages near the canal in the Cuddapah District.

(Signed) J. O. DUNPHY,

Acting Conservancy Engineer.

Ootacamund,
7th July 1876.

Proceedings of the Madras Government, Public Works Department,
25th August 1876. No. 2,256.

MADRAS IRRIGATION AND CANAL COMPANY.

LOWER DIVISION.

Table of Rainfall Readings in previous years at Dhoor.

Total Rainfall in June 1869.	Total Rainfall in June 1870.	Total Rainfall in June 1871.	Total Rainfall in June 1872.	Total Rainfall in June 1873.	Total Rainfall in June 1874.	Total Rainfall in June 1875.	Total Rainfall in June 1876.
4.30	3.80	1.01	4.00	3.33	8.33	2.43	0.27

Dhoor,
30th June 1876.

(Signed) J. O. DUNPHY,
Acting Conservancy Engineer.

MADRAS IRRIGATION AND CANAL COMPANY.

LOWER DIVISION.

Table of Rai fall Readings during the Month of June 1876.

Month and Date.	Yalloor.	Chinta canta.	Rajoly.	Dhoor.	Adima- puly.
2nd June 1876	0.75	...	...	0.10	...
3rd "	...	...	1.10	...	...
6th "	...	...	1.10	...	...
7th "	...	...	...	...	...
11th "	0.40	...	...	0.07	...
12th "	...	...	...	...	...
13th "	...	...	...	0.06	...
14th "	...	...	...	...	0.40
17th "	...	0.08	...	0.02	...
24th "	...	1.16	...	...	...
25th "	...	...	...	...	0.03
28th "	...	...	...	0.02	...
Total	1.15	1.22	2.20	0.27	0.43

Dhoor,
30th June 1876.

(Signed) J. O. DUNPHY,
Acting Conservancy Engineer.

MADRAS IRRIGATION AND CANAL COMPANY.

Chief Engineer's Report to accompany the Monthly Divisional Reports for June 1876.

The only matters of interest this month were the progress of repairs and the rainfall.
2. The repairs of the main canal have been fairly executed, notwithstanding that the absence of both Engineers on privilege leave and the unusually tedious settlement occurred during the short season available for repairs. In the Lower Division the masonry works required on channels have had to be postponed, and the lock repairs (masonry) have been inefficiently done by the Overseers.

3. This has been very much due to the uncertainty of the finances, which prevented the proceeding of stone and carting it to the sites in time to get the building done before probable rain.

4. The rainfall has been very light, and up to this date (2nd) no crops are sown here, and not half the ground ploughed yet.

Proceedings of the Madras Government, Public Works Department,
25th August 1876. No. 2,256.

5. The water has now (22nd) reached all the irrigating sluices, unless it be a sluice near the Pennar (north side) about which I have not heard.

6. I enclose a table showing the extent of various crops cultivated under the canal, 1875-76.
(Signed) J. H. LATHAM,
Dhoor,
24th July 1876.
Chief Engineer and Manager.

MADRAS IRRIGATION AND CANAL COMPANY.

Table showing the Extent of various Crops cultivated under the Canal, 1875-76.

Class.	Crop.	ACRES UNDER CANAL IRRIGATION, 1875-76.					
		Upper Division.		Lower Division.		Total.	
		Acres.	Per cent.	Acres.	Per cent.	Acres.	Per cent.
1st Class	Sugar	7.89	0.15	...	...	7.89	0.06
	Betel	20.12	0.37	61.76	0.79	81.88	0.63
	Fruit trees	54.21	1.01	19.75	0.25	73.96	0.56
	Rice	4,229.94	78.52	8,783.29	43.21	8,913.23	60.63
	Turmeric or Saffron	15.15	0.28	2.49	0.03	17.64	0.13
	Chilly	446.68	8.29	227.29	2.90	673.97	5.09
	Indigo	128.18	2.38	1,789.71	22.81	1,917.89	13.49
2nd Class	Korra	2.06	0.04	384.86	4.90	386.92	2.30
	Cumin	18.81	0.35	320.14	4.08	338.95	2.56
	Raggoe	56.75	1.05	943.79	12.02	1,000.54	7.60
	Vegetable	86.64	1.61	78.62	1.00	165.26	1.25
	Miscellaneous	254.67	4.73	128.16	1.63	382.83	2.39
	Cholum	26.58	0.49	68.19	0.87	94.77	0.73
	Oil	...	...	3.70	0.05	3.70	0.03
3rd Class	Miscellaneous	39.31	0.73	86.11	0.46	125.42	0.97
	Under Tanks Supply	5,386.99	100.00	7,347.76	100.00	13,234.75	100.00
	Grand Total	834.26	...	409.59	...	1,337.14	...
		91.29	...	...	...	...	...
		6,312.54	...	8,257.35	...	14,571.89	...

(Signed) J. H. LATHAM,
Chief Engineer and Manager.

SUBMITTED for the information of Government.

(Signed) J. MULLINS, Lt.-Col., R.E.,
Chief Engineer for Irrigation.

No. 587.

ORDER THEREON, 25th August 1876, No. 2,256.

IRRIGATION, No. 61.

ORDERED to be recorded.

(True Extract.)

(Signed) G. W. WALKER, Major-General, R.E.,
Secretary to Government.

To the Chief Engineer for Irrigation.
" Chief Engineer and Manager, Irrigation and Canal Company.
" Revenue Department.

Exd. W. H. French.
Spare Copies

N 7

*M. J. & Co.
Lower Division
Table of Rainfall readings in previous years at Dhoor*

<i>Total rain fall in June 1869.</i>	<i>Total rain fall in June 1870.</i>	<i>Total rain fall in June 1871.</i>	<i>Total rain fall in June 1872.</i>	<i>Total rain fall in June 1873.</i>	<i>Total rain fall in June 1874.</i>	<i>Total rain fall in June 1875.</i>	<i>Total rain fall in June 1876.</i>
4.30	3.80	1.91	4.00	3.53	8.38	2.48	0.27

/Signed/ J. O. Dunphy
Acty. Conservancy Engineer

Dhoor
30th June 1876.

/True Copy/
Bogavamood
Clerk.

Madras Irrigation & Canal Co.
Chief Engineer's Report to accompany
the Monthly Divisional Reports
for June 1876.

The only matters of interest this month were the progress of repairs, and the rain-fall.

2. The repairs of the main Canal have been fairly executed notwithstanding that the absence of both Engineers on privilege leave, and the unusually tedious settlement occurred during the short season available for repairs. In the Lower Division the masonry works required on channels have had to be postponed and the lock repairs (masonry) have been inefficiently done by the Overseers.

3. This has been very much due to the uncertainty of the finances, which prevented the proceeding of stone and carting it to the sites in time to get the building done before probable rain.

4. The Rainfall has been very light, and up to this date (22nd) no crops are sown here, and not half the ground ploughed yet.

5. The water has now (22nd) reached all the irrigating sluices, unless it be a sluice near the Pennar (N. side) about which I have not heard.

6. I enclose a table shewing the extent of various crops cultivated under the Canal 1875/76.

Chief Engineer Manager
/ Signed John H. Latham
Chief Engineer & Manager

17/8

M. J. and L. C. Jr.
 Lower Division
 Table of Rain fall reading during the
 month of June 1876.

Month & Date	Gallon	Chiuta Cunta	Rajoly	Shoor	Adima pully	Remarks
June 1876.	2 nd	0 75	Nil	0 10	Nil	
	3 rd	Nil	1 10	Nil	Nil	
	6 th	Nil	1 11	0 07	Nil	
	7 th	Nil	Nil	Nil	Nil	
	11 th	0 40	Nil	0 06	Nil	
	12 th	Nil	Nil	Nil	0 40	
	13 th	Nil	Nil	0 02	Nil	
	14 th	Nil	Nil	Nil	Nil	
	17 th	0 06	Nil	Nil	Nil	
	24 th	1 10	Nil	Nil	0 05	
	25 th	Nil	Nil	0 02	Nil	
	28 th	Nil	Nil	Nil	Nil	
	Total	1 15	1 22	2 20	27	45

Shoor.
30th June 1876

(Signed) *J. O. Murphy*
By Joney Engineer

True Copy!
C. Bagawa Mood
 Clerk

Clerk



B.W.D.

1875-76

1/11


Madras Irrigation & Canal Co. Ltd.

Table Shewing the extent of various crops Cultivated under the Canal 1875-76.


Class.	Crop.	Acres under Canal Irrigation 1875-76.					
		Upper Division		Lower Division		Total	
		Acres	Per Cent	Acres	Per Cent	Acres	Per Cent
1 st Class.	Sugar	7.89	0.15			7.89	0.06
	Betel	20.12	0.37	61.76	0.79	81.88	0.62
	Fruit trees	54.21	1.01	19.75	0.25	73.96	0.56
	Rice	4229.94	78.52	3783.29	48.21	8013.23	60.63
2 nd Class.	Turmeric or Saffron	15.15	0.28	2.49	0.03	17.64	0.13
	Chilley	446.68	8.29	227.29	2.90	673.97	5.09
	Indigo	128.18	2.38	1789.71	22.81	1917.89	14.49
	Cumin	2.06	0.04	384.86	4.90	386.92	2.80
	Korra	18.81	0.35	320.14	4.08	338.95	2.56
	Ragga	56.75	1.05	943.79	12.02	1000.54	7.60
	Vegetable	86.64	1.61	78.52	1.00	165.16	1.25
	Miscellaneous	254.67	4.73	128.16	1.63	382.83	2.89
3 rd Class.	Cholum	26.58	0.49	68.19	0.87	94.77	0.72
	Oil			3.70	0.05	3.70	0.03
	Miscellaneous	39.31	0.73	36.11	0.46	75.42	0.57
		5386.99	100.00	7847.76	100.00	13234.75	100.00
Under Tanks Supply		834.26		409.59		1243.85	
Grand Total		6321.25		8257.35		14578.60	

/ Signed / John H. Latham
Chief Engineer & Manager

/ True Copy /
Ragava Moode
Clerk

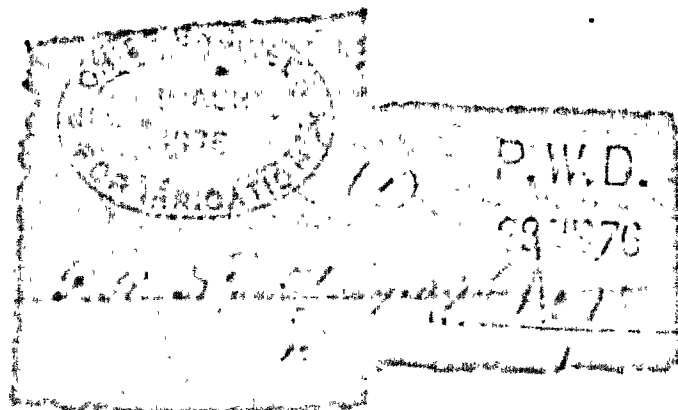

fo. 22 74/76-479.
20 June - 1885 -



P.W.D.
28 AUG 76

Sub. 5129-876.
to be kept for inspection
by 152-11
Submitted with information
of Government

Obtained from the
Bangor 876 Chief of
No. 2256/25 Aug 76
Record

44-178

586/87

Aug 24 876
a.h. shut 24 Aug.

Aug 25 876
Rev Sept 23/9/76

6210 (H)

Gobt. of 1876 Madras.

PUBLIC WORKS.

To

The Chief Eng^r for Eng^s.

Dated

Issued

Recd.

Filed.

G. O. 25th Sept 1876, No. 2256

Nos. 5

*For the
25-9-76*

Madras Irrigation &
Canal Company

The report of the Chief
Engineer and Manager
on the Upper and Lower
Divisions of the ———
for the month of
June 1876, received
