

Public Works (1899) Department

✓ G.O., No. 2788 W

DATED 13th Oct 1899.

[Despatch Abstract.]

Stationary Sub-Magistrate's Office at Perambalur
Trichinopoly Dt.

Authorizing the Exr, P. W. Accts, to admit
the outlay of Rs 577 incurred in excess of the
estimate of Rs 7,600 for constg a —

BACK PAPERS.

G.O.	No.	Department.	Date.	G.O.	No.	Department.	Date.

FURTHER PAPERS.

G.O.	No.	Department.	Date.	G.O.	No.	Department.	Date.

Public Works Department

Public Works (1899) Department

CURRENT No.

7869

No: 2798 W & 23-10-99 From

Order

11.10.99

The Superintending Engineer

No. 1641 TC.

The Examiner of P.W. Accounts is authorized to admit the outlay of Rs 577 incurred in excess of the estimate sanctioned in G.O. No 1997 W dated 6th July 1896 for constructing a Stationary Sub-Magistrate's Office at Perambalur, Trichinopoly District.

Dated 19 September 1899.

Received

Registered

Enclosures

Spare copies.

23-9-99
Plans with 22 tabs
Others - 3 3 3

11/10/99

P.K.S.

To

The S.E. VI circle with completion report of 2 roads examined P.W.A.

SUBJECT.

Note. The chief causes of excess are the following.

(1) As the soil on excavation was found unsuitable for building purposes, it was necessary to lay deeper foundations in concrete than was estimated for.

(2) There was also an excess on the item "Supervision" as a competent mastery on Rs 25 per mensem.

Stationary Sub-Magistrate's Office at Perambalur - Requesting sanction of Govt. to the excess outlay on the work of

11.10.99

11.10.99

The Examiner

G.O. No. Depart PERS.

FURTHER PAPERS.

Date.

No.

Date.

5707C 1-7-97
 347C 20-1-97
 4326C 21-11-96
 2369W 19-8-96
 1991W 6-7-96

had to be employed, no suitable
 men being available in the locality.

W. H. H. 10.10.99

W. H. H.
 P. K. S.

11.10.99

Current No. 7869
 Letter No. 1641 T.C.
 Dated 19 Sep 1899
 From the S.E. VI Circle

NOTE BY TECHNICAL SECTION.

Name of work Requesting Sanction
 of work. W. H. H. on the
 on the Stationary Submarine
 - under office at Perambalur

Original Estimate 7600
 Deviation Statement to
 1332 T.C. 9-15-8-97 329
 Final Estimate as
 & Completion Report 248
 Excess. Rs. 577

Total expenditure Rs. 8177

1. The S.E. in the above
 quoted number forwarded
 through the Examiner P.W.D.
 requests Sanction for excess
 expenditure of Rs. 577 over the
 sanctioned Estimate for this
 building - the excess being
 above spent. The completion
 report attached has been
 verified by the Examiner
 and explanation of the
 difference is given in the
 slip attached to the report.

2. The Chief Engineer is in the
 item. Considered in foundation
 It was found necessary to
 deepen the foundation as the
 soil on excavation was
 found

much the inevitable for building purposes.

There was also a large excess on the item Taxes - vision - as a constant necessity on the 25th March at least the employees, no suitable building could be got in the locality -


Under the right amount of the excess might be sanctioned.

Am. Pr.
3.10.99

W. The excess over the sanctioned estimate may be sanctioned.

Will
5/10/99

Yes
L. H. C.
6.10.99

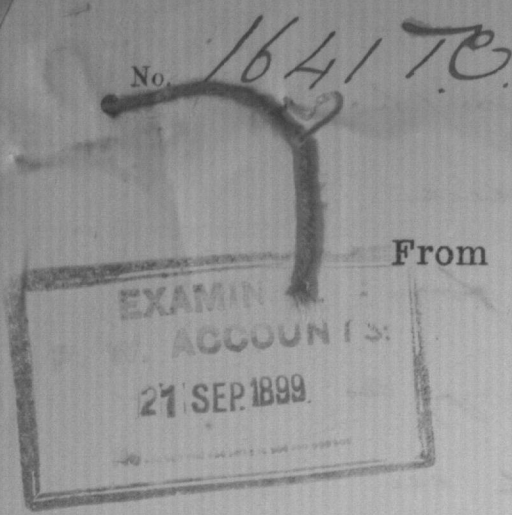

OFFICE OF THE SUPERINTENDING ENGINEER,
6TH CIRCLE,
Trichinopoly, 19 September 1899.
9/20.

From

Robert O. T. Maddy Esq.
Superintending Engineer,
6th Circle.

To

The Chief Engineer,

P. W. D.

3 ENCLOSURES.

1. Completion Report.
2. ^{with} L. H. C. return.

Thro'

The Examiner of
Public Works Accounts
Madras.

Sir,

I have the honor to forward for your information and return the enclosed Completion Report for Constructing Stationary Sub Magistrate's office at Perambalur, Estimate Rs 7600, sanctioned in G.O. No: 1991 W dated 6 July 1896 and to request that sanction may be obtained for the excess outlay of Rs 577 over the sanctioned estimate which is above 5%.

2. The Completion Report has been duly verified by the Examiner of P. W. Accounts, Madras.

Vol 100

3. It will be seen from the Comptroller's Report that the excess is due chiefly to the item "Concrete in foundation". This was found necessary, as deeper foundation had to be laid in concrete as the soil on excavation was found to be unsuitable for building on. It looked extremely hard, but a little water reduced it to paste.
4. There has been an excess outlay also on item "Petty Supervision". This is due to the employment of a competent British-layer masonry on Rs 25 per mensem in a place where one cannot be obtained locally.

I have the honor to be
Sir,

Yours obedient servant.

J. V. Boddy Esq. R.E.
Superintending Engineer

N. 3141 P/A, dated 22-9-99 W. C. C.
Forwarded.

19/9/99

H. Raimier
Off. Examiner, P. W. Accounts
Madras.
22/9/99
