

- (1) பக்கங்களின் எண்ணிக்கை 32
(2) புதுக்கித் திருப்பிய நாள் Feb. 88
(3) ஆதாரங்குறிப்பவர் சுருக்கொப்பம் 10/3

தமிழ்நாடு ஆவணக் காப்பகம்.

தமிழ்நாடு அரசு

Revised துறை

அரசாணை எண். மு. கோப்புத் தாள் எண்.	<u>55</u>	அச்சகம் பலவகை
நாள் :	<u>11.1.1879</u>	<u>178</u>

மடிக்கவோ கண்டபடி கையாளவோ கூடாது

No. 152. Endorsement of the Deputy Chief Engineer, Public Works Department, dated 6th January 1879, No. 30.
 Famine Relief.
 Read the following paper:—
 FORM No. I.
 For all Works (except Miscellaneous Minor Works).

General Number of Work	Name of Work and Takut in which situated.	EXPENDITURE.										CLOSING.	
		Amount of Estimate.	Cost of Materials.	Wages.			Supervision.	Contingencies.	Total.	Date of Sanction.	Date of Opening.	Date.	Cause.
				Grain.	Value.	Money.							
1	2	3	4	5	6	7	8	9	10	11	12	13	14
	Road Works.	RS.	RS. A. P.		RS.	RS. A. P.	RS. A. P.	RS. A. P.	RS. A. P.				
60	Repairing the road from Coimbatore to Metapallem.	4,579	112 15 6	..	..	4,288 15 8	176 13 1	..	4,578 12 3 11th Nov. 1878.	16th Sep. 1877.	6th Dec. 1877.	6th Dec. 1877.	Closed.
61	Resetting revetments of the County Tank.	2,040	116 9 6	..	..	1,858 6 0	65 0 0	..	2,039 14 6 14th May 1878.	1st May 1878.	31st Aug. 1878.	31st Aug. 1878.	Completed.
62	Closing breaches and strengthening the bund of Calingarozen Channel.	6,135	643 1 4	..	..	7,065 1 9	63 6 4	..	7,771 8 5 6th & 26th June & 11th July 1877.	20th Oct. 1877.	31st Dec. 1877.	31st Dec. 1877.	Completed.
63	ROAD—MINOR WORKS.												
	New Works	33,786	65 7 0	..	..	2,371 14 11	NIL. 25 9 0	..	2,463 14 11	..	..	..	..
	Repairs			..	..								
64	IRRIGATION—MINOR WORKS.												
	New Works	4,858	377 2 0	..	..	3,199 13 8	NIL. 69 2 1	9 13 0	3,645 13 9	..	..	..	..
	Repairs			..	..								

COIMBATORE.
 20th December 1878.

(Signed) H. R. MEAD, Major, R.E.,
 Superintending Engineer, Fourth Circle.

55

FORM No. 2.

Roads—New Works and Repairs.

General Number of Works.	Name of Work and Taluk in which situated.	Total of the Numbers employed daily during the entire progress of the Work.						WORK DONE.											
		Men.		Women.		Children.		Total.		Length in Miles.		Earthwork.		Collection of Material.					
		3	4	5	6	7	8	9	10	11	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	Value.	Metal.		Gravel.	
																At Normal Rates.	At Estimate Rates.	At Normal Rates.	At Estimate Rates.
1	2																		
	ROAD WORKS.	NO.	NO.	NO.	NO.			C. YDS.	RS.	A. P.	RS.	A. P.	C. YDS.	RS.	A. P.	RS.	A. P.	RS.	A. P.
60	Repairing the road from Coimbatore to Mettupolhem.	7,863	16,467	2,718	27,018	..	..	17,772	367	9	4	..	232	462	0	1	..	519	64
63	ROAD—MINOR WORKS.																		
	New Works..																		
	Repairs..																		
		8,979	16,182	6,818	31,979	..	..	2,056	295	5	2	..	2,747	1,040	8	1	..	210	52

* Number of oodles could not be given for one of the works, the nominal value whereof is Rupees 218-2-6 as the payment was made on contractors' bills, the work being masonry.

Roads—New Works and Repairs—continued.

General Number of Works.	Name of Work and Taluk in which situated.	WORK DONE—continued.										Total Value.			
		Spreading.		Tamping.		Building.		Miscellaneous.		—		Value.		At Normal Rates.	
		Value.		Value.		Value.		Value.		Quantity.		At Normal Rates.		At Estimate Rates.	
		Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.

COIMBATORE,
14th December 1878.

(Signed) H. R. MEAD, Major, R.E.,
Superintending Engineer, Fourth Circle.

FORM No. 3.

Irrigation—New Works and Repairs.

REVENUE DEPARTMENT, 11TH JANUARY 1879, No. 55.

WORK DONE.																	
Name of Work and Taluk in which situated.	Total of the Numbers employed daily during the entire progress of the Work.						Earthwork.			Masonry.			Revetting.			Laying stone collected.	
	Men.	Women.	Children.	Total.	Quantity.	At Normal Rates.	Value.		Quantity.	At Normal Rates.	At Estimate Rates.	Value.		Quantity.	At Normal Rates.		At Estimate Rates.
							At Normal Rates.	At Estimate Rates.				At Normal Rates.	At Estimate Rates.				
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18
IRRIGATION WORKS.																	
61.	Revetting revetments of the Coorby Tank.	1,189	1,050	115	2,354	1,025	115	10 0	3,302	1,658	4 0	..	..	..	..	..	..
62	Closing breaches and strengthening the bank of Calingaryen Channel.	17,392	28,780	5,559	61,712	59,447	5,713	13 0	..	..	..	..	503	8 0	..	468	292
63	IRRIGATION—MINOR WORKS.																
	New Works	6,047	11,599	2,649	20,495	5,333	1,163	9 4	..	..	..	82	135	0 0	..	192	216
	Repairs	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..

• Number of coolies could not be given for four of the works, the nominal value whereof is Rupees 834.15-10, as the payment was made on contractors' bills, the works being masonry.

REVENUE DEPARTMENT, 11TH JANUARY 1879, No. 55.

5

Irrigation—New Works and Repairs—continued.

WORK DONE—(Continued).																						
General Number of Works.	Name of Work and Taluk in which situated.	Clearance of Prickly-pears.						—				MISCELLANEOUS.				Total.						
		Value.			Quantity.	Value.			Quantity.	Value.			Quantity.	Value.		Quantity.	At Normal Rates.	At Estimate Rates.	At Normal Rates.	At Estimate Rates.		
		At Normal Rates.	At Estimate Rates.	Quantity.		At Normal Rates.	At Estimate Rates.	Quantity.		At Normal Rates.	At Estimate Rates.	Quantity.		At Normal Rates.	At Estimate Rates.							
		Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.	Quantity.	At Normal Rates.	At Estimate Rates.
		19	20	21	22	23	24	25	26	27	28	29	30	31	32							
IRRIGATION WORKS.																						
61	Revetting revetments of the Coorby Tank.	..	..	..	..	..	..	..	..	..	1,123	140 6 0	..	..	4 4 0	..	..	..	..	..	..	..
62	Closing breaches and strengthening the bank of Calingaryen Channel.	292	54 12 0	..	..	..	..	..	..	..	580	145 0 0	..	..	6,711 9 0	..	..	..	..	..	..	..
IRRIGATION—MINOR WORKS.																						
	New Works	4,178	217 15 0	..	..	..	..	..	..	..	61	607 14 4	..	..	2,919 14 8	..	..	..	..	..	..	..
	Repairs	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..	..

COMPTROLLER,
20th December 1878.(Signed) H. R. MEAD, Major, R.E.,
Superintending Engineer, Fourth Circle.

* Miscellaneous No. 4,222 of 30th December 1878.

TRANSFERRED to the Revenue Department in continuation of endorsement. No. 5,693,* dated 18th December 1878,

(Signed) W. FAREWELL, Colonel,
Dy. Chief Engineer, P.W.D.

No. 133.

ORDER THREE

11th January 1879, No. 55.

Miscellaneous.

COMMUNICATED to the Examiner of
Public Works Accounts.

(True Extract.)

(Signed) G. STOKES,
Addl. Under Secy. to Govt.

To the Public Works Department.
„ the Financial Department.
„ the Board of Revenue.
„ the Collector of Coimbatore.
„ the Chief Engineer for Irrigation.
„ the Examiner of Public Works Accounts.

55
4

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII


RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

RECEIVED
JAN 10 1964
U.S. AIR FORCE
HONOLULU, HAWAII

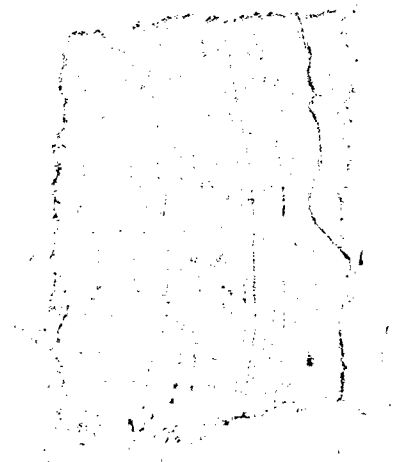

~~5~~

55
8

Wm. M. — Major R.E.
Superintending Engineer S. Circle.

Superintending Engineer's Office, Portland
Maine Dec 20 December 1878.

M. Ward
Major R.E.
Superintendent Engineer 4th Circle

FORM No. 3.
Irrigation, new-works, and Repair.

General Number of works.	Name of work and Taluq in which situated.	Total of the numbers employed daily during the entire progress of the work.				WORK DONE.																				Total.						
		Men.	Women.	Children.	Total.	Earth work.			Masoury.			Revetting.						Clearance of prickly pear.						Miscellaneous.								
						Quantity.	Value.		Quantity.	Value.		Collecting of stone.		Laying stone collected.		Quantity.	Value.		Quantity.	Value.		Quantity.	Value.		Quantity.	Value.						
							At Normal rates.	At Estimate rates.		At Normal rates.	At Estimate rates.	Quantity.	Value.		Quantity.		Value.			Quantity.	Value.		Quantity.	Value.		Quantity.	Value.					
													At Normal rates.	At Estimate rates.			At Normal rates.	At Estimate rates.			At Normal rates.			At Estimate rates.			At Normal rates.	At Estimate rates.	At Normal rates.	At Estimate rates.	At Normal rates.	At Estimate rates.
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32	
61	Reaching touchments of the Goomby Tank	1187	1060	115	2364	1125	115-10		3302	1698-4																	1123	112-6		1751-4		
62	Closing breaches and strengthening the bank of the Goomby Tank	11393	2876	5539	6772	10147	5713-3					337	305-2	162	202-2	271	12-0										520	115-0		6711-9		
64	Construction of the tank																														55	16
65	Construction of the tank																															
66	Construction of the tank	11877	2517	2075	5333	1133-7			30072	375-15		92	138-0	19272	267-9	1475	37-15										5772	67-44		2719-15-8		

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5/5

5

* The No of Corder could not be given for 1 of the work for the tank in Corder
When of 10 to 834-15-10 as the payment was made to the Contractor
Bills, the work to be done in masonry.

Superintendent Engineer's Office & Circle
Comptroller 20th Decr 1878

Major R. O.
Superintendent Engineer & Circle.

^{11/11/79}
 From Rev No 102
 The Supy Engineer
 & Circle
 To The Chief Engineer
 M.D.
 Rev. Dept
 8 nos. of 11 of Aug 1879
 Back Nos 152 to 153

Dated 20th December 1879

And 7 parts

200

Statements in form of
 Roads and Irrigation

No 30.

Transferred to the
 Revenue Department in con-
 -tion of Endorsement
 5693 dated 18th Dec 1879

X m 4922 of 30-12-79

6 Jan 1880

Wm. B. Clark
 Asst. Chief Engineer

Mr. W. B. Clark
 11/11/79
 Communicated to the Engineer
 Public Works Branch

11/11/79
 10/11/79
 9/11/79
 10/11/79

25 P. M. Sept.
 4 P. M. Sept.
 13th of Revenue
 20 Cords of Coimbatore
 6 Chief Engineer
 1 Exp of P. M. Accounts

64/11/79 13/11/79

4/12
 Nov 152 & 153

9/1/79 12/1/79
