

(1) Number of pages _____

(2) Date of repair _____

(3) Initials of the Referencer _____

MADRAS RECORD OFFICE.

Government of Madras.

Public Works DEPARTMENT.

G.O. No.	1613	Press
		Mis.
Dated	2-16-	1866.

Not to be folded or roughly handled

Superintending Engineer's
Office 1st Division
No. 64
Waltair 14th May 1864

To
Hon^{ble} Lt. Colonel Chambers R. E.

Superintending Engineer
1st Division

To
Colonel C. A. Orr R. E.

Secretary to Government
D. D. W.

Sir,

Referring to para 110 of G. O.

No. 381 of 6th February 1864, I have the

honour to forward 3 statements marked

A, in which the information called for

by Government, is duly given.

2. I beg also to enclose 3 other

statements, marked B, in which the

works, on the allotments of which

excess outlays have taken place, are

embodied, and to request that, as

the savings on other works from

which the surplus expenditure is

* For
Goujan
Vizagapatnam
and
Godavary.

* for
1863-64.

referred

(2)

referred to can be met; are also
pointed out in the same statement,
the necessary sanction of Government
may be accorded to the revised
allotment entered opposite each work
to enable the Comptroller and Auditor
of Public Works Accounts to pass
Bills for the apparent necessities.

I have the honor to be

Sir,

Yours Most Obedient Servant.

Wm. Chambers Holbe
Superintending Engineer, W. Division

~~As per memo~~
managers

No. 53.
 I am in receipt of your letter of the 10th inst. and in reply to inform you that the same has been forwarded to the proper authorities for their consideration.

18th May 1864
 1864

The Secretary to the
 Public Works
 Department
 Madras

The Secretary to the
 Public Works
 Department
 Madras

The Secretary to the
 Public Works
 Department
 Madras

The Secretary to the
 Public Works
 Department
 Madras


Statement showing the present allotment and that proposed for each of the following works which are in execution during the year 1863-64.

Name of work	Amount of present allotment		Amount of proposed allotment		Total
	Estimated	Actual	Estimated	Actual	
Constructing Railway to the 3rd S. S. Hospital	61	61	65	65	126
Enlarging Kuruvah, Salt Platform	630	300	354	355	984
Constructing a Calingulak and 2 Divisions to the 3rd S. S. Hospital	2840	829	839	840	3679
Constructing a Calingulak and 2 Divisions to the 3rd S. S. Hospital	2660	1078	1504	1505	4165
Road from Kuruvah to Gungewah	8720	4476	5300	5301	14021
Road from Viganagrum to Cherpurpilly	20430	9500	9833	9834	30264
Zillah, Jail at Vizagapatam	20350	10000	6699	8344	34993

Superintendent Engineer
 Office 1st Division
 Madras

Superintendent Engineer
 Office 1st Division
 Madras

18th May 1864

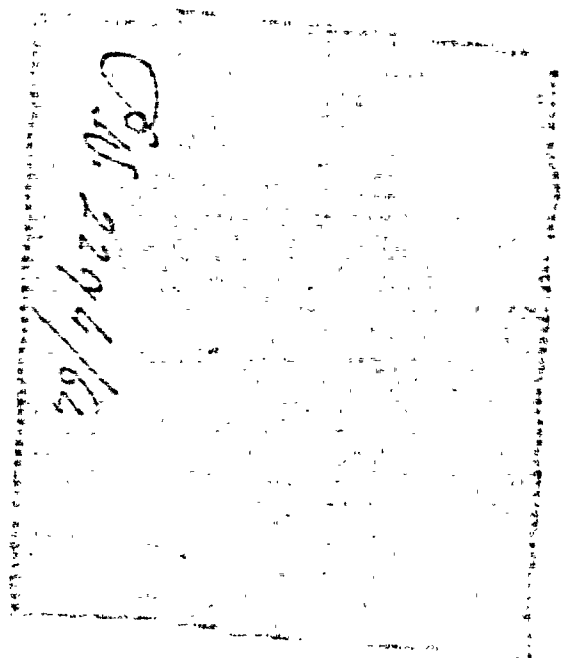

Chengam, Madras
1864-65

Statement showing the present allotments and total proposed for each of the following works which were undertaken during the year 1863-64

Names of works	Amount of Estimate		Amount allotted for 1863-64		Expenditure in 1863-64		Balance		Remarks
	1863-64	1864-65	1863-64	1864-65	1863-64	1864-65	1863-64	1864-65	
1 Jail at Berhampore	17,750	13,957	17,750	14,423	14,423	14,423	0	0	from Rs 1008 balance
2 Road from Akota to Mund...	200		200						
3 Road from Akota to Mund...	64,660		64,660						
4 Branch Road from Bul...	4,000		4,000						
5 Road from Bul...	22,670		22,670						
6 Bridges Over Brahantra...	16,000		16,000						
Minor	400		400						
Minor New works	2,500		2,500						
							2,568		
							1218	1218	

Road from Meeramundalam to howpada salt pans	6460	6460	6460	6182	6182	278
Road from Bursolich to Loola salt Platform	2000	2000	2000	992	992	1008
						2,588

Superintending Engineer's Office
 1st Bn. Ballair 16 May 1864

Oliver Chamberlain
 Superintending Engineer 1st Bn.

[Signature]

From
The Superintending
Engineer of
Division

To The Secretary to Govt.

Dated 16th May 1864
D.P.M.

Received
P.O. 2296/61,

Statement showing
the works on which the
Actual Expenditure
incurred up to the end of
1863-64 has been set out
in the Budget for 1864
65, in Column entitled Ex-
penditure up to 30th April 1864.

From

The Superintending Engineer
of Division

To

The Secretary & Comptroller
of Public Works Department

Madras

Recd.
No.

P.M. 2296/61

Statement showing the works
on which the actual outlay
up to the end of the year 1863-64
exceeds the amounts entered in
Budget for 1864-65 in the
Madras Comptroller & Secretary's
30th April 1864.

①

Statement showing the work on which the actual expenditures incurred up to the end of 1863-64: has exceeded the amount authorized in the Budget for 1864-65 in Columns Confirmed September 1864 up to 30th April 1864

Amount of actual expenditures in excess of authorized amount for 1864-65 April 1864

Communications
Metalled Roads

1 Road from Meeramundalam to Pudukkottai - 6460, 5000 618111. 118111.

31 Oct 279

This excess has been met from the amount of Rs 4460, allotted from the Revenue for Expenditure on this work in 1863-64. -

Superintendent Engineer's Office
Madras Division Station
16th May 1864.

M. Chambers. Commr. & Secy.
Superintendent Engineer & Division

②

Statement showing the works on which the actual Expenditure incurred upto the end of 1863-64 has exceeded the amounts entered in the Budget for 1864-65 in column Computed Expenditure upto 30th April 1864. —

(5)

Number	Name of work.	Amount of Estimate.	Computed Expenditure as per Budget for 1864-65	Actual Expenditure.	Difference	Remarks.
1.	Constructing Sea fort. House at Vizagapatam	4510	2000	2673 10 1	673 10 1	To Cover the Excess over the Computed Expenditure entered in the Budget for 1864-65, 860 Rupees were sanctioned by Government on the 4 th April. See G. O. No. 940 of that date. —
	Constructing Civil Dispensary at Bimlipatam	3945	1985	2387 8	1102 8	To Cover the Excess over the Computed Expenditure entered in the Budget for 1864-65, 1000 Rupees were sanctioned by Government on the 4 th April. See G. O. No. 940 of that date. —
3.	New Salt Pans at Bimlipatam	9820	5686	6956 8 9	1270 8 9	To Cover the Excess over the Computed Expenditure entered in the Budget for 1864-65, 1270 Rupees were sanctioned by Government on the 4 th April. See G. O. No. 940 of that date. —
4.	Trunk Road N ^o 6 from Chittimaleah to Chiacole.	93460	25000	27598 10	2598 10	This Excess Expenditure has been met from the unexpended balance of the Allotments of the following work. — Construction of Jeyapore Road from Tiragapatam to Kotoor. Allotment — 6000 — Expenditure in 1862-63 ————— 3308-15-1

Savings transferred to Trunk Road. ————— 2691-11

Superintending Engr. Office. Secy.
Maltair May 1864.

Ord. Chamber Lieut. Col. R. B.
Superintending Engineer first division.

Proceedings of the Madras Government
Under date the 2nd June 1844.
Read the following

Forwards 3 Statements marked A
showing the actual Expenditure
incurred during 1863. 64 also another
set of 3 Statements marked B
showing Excesses of Expenditure
during the past official year.

H. E. 17th May 1864. No 64

10

of
from
The California Engineer
No. 1
The Secretary & Government
of Public Works & State
Roads
State
Road
No. 22214/04

Of the amount showing the work
on which the actual expenditure
incurred up to the end of 1863-64
has exceeded the amount estimated
in the Budget for 1864-65 in
columns headed "Confundit & perit"
there was 30% April 1864. —

With this letter
the Superintending Engineer
1st Divⁿ submits the follow-
ing statements -

A. Having the sums expend-
ed on works during the past
Official year in excess of those
intend in the current years
budget under the head "Com-
puted expenditure up to 30. June

B. having the outlay
on works during the same
period, in excess of their
allocments, and the same
against which the excess
are to be charged.

Rs. 11,60 are provided
in the present year

Budget for the work
noted in the margin

As however it appears
that the amount, Rs. 5,000,

entered as the "computed
expenditure up to 31st April
1864" has been exceeded

by Rs. 1,181-11-0, and

as Rs. 279 only are
now required for the

completion of the road

Road from Heeramun,
Dalum to Norepaddah
Salt pans Estimate Rs.
- 6,460 Jemayam Dutt

Colonel Chamber
will report on what other
works in the Budget
he would propose to ex-
pend the available
funds. (11)

The actual ex-
penditure upon the con-
struction of the new
Custom House at Vizag-
apatnam ~~is~~ is given
at Rs. 2,673, while the
List of incomplete works
forwarded by the Supy
Govt on the 11th Nov 64
it is entered at Rs. 2,693
The cause of this differ-
ence should be explained

I

The J. S. C. approve
of the excess expenditure
from Income Tax funds

on the work noted in
the margin being charged
against the allotment

(from similar funds) for
the Jeypore Road from
Vizagapatnam to Kotoor.

They also approve of the
sum expended on work
in 1863/64 in the Jeypore
and Vizagapatnam Districts

in excess of the allot-
ments being charged
against the sum specified
opposite to each in

Expenditure Rs 27598.10.
Allotment Rs 25000
+ Rs 2578 Rs 2598.10

Trunkroad No 6 from
Chulowalea to Chicacole
Vizagapatnam St

Rs 6000

opposite to each in
Statement B for those
Districts.

Statement B for
the Jeypore District will
be returned to the Supy
Engr, with an intimation
that as recoveries from
previous years' expenditure
were not available in
1863/64 in addition to
the allotment for that
year, the sum noted

recovery from previous years'
expenditure on Central Jail
Vizagapatnam Rs 7000

in the margin cannot
be appropriated in the
manner proposed.

Coll. Chambers will
accordingly prepare
submit a revised

Statement for the
Godavay Distt showing
the source from which each
excess is to be met.

The estimated cost
of the work marginally
noted is entered as Rs. 28650 -

The Supergr. will be
reminded that the sum

Estimated sanctioned in
G.O. No. 816 of 17th March/64
amounted to Rs. 41960 -

So. Ho. & Culmugulaho
in the Mundaipetla
Canal

W.B.

The Supergr. 1st 1st with 2
printed Stat^s & 1st Statement
B for Godavay Distt
Aoch Land
Conlr. with 2 printed
Statements -

Sanjiv Kumar

W 1864 Dept
Pro. of Govt for June

7th 1863
Pro. of the Albany
of 2nd June 1864

Washington State
amount showing the same
expended on blacks
during 1863/64 in excess
of those entered on the
Budget of 1864/65 under
the head Compulsory
education up to 30th
April 1864; &c.

No 55. 56
