

Public Works (1899) Department.

G.O., No. 1979 W

DATED 28 July 1899.

[Despatch Abstract.]

Anamalai Division:

Cancelling G.O. No: 1191 W of 3rd
May 1899. Treating the — as a Sub Division
of the Coimbatore Division for Accounts purposes
and stating that the Examiner will arrange
to post an Accountant to the —

Po.

BACK PAPERS.

FURTHER PAPERS.

G.O.	No.	Department.	Date.	G.O.	No.	Department.	Date.

P. W. DEPARTMENT.

READ the following:—

From the Sept. Inscr. in Circle, No 348 W
of 3rd July 1899

Circulated to

ORDER.

The Supty. Engineer, IV Circle, having represented that there was no necessity for the services of an accountant in the Anamalai division, it was decided in G.O. No 1191 W dated 3rd May 1899 that that division should be treated as a sub division of the Coimbatore division for Accounts purposes. The Supty. Engineer now brings to notice that this arrangement is not acceptable to either the Anamalai or the Coimbatore Division Officer. G.O. No 1191 W dated 3rd May 1899

it accordingly be can-
celled and the examine
will arrange to post an
accountant to the ana-
malai Division.

19/7
19/7
19/7

The left ledger, W
Circle, having been
that there was no
for the account of
accountant in the
malai division, it was
decided in 80 W 141 W
dated on 12/12/99 that
that division should be
treated as a sub-division
of the Comptroller's division
for accounts purposes. The
left ledger was being
to notice that the same
amount was not acceptable
to enter the Comptroller's
the Comptroller's division.

To
The Supy. Inq. W Circle
" Examine, P.W. Accts.

29/1/99

P.W. (1899) Department.

CURRENT No. 5404

~~linked 5467~~

for orders.

all
with
DW

From

SE IV Circle

No. 348 W

Revised

12/2/99

Dated 3rd July 1899

Received 5th " "

Registered " " "

Enclosures

Spare copies

rule under minute
what last

SUBJECT.

File incomplete
N.S.C. said he did
not want an accountant;
but this was pondance
is not put up. see note
P.W. 7/55
in 2076, 18750 + 119
29-3-58 799

Submits Suspicion notes
in Annamalai Land to

2076, 18750 + 119
29-3-58 799

all complete
12/1/99

12/1/99

BACK PAPERS.

G.O.	No.	Department.	Date
	1191W	OW	3-5-99
	1875C-		29-3-99
	2077C-		14-4-99
	1751C-		23-3-99
	624W-		1-5-99
	2014W-		13-7-96
	1591W-		27-5-96

FURTHER PAPERS.

G.O.	No.	Department.	Date.
	2419W	OW	30-8-99
	2386W-		6-8-99
			8 Feb

No 348
5

Notes of inspection of
A. H. Ganett Esquire, Superior -
- leading Engineer, W. Chile

June
23-24

Anamalai Road.

Division office and Quar-
-ters for Mr. Brodie.

These buildings are
both progressing slowly and
are only up to basement
level. Stables nearly finished.
The well has been carried
down a considerable depth
through rock and I should
say there was very little
chance of ever meeting
with water. No work
should be done in excess
of the estimate till a
report has been submitted
showing the prospects of
getting water by giving
level of water surface
in neighbouring wells
and a description of
strata pierced for purpose
of

of comparison

Office Establishment.

As the work is all going to be done on Contract I thought an accountant unnecessary and that the accounts could be managed by the head clerk. As this procedure is however against the rules, the Division is for accounts purposes treated as a Sub Division of the Coimbatore Division. This arrangement is not acceptable to either the Anamalai or the Coimbatore Division officer and I think it would be a far better plan to have an accountant instead of a head clerk. This would only cost Rs 10/- a month more and I should be glad if early orders could be passed on the proposal.

Aliar Bridge. Girders over

The Dypty. Insp. himself said that there was no necessity for an Accountant. If he now requires one, No 1191 Wd 3.5.95 must be cancelled.

Cancel it & ask C to send an acct.

12-2-11

over two spans have been put up. There has been some delay in consequence of the late arrival of girders from Calcutta, Bunn & Co. have completely failed to despatch the girders within the time agreed upon. Mr. Brodie expects to complete the Bridge within two months from now, but I am doubtful about this.

Road up to 3½ Miles.

This portion of the work was given to Syed Abdul Razack Sahib who has proved a very incompetent man for a large work. He invariably breaks promises and should only be given small works in future.

In the first mile of the road too much blinding has been put over the metal and some of it is nothing but mud

The grave used in other places is of excellent quality and the road has a very good surface. The work might be made to look a little neater and the Executive Engineer has been asked to attend to this. The Contractor has been delaying the small road bridges and they will now be taken out of his hands. Proper designs have been prepared for these works and approved by the undersigned.

Messrs Mitchell and Mackenzie are working between $3\frac{1}{2}$ miles and Punachi. In another month they will have completed all the blasting and earthwork and will then put in hand pavements and metalling. The value of the work turned out

by them up to date is about $\frac{1}{2}$ lakh, and there is no fear of the grant not being fully utilised.

Estimate

There has been great delay in submitting this partly due to Mr. Wood having been laid up with fever. I am daily expecting the Estimate for the road up to Punachi.

As regards the estimate for the remaining portion, the longitudinal section from 11 to 21 miles has been plotted and inked in and all (250) of the cross sections have been plotted and 132 inked in.



June 29th 1899.

Inspected married Quarters at West Hill one

One block nearly completed
and will I think make
very comfortable quarters.

The Executive Engineer
wishes instead of im-
proving the second
block to dismantle
it, and build an
entirely new set of
quarters. He was led
to make this suggestion
because he considered
it somewhat risky
raising the partition
walls which are only
9" thick, and also
because the present
basement being low,
air is excluded
by the high ground
in rear.

This latter point
however has been
taken into consideration
in designing the im-
provements, and as
the

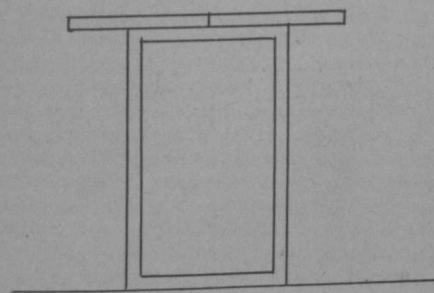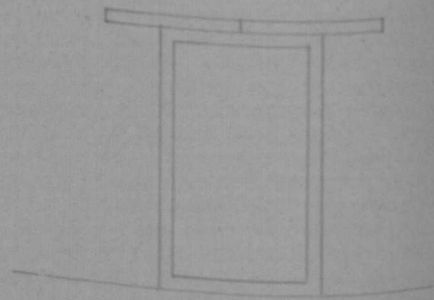

The new roof is lighter
than the old one, the
partition walls may
safely be raised.

I much regret to find
it will be necessary
to send in a revised
estimate for the work.

It was found that the
lintels over doorway
were in two pieces so
that the whole weight
of the walls rested on
the door frames. As
the walls had to be
raised the Executive

Engineer very properly
decided that it would
be necessary to insert
relieving arches. Another
reason for revision is
that in estimating for
the new front verandah
no allowance was
made for the fact
that the retaining
wall

wall had to be built
on sloping ground.
This mistake must
be put down to Care-
lessness, but with
regard to the lintels
it may be pointed out
that the presence of
the occupants inter-
feres with a very mi-
nute inspection of
the interior of a building

Police Superintendent's
Office, Calicut.

The roof is now on
and the building will
be completed by the
end of next month. Progress
has I understand been
delayed by the difficulty
in getting good timber.

Initiated
July 1899 }
Supt Engineer W. C. M. C.

To Mr. M. C. M.

Notes of Inspection of
A. H. Garrett Esq. - Supt. Engineer
IV Circle for June 1899.
