

(1) Number of Pages 10
(2) Date of repair 11.2.1969
(3) Initials of the Referencer S.V.B.

MADRAS RECORD OFFICE

GOVERNMENT OF MADRAS

Revenue. DEPARTMENT

G.O. No.
B.P. No.

519

Press
Mis.

Dated 21.4.1976 196 .

Not to be folded or roughly handled

No. 121. Read the following Proceedings of the Board of Revenue, dated 31st March 1876, No. 886, Forest No. 34 :—

Read the following letter from J. R. COCKERELL, Esq., Commissioner of the Nilgiris, to C. A. GALTON, Esq., Acting Secretary to the Board of Revenue, dated Ootacamund, 28th February 1876, No. 11.

GOVERNMENT Order, Revenue Department, No. 1,294, of 27th August last, calls for plan and estimate for office accommodation for Major Jago, the Deputy Conservator of the Nilgiri Range, to be attached to the Commissioner's Office. I have the honor to submit the plan and estimate, amounting to Rupees 6,000, prepared by the District Engineer.

2. The addition consists of an elongation of the eastern wing of my Office, and will consist of three rooms, 18' 8" by 12', with a bow window.

3. Under the altered circumstances of the Forest Department, this letter is forwarded to the Board through the Conservator of Forests.

No. 322.

FORWARDED to the Secretary, Board of Revenue, by the Conservator of Forests.

MANANTODDY,
7th March 1876.

(Signed) R. H. BEDDOME, Lieut.-Col.,
Conservator of Forests.

SUBMITTED for the orders of Government with reference to G.O., dated 27th August 1875, No. 1,294.

2. The Board approve the plan which, it is presumed, has the approval of the Commissioner also, although he expresses no opinion.

(A true Copy and Extract.)

(Signed) C. A. GALTON,
Acting Secretary.

No. 122. ORDER THEREON, 21st April 1876, No. 519.

Forests, No. 10.

ORDERED to lie over for the present.

(True Extract.)

(Signed) D. F. CARMICHAEL,
Secretary to Government.

To the Board of Revenue.
,, the Conservator of Forests.

Exl. A. Grubert.

519
2

FOREST No. 34.

PROCEEDINGS OF THE BOARD OF REVENUE, dated 31st March 1876, No. 886.

Read the following letter from J. R. COCKERELL, Esq., Commissioner of the Nilgiris, to C. A. GALTON, Esq., Acting Secretary to the Board of Revenue, dated Ootacamund, 28th February 1876, No. 11 :—

GOVERNMENT Order, Revenue Department, No. 1,294, of 27th August last, calls for plan and estimate for office accommodation for Major Jago, the Deputy Conservator of the Nilgiri Range, to be attached to the Commissioner's Office. I have the honor to submit the plan and estimate, amounting to Rupees 6,000, prepared by the District Engineer.

2. The addition consists of an elongation of the eastern wing of my office, and will consist of three rooms, 18-8" by 12', with a bow window.

3. Under the altered circumstances of the Forest Department, this letter is forwarded to the Board through the Conservator of Forests.

No. 322.

FORWARDED to the Secretary, Board of Revenue, by the Conservator of Forests.

MANANTODDY,
7th March 1876.

(Signed) R. H. BEDDOME, Lieut.-Col.,
Conservator of Forests.

SUBMITTED for the orders of Government with reference to G. O., dated 27th August 1875, No. 1,294.

2. The Board approve the plan which, it is presumed, has the approval of the Commissioner also, although he expresses no opinion.

(A true Copy and Extract.)

Ch. A. Galton
Acting Secretary.

To the Secretary to Government, Revenue Department,
with plan and estimate, to be returned.
,, the Commissioner of the Nilgiris.
Copy to the Conservator of Forests.

Exd. A. Gruberf.

Govt. of Madras.

REVENUE.

THE BOARD OF REVENUE.

Dated April, 21st.

Recd.

G.O. 21st April 1876, No. 619.

Encl.

APRIL.

Nos. 121-122.

Office Accommodation for Major Jago, Deputy
Conservator of the Nilgiri Range.—Consent
to the over Proceedings of the Board of Revenue
submitting plan and estimate for—

— Detailed Estimate No. 67 of 1875-76 —

519/25

— Neilgherry District —

Work. Cost of proposed additions to the Commissioner's Office at Ootacamund, providing accommodation for the Deputy Conservator of Forests.

No.	Measurements			Contents	Particulars
	L	B	D		
————— Brick in Chumam —————					
2	40-0	2-2	3-0	620-0	Foundations to front and rear walls
2	17-8	2-2	3-0	229-0	" Cross walls
1	8-8	2-2	3-0	56-4	" End wall
1	17-0	2-2	3-0	110-6	" Bow window
3	5-0	1-0	3-0	30-0	" projection to chimneys
3	4-3	2-0	0-9	19-1	" Steps
2	39-3	1-8	2-0	261-8	Basement to front and rear walls
2	18-2	1-8	2-0	121-1	" Cross walls
1	8-8	1-8	2-0	28-11	" End wall
1	17-6	1-8	2-0	58-4	" Bow window
3	4-6	1-0	2-0	27-0	" projection to chimneys
3	4-0	2-0	0-8	16-0	" Steps
3	4-0	1-0	0-8	8-0	" "
2	39-6	1-2	13-6	1244-3	Front and rear walls
2	18-8	1-2	13-6	587-3	Cross walls
1	8-8	1-2	13-6	136-6	End wall
1	18-0	1-2	10-6	220-6	Bow window
3	4-0	1-0	22-0	264-0	Chimneys
3	19-0	1-2	5-0	332-6	Gables
3	3-0	3-0	9-0	20-3	Chimneys above roof
1	6-0	1-2	1-0	7-0	Gable to ventilate roof
				4298-2	Total
				343-2	Deductions
				3955-0	Total cft. of Brick in Chumam

Q. D. 27 August 1875

No. 14/14

Resoln 1876. &c

Board of Revenue,

MADRAS.

PROCEEDINGS, 31st MARCH 1876, No. 386.

Copy 604/1876

Encl.

Received 7:00 AM 1876

MARCH
Forest No. 34.

Office accommodation—for Major Jago, Deputy Conservator of Nilgiri Range.—Approving and submitting to Government plan and estimate for —

No. 579. 21 June 1876
with plan.

114 To Mr. Secretary, Government of Madras
81 Mr. Conservator of Forests

21st June 1876

Advert this over for the present.

No. 579

C. 20: 64/1876 A 21: 64/1

3	5-0	1-2	0-9	13-1	Dows
2	4-6	1-2	0-9	7-10	"
2	5-0	1-2	0-9	8-9	win Dows
3	4-6	1-2	0-9	11-10	"

3	5-0	1-2	0-9	13-1	Dows
2	4-6	1-2	0-9	7-10	"
2	5-0	1-2	0-9	8-9	win Dows
3	4-6	1-2	0-9	11-10	"

2 4-6 1-2 0-9 7-10

2 5-0 1-2 0-9 8-9 windows

3 4-6 1-2 0-9 11-10

41-6 Total c.f. of Archwork

63 Squares of Plastering

63 squares of white and yellow washing
Flooring

0	684-0	Rooms
2	11-8	Born window
0	24-0	"
	719-8	Total sq. ft. of Leak flooring &c

0	684-0	Rooms
2	11-8	Born window
0	24-0	"
	719-8	Total sq. ft. of Leak flooring &c

2 11-8 Bow window
-0 24-0 "
7-9-8 Total sq. ft. of Leak flooring etc
Cut floor

24-0
719-8 Total sq. ft. of Leak flooring bc

719-8 Total sq. ft. of Leak flooring &c

24-0 Steps Cut stone work

24-0 Total sq. ft. spent stone work

24-0 Total sq. ft. spent stone work

1148-0 Building

1148-0 Building

287-0 Ventilator
1435-0 Latex

1435-0 Total
345-0 in aspage

345-0 wasage
1780-0 Total Grps. of roosting with the al

1780-0 Total Exps. of roofing with teak shingles

38-5-3 Rafters woodwork

4 38-5-3 Rafters
1-0-0 male white box

1-0-0 wall plate to B. window
4 8-11-7 rafters

4 8-11-7 Rafters
1/2 3-0-8 H. Rafters to B. W.

3-0-8 H. Rafters to B. w
35-7-1 Purkins &c

6-3-0 B. W. C. after

6-10-0 Stubs to ridge Vambikator
7-6-0 Beans

7-6-0 Beans
3-4-0 Cotton prices to

3-4-0 Collar pieces to _____
110-11-7 Total

110-11-7 Total
36-0-5 wastage
147-0 Total cft. woodwork wrought- Iron etc.

147-0. Total cts. of woodwork wrought - 8 feet 1/2

— Eggs and windings —

4-0 - 8-0 96-0 Sous

3-6 7-0 49-0

4-0 7-0 56-0 winds

3-6 5-6 57-9

258-9 Total Acft. of Bors & Associates

3 teakwood Surfer & complete

340 Running feet - perineal work

64 ref. fr. of continuous line signing

Abstract Estimate No. 17 of 1875-76

Neil Cherny District

work - Cost of additions to the Commission's Office at Ootacamund, providing accommodation for the Deputy Conservator of Forests.

	Particulars	Rate Per	Am't	Total
2755	Cfr. of Brick in chumam	40 " each	1582 " "	
42	Cfr. of Archwork in chumam	45 " "	1844	
63	Squares of Plastering	10 " sq ft	630 " "	
63	Squares of white and yellow washing	14 " "	552 " "	
220	Sqft of Teak flooring &c	102 " "	73464	
24	Sqft of cut stone for steps	85 " "	2064	
180	Sqft of roofing with teak shingles			
	reapers, Carpenter's line nails &c	35 " "	623 " "	
147	Cfr of teakwood wrought & put up	4 " cfr	588 " "	
259	Sqft of doors and windows	24 " sq ft	58212 " "	
3	Teakwood timbers &c complete	80 " each	240 " "	
340	Sqft of cornice work	14 " sq ft	425 " "	
64	Sqft of continuous iron roofing	2 " "	128 " "	
	Excavating foundations		8 " "	
		Total	56359 " "	
		Lundries	3647 " "	

Total Estimate Re^y ^{Surplus} 3647. 6000.

Specification

The Proposed additions to the Commissioner's Office consist of 3 rooms viz: one 12' x 18' x 8" with a Bow window for the Deputy Conservator of Forests Office, two rooms each 12' x 18' x 8" for Clerks and Records; the walls to be 1-2" thick and 12 ft. high to the bottom of eaves, Basement to be 2 ft. deep and 1-8" thick, Foundation to be 3 ft. deep and 2-2" thick, all of brick in common, plastered, white washed inside & yellow washed outside, roof to be of teak shingles &c, 3 doors 4 x 8, 2 doors 3-6 x 7, 2 windows 4 x 7 and 3 Bow windows 3-6 x 5-6 the building to have a ridge Ventilator; steps to be of cut stone



Dist. Engr's Office
 Nilgherries
 Kotacamund 30th Decr 1875

John Morant
 Captain R.E.
 District Engineer


By A. R. No 55/76

Dec 14/14/76

Proposed additions to Office at Kotacamund

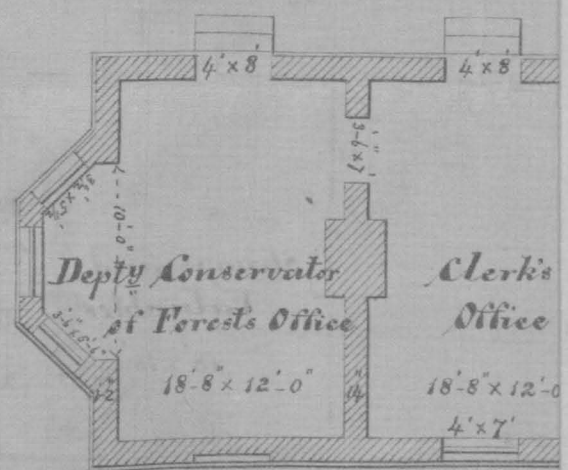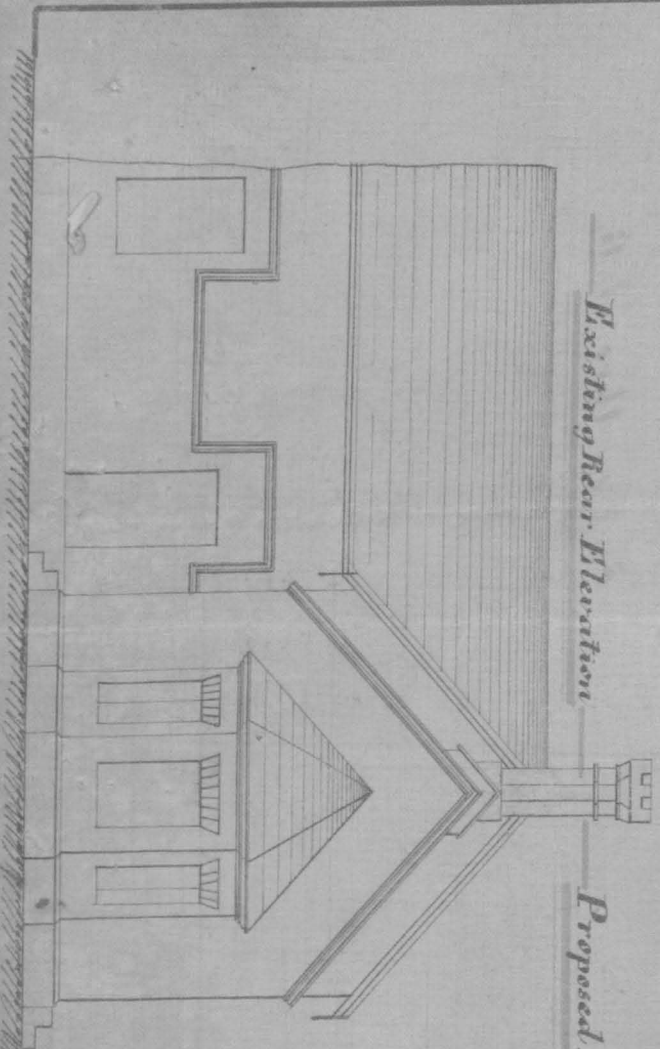

Proposed End Elevation

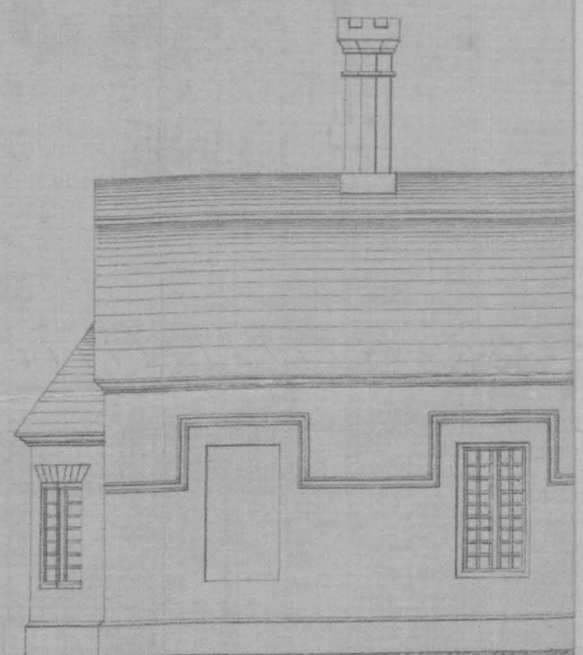

Additions - Shaded

Dist. Engr's Office
 Nilgherries
 Kotacamund 2nd Decr 1875

Blank Window

Pages 10

r. 11.2.1969


Referencer 2.4.69

OFFICE


DRAS

RTMENT


is to the Comm^{rs}
nd, providing accom
Dept^y Conservator
ests

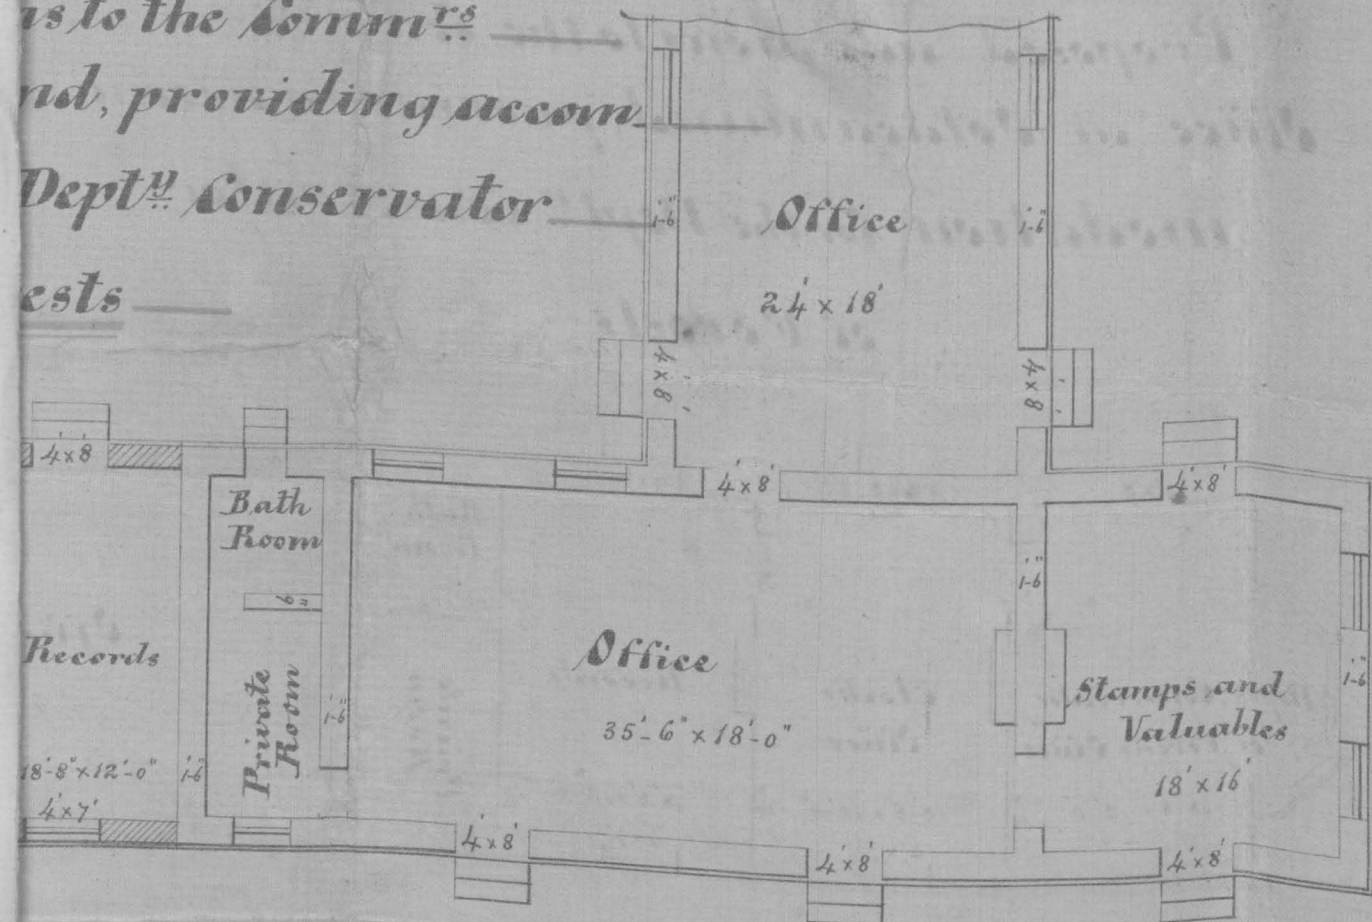

Section Thru: A.B.

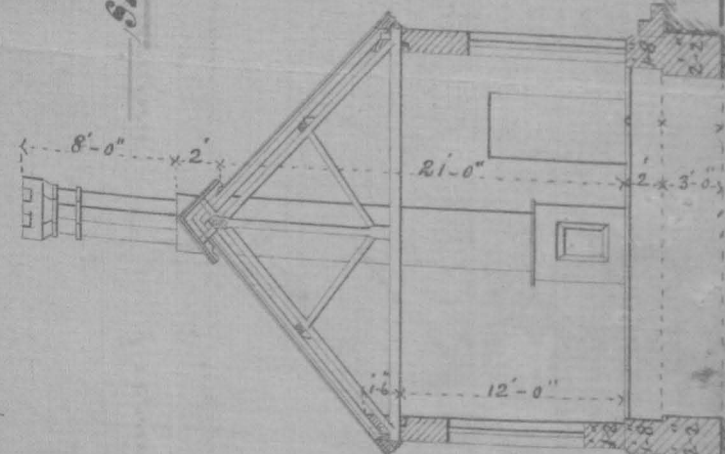

Existing End Elevation

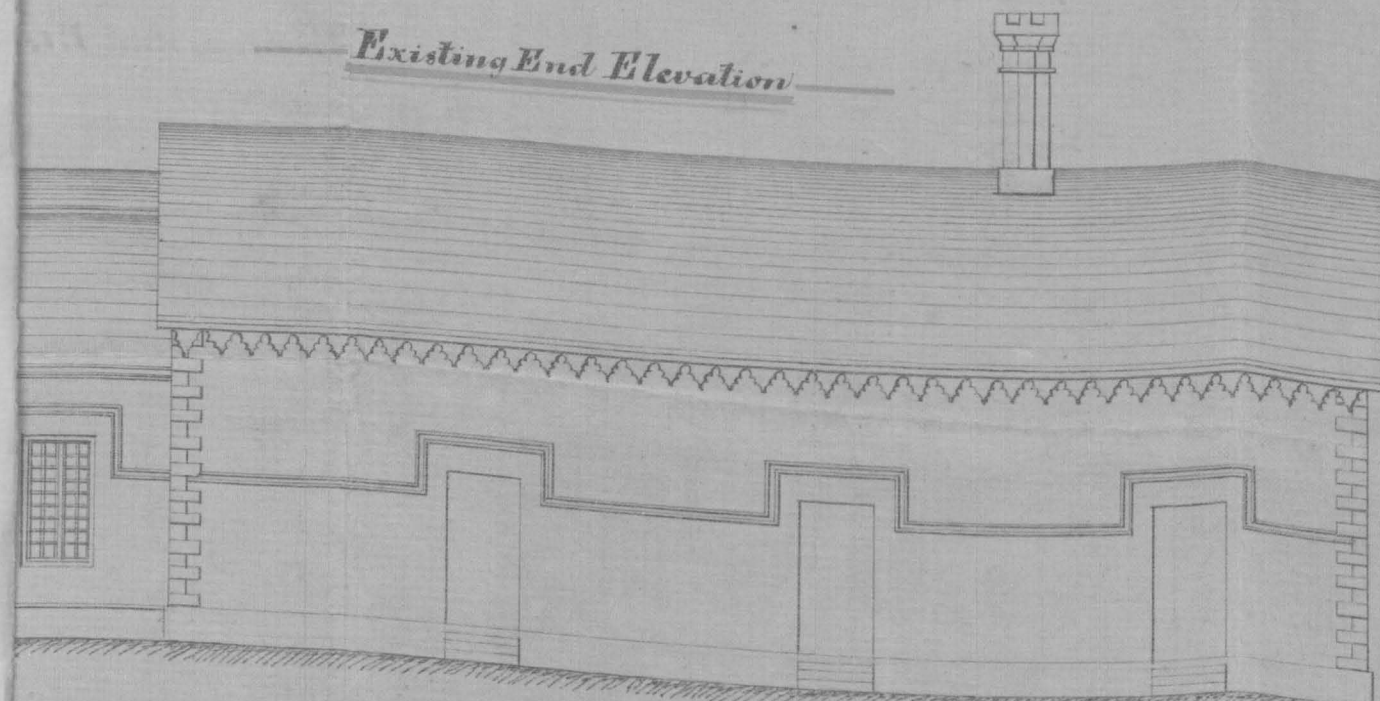

Jack Morant
Captain R.E.
District Engineer

Free
Aug 12 1858/76

Decr 14 14/36
