

(1) Number of pages _____

(2) Date of repair _____

(3) Initials of the Referencer _____

MADRAS RECORD OFFICE

Government of Madras

Public Works

DEPARTMENT

G.O. No.	1545	Press
B.P. No.		Mis.
Dated	2 - 6 - 195	6875

Not to be folded or roughly handled

*Proceedings of the Madras Government, Public Works Department,
2nd June 1875.*

Read the following :—

No. 562.

No. 52.

Note by the Officiating Chief Engineer.

THE following repair estimate has been submitted for sanction by the
Superintending Engineer, Chingleput :—

Vellampakum tank	..	..	..	..	..	..	Rupees	546
Ayacut area	..	..	..	..	..	..	Acres	116
Do. assessment	..	..	..	..	..	..	Rupees	386
Average revenue	..	..	..	..	..	..	"	313
Highest "	..	..	..	..	..	..	"	350
Expenditure on repairs in last four years	..	..	..	..	..	..	"	161

and this was divided into three years' work.

The area of the catchment basin is said to be half a square mile, and no other source of supply has been referred to. The acreage is very large for so small an area. The tank was breached in three places in the cyclone of 1874. It is proposed to provide for the disposal of surplus by an extension of the present opening of 20 feet to 60 feet. The nanel and kuskus to be here used must not be planted so as to impede discharge. The item for nanel in the estimate does not show how or where this grass is to be planted.

OOTACAMUND,
26th May 1875.

(Signed) JOHN MULLINS, Lieut.-Col., R.E.,
Officiating Chief Engineer, P.W.D.

No. 53.

ORDER THEREON, 2nd June 1875, No. 1,545.

IRRIGATION, No. 2.

THE following estimate is sanctioned :—

Repairing Vellampakum Tank, Chingleput District	..	..	..	RS.
(True Extract.)				546

Major, R.E.,
Offg. Joint Secretary to Government.

To the Superintending Engineer, Chingleput.
" Chief Engineer for Irrigation.
" Controller of Public Works Accounts.

Exd. A. Grubert.
Spare Copies

Note by the offg. Chief Engineer.

The following repair estimate has been
Enclosures 4. submitted for sanction by the Superintending
Engineer Chingleput.

Vellamparum tank	Rupess 546
Ayacut area	Acres 116
do assessment	Rupess 386
Average revenue	" 313
Highest do	" 350

Expenditure on repairs in last 4 years " 161
and this was divided into 3 years' work.
The area of the catchment basin is said
to be half a square mile, and no other
source of supply has been referred to.
The acreage is very large for so small
an area. The tank was breached in
2 places in the cyclone of 1874. It is
proposed to provide for the disposal
of surplus by an extension of the
present opening of 20 feet to 60 feet.


The

The Panel and Kuskus to be here used
must not be planted so as to im-
-pede discharge. The item for
Panel in the estimate does not show
how or where this grass is to be
planted.

Leadbolt R.C.
Offg: Chief Engineer
S.H.B.

Ostacumund
26th May 1875.

The Offg: Secy: of Government
S.H.B.

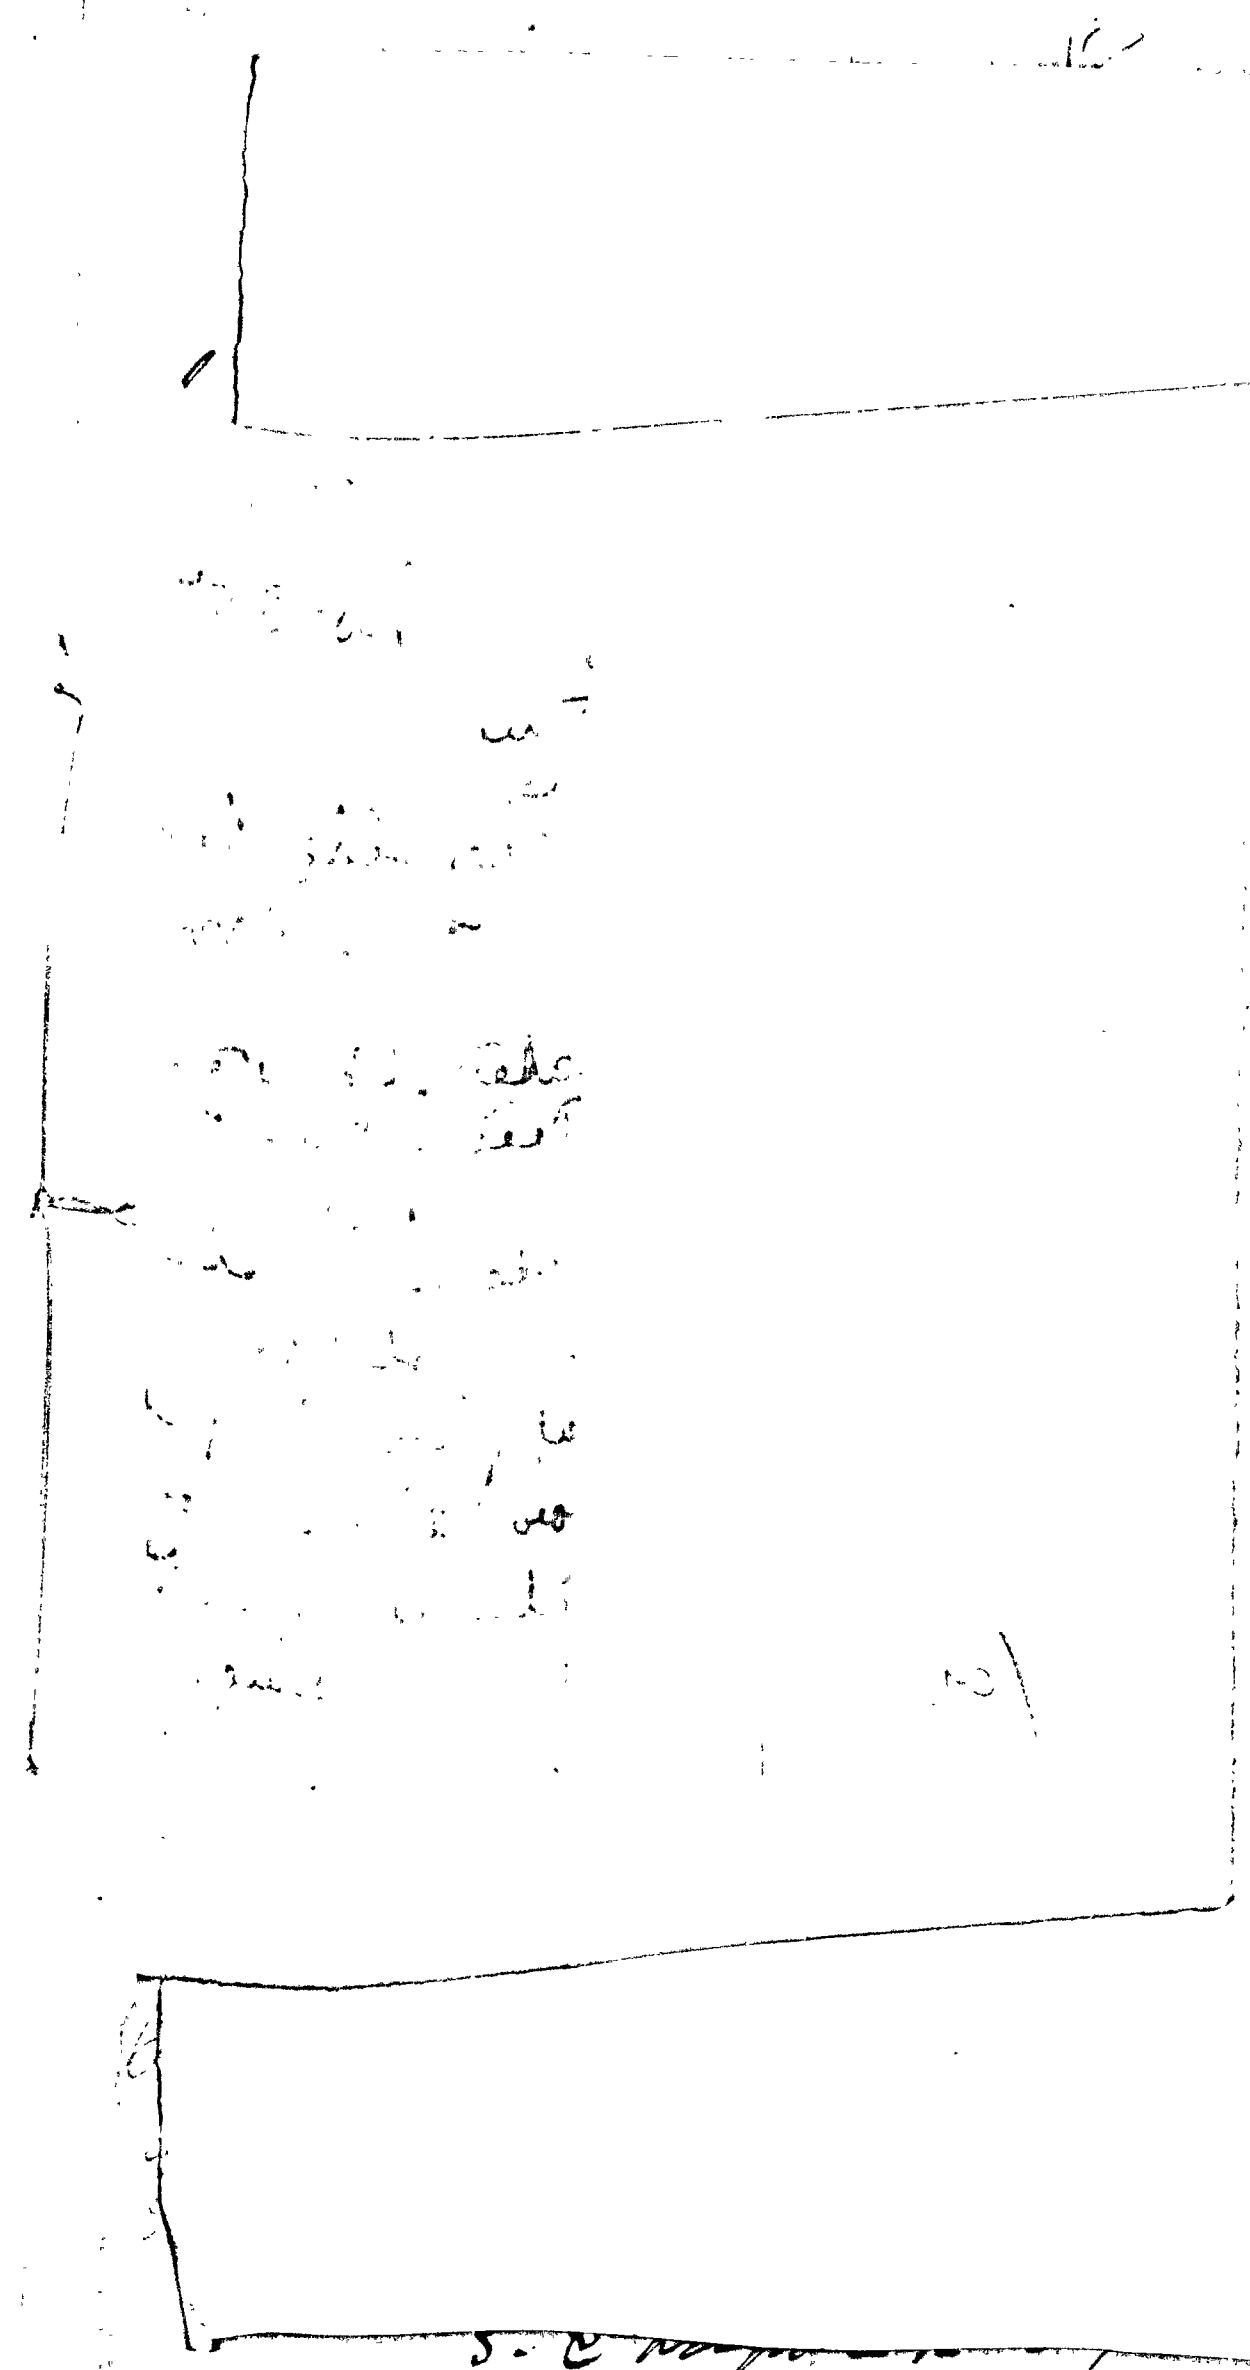

P. W. 1875 Sept.
No: 3570.

From

The Offg. Chief
Engr., P. W. D.

Dated 26 May 1875.
Recd. 31st May 1875.
No: 562
Note on an estimate
submitted by the
Supt. Engr., Chingleput
for the repair of the
Vallambakam Tank,
Ponnery Taluk.

B. No. 1545. 2-6-75.

1545

^{Sanction}
P. W. Dept.
Proceedings of the Madras Government

Read the following

From the Offg. Chief Engineer,
P. W. D. } (M. S. No. 562 d/26 May/75)

G. O. No: 1545 d/22nd June 75

The following estimate
is sanctioned.

Repairing Vallambakam
Tank, Chingleput District.
Rupees 54.6

6. Repeating Chingleput -
5. Of Engr for same with 4 Enclosures
5. To Mr. W. A. C. ✓

S. C. Bishop - 12-6-75

3570

Govt. of (1875) ~~Madras~~

PUBLIC WORKS.

To The Supergr,
Chingleput

Date:

Recd:

G. O. *L. L. L.* No 1545

Nos. 52 & 53

Vellampakam Tank,
Chingleput — Estimate
of Rs. 546 for repairing
the ———, sanctioned.
