

N^o 2414 Inspection Notes of the Suppy Eng^r 3^d Circle.

Royachoty
Cutcherry

On the 21st January I inspected the new Iron Strong room in the Salug Cutcherry at Royachoty Cuddapah District which has been erected in a satisfactory manner. The Executive Engineer has ordered a window to be opened in rear of the new room, so as to give more light at the back of the room.

Gurramkonda. On 23rd. I visited the European graves at Gurramkonda. Found that the ground had been cleared, the tombs repaired and a low wall built round them. Ordered all debris to be removed from the vicinity and the opening in the enclosure wall to be built up.


Subcollector
Cutcherry
Madanapalle

On 28th. I visited the Sub Collector's Cutcherry at

Madhanapally which with the exception of a few trifling matters may be said to be complete.

Generally the work is, I consider satisfactory, but I found fault with a few minor details as follows:-

Finials to roof to be removed the Contractor having put them up in an extraordinary not to say comical manner.

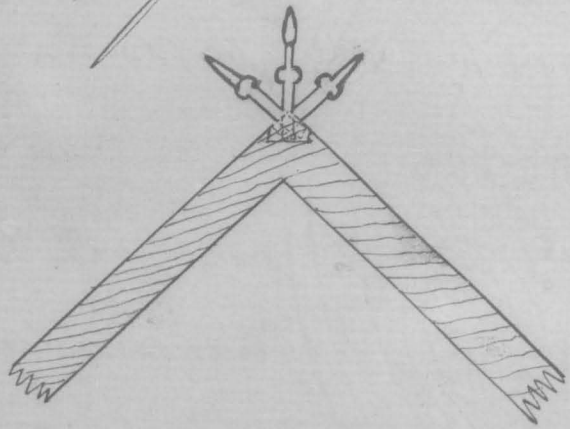

Circular lights in Court Rooms should, if now possible, be made moveable and the glass should be posted to keep out excessive sunlight.

The locks fitted to the doors very inferior. They must be replaced by better ones.

The wall in the Court room

has a mottled appearance this should be removed. The ground round the building was being cleared. A wire fence is required for the compound.

The coupled roof of the porch I think should be strengthened. It has only one collar-piece.

There is no good camping ground for Officers at Madhanapally. I would suggest that the ground in rear of the new futcherry should be reserved for this purpose and that a small wall should be built separating the camp ground from the futcherry ground. This wall should have a gate into it.

Taluk Cutcherry
Madhanapally

While at Madhanapally I visited the Taluk Cutcherry a small portion of the roofs over the covered passage between the Police room

This might be
referred for opinion
of Collector

and the Cells was insecure.
owing to bad work. ordered this
to be attended to at once. The
work ought to be finished before
the rains.

On 8th February inspected Kadiri
Kadiri Talagutcherry. Talagutcherry.

It appears in very fair
order. Merely requires
a little painting. It has
been built several years.
Some of the doors which had
been obtained from Madras
still had painted on them
the address to which they
had been sent when they
were set up. No one had
taken the trouble to have
them repainted. Ordered
this to be attended to without
delay.

On 18th February I inspected Pulivandla
Pulivandla Talagutcherry. Talagutcherry.
which has just been com-
pleted with the exception of
the wooden roof to the tower.

and some other petty matters.
The work is generally satisfactory.
factory

Jail Privy. Roof consists
of Palmyra couples with
teak bressummers. Jang
wood would have been better
than Palmyra. Another
coat of tar required. Asphalt
floor has still to be done also
the Cistern.

An aloe hedge has been
planted round the compound.
The Cook room for Jail ward
is complete. Same kind of
roof as the privy.

Jail wards. Two doors
to each double bend. One
of these should be a fixture
asphalte floor to be laid.
Iron work must be re-
pitched. Filling up over
doors to be done.

As regards the main build-
ing I may state that the
locks on the doors are not
good enough. They must

be replaced by better ones.

Another coat of paint was required for all doors &c.

Chunam has been too much daubed over the exterior stone work and effort must be made to remove this most unsightly defect.

The iron work of the Treasury requires painting.

Second Room, reached by means of the tower is complete except that the wooden shutters are not yet fixed although they are ready at the spot.

The rafters used in the Verandah are not of equal length and thus their irregularity is observed in the interior of the room where the rafters of Verandah rooms are side by side.

The painting of the verandahs should be more carefully attended to.

Whitewashing should be redone. In some parts it is put up badly.

In some cases the plaster used for wall has not been thoroughly slaked as a consequence it is observed here and there to be slaking in the wall.

Ryot Shed Complete. Coupled roof with single collar piece. It had better be strengthened.

Walls between pillars, $2\frac{1}{2}$ feet of solid wall, $2\frac{1}{2}$ feet of honey comb work. Elsewhere the solid walling has, I think, been taken up higher well. There has been great difficulty about finding water in the compound although in the L. F. Dispensary compound ^{very} closely there is an excellent well.

South of the futcherry the excavation for well has been

taken down 31 feet. no water
but solid rock this well
must be abandoned.

A former trial, I am told,
was made N. W. of the Build-
ing this excavation was taken
down 41 feet but no water was
found it is proposed to make
another trial at a point short-
ly beyond the South East corner
of the Compound

Public Latrine - Asphalt
floor has to be done and screen
walls at ends has still to be
built as also honeycomb
work

Site is good, being on high
ground, and I should think
healthy; but it is sadly
bare of trees.

As soon as the rains begin
trees should be planted

Visited Registrar's Office
completed last year.

Seems in good order but
was unable to see the
interior owing to the absence.

of the Registrar at the time
of my visit.

Henry M. Robert
Suprog Engineer
III Circle

Suprog Engineer's Office
Belgaum 10 March 86.

To The Ch. Engineer
M.D.
Madras

No 1011 Cay 12 March 86

March 1886 ✓

From
The Superintending Engineer

III Circle

Extract forwarded
to the Revenue Dept.
for favor of the
opinion of the Collector
of Cuddapah.

To
The Chief Engineer
P. W. D.

Madras



Dated 10/3 March 1886
Recd 11/3

11/3
12-3-86

No 1011 Cay 12-3-86

No 2414

Inspection Notes of the
Superintending Engineer
3rd Circle

With disposal

To
The Rev. Dept.

Desd 12/3-86

13/3

4/5/86

S. S. S. S.

Revenue Department

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ Pro. of the Board of
of 17th May 1886, Mis. No. 3347, Subm.
letter from Colr. of Cuddapah re-
-porting on the sites available at
Madanapalle for officers to camp in.

Order thereon, 21st May 1886, No. 2979.

The Board will call upon the
Collector to submit a plan, drawn to
scale, of the compound of the new Cutcherry,
referred to by the Superintending Engineer,
III Circle, marking thereon the portion
which that officer suggests should
be assigned as a camping ground.

(Enc. Extract.)

(Sd) J. T. Rice

Secy. to Govt.

(Enc. copy.)

H. S. S.

Secy. to Govt.

PROCEEDINGS OF THE MADRAS GOVERNMENT.

Read the following letter.

* Copy attached.

Mis: G.O. 21st May 1886, No: 2979.

Read also the following Res: of the Board of Revenue, of 5th July 1886, Mis: No: 5000, on letter from the ag: Collr. of Cuddapah, of 28th June 1886, No: 557.

As directed in G.O. No: 2979, dated 21st ultimo communicated with Board's Proceedings at 3992, Mis., dated 28th idem, I have the honor to submit the plan drawn to a scale of 30 ft. to an inch, of the compound of the new Sub-Collector's cutcherry, marking thereon the portion which the Superintending Engineer, 3^d Circle, suggests should be assigned for a camping ground.

2. It will be seen from the plan that the ground suggested for a camping ground is sur-

— rounded

rounded on all sides by the compound of private houses and of the Sub Collector's office and it will certainly be a nuisance to the occupants of the private houses, one of which is about 20 yards and the other 40 yards from the proposed camping ground, to have bandies, bandymen, and servants &c located so near them.

3. The Sub Collector points out that there is a piece of ground adjoining the house formerly occupied by the Sub Collector and opposite to the one now occupied by the Assistant Superintendent of Police, available for a camping ground and recommends that it be selected. This is in charge of the District Forest Officer who suggested its use as a camping ground to the

Sub

Sub Collector and does not seem to have any objection to its being used as such. A plan showing the position of the site now recommended is also enclosed. The Sub Collector reports that it is a fort: type and has now some and will have plenty of shade in it.

Resolution.

Submitted to Govt. with reference to G.O. 21st May 1886, No: 2379. The Board approve of the Commr's: proposal.

Order thereon, 24 July 1886, No: 4383.

The Collector's proposal is approved accordingly.

(Enc Extract.)

H.E. Stokes

Secy. to Govt.

To

The Board of Rev.
" P.W. Deptt.
" Mil. Deptt.

21/8/86

No 1011c. 12. 3. 86.

P.M.C. No 5975. ✓

B. W. 2007 W of 11 August/86

3. Comd to the
Supt Engr III Circle,
with reference
to his inspection
notes submitted
under No 2414,
of 10. 3. 86.
of 10. 3. 86.

Recd: 2. 8. 86.

B. W. 2007 W of 11-8-86.

1
2/8/86

W
5. 8. 86

S. E. III Circle ✓
S. E. III Circle
12/8/86

Regulation No 56. 3. 8. 86. 2. 7. 8. 86

139/7. 10/11/86

Indudakk
