M.R.O. 1—77,006—9-6-37.

(1) Number of pages _____

(2) Date of repair 4-7-00

(3) Initials of the Referencer _____

ADRAS RECORD OFFICE.

Government of Madras.

Public works DEPARTMENT.

G.O. No. 2803 Press Mis.-

88-89

Dated 6. 11 1891.

ot to be folded or roughly handled

Proceedings of the Madras Government, Public Works Department, 6th November 1871.

No. 88. Read the following letter from the Officiating Superintending Engineer, 6th Division, to the Secretary to Government, Public Works Department, dated Tanjore, 17th October 1871, No. 641 :—

I HAVE the honour to submit for sanction the undermentioned estimates aggregating Rupees 2,068, and which have received the approval of His Excellency the Commander-in-Chief.

3 Estimates.
1 Plan.

The first two estimates, amounting to Rupees 112 and 116, respectively, may be charged to the allotment of Minor New Works "Military," but the third, amounting to Rupees 1,840, will have to be provided for from the Reserve, or by a transfer from other districts, if the work is to be undertaken in 1871-72 :—

	RS.
Ventilating the Barrack Guard-room in occupation by 38th Regiment N. I.	112
Constructing four dust bins to be built of stone masonry in rear of Staff Serjeants and Family Quarters, Royal Artillery ...	116
Re-roofing the 26th Regiment N. I. Hospital	1,840
	2,068

No. 89. ORDER THEREON, 6th November 1871, No. 2,803.

MILITARY WORKS, No. 4.

THE estimates submitted with this letter are sanctioned.

2. As the Government are unable to allot the sum of Rupees 1,840 required for re-roofing the hospital of the 26th Regiment N. I. at Trichinopoly during the current official year, the Superintending Engineer should apply for funds after the 1st April next.

(True Extract.)

Colonel, R.E.,
Secretary to Government.

To the Superintending Engineer, 6th Division.
„ Controller of Public Works Accounts.
„ Military Department.

Exd. S. T. Augustin.

No. 641.

Supdg Engr's Office 6th Division
Trichinopoly 17 October 1871.

From,

Captain J. O. Hawkes. R.E.
Offg Supdg Engineer 6th Division

To,

Colonel J. Carpendale. R.E.
Secretary to Government &c &c &c
Fort Saint George.

Sir,

I have the honor to submit for sanction the undermentioned Estimates aggregating Rs. 2068 & which have received the approval of His Excellency the Commander-in-Chief—

The first 2 Estimates amounting to Rs. 112 & 116 respectively may be charged to the allotment of Minor New works "Military" but the third amounting to Rs. 1840 will have to be provided for from the Reserve or by a transfer from other districts if the work is to be undertaken in 1871-72.—

Rs.

Ventilating the Barrack guard Room in occupation by 38th Regiment N. I. } 112.

Constructing

Constructing 4 Dust Bins to be built of Stone Masonry in rear of Staff Serjeants & Family Quarters Royal Artillery ——— Rl. 116

Reroofing the 26th Regiment Hospital ——— Rl. 1840

2068

Have the honor to be

Sir,

Your Most Obdt Servt

H. Scallon Capt. RE

Offg Supt & Engineer

P. W. 1871 Depart
From Ro. of Gov. Inclosing
The Offg Supg Engr
6" D.
To, The Secretary to
Govt D.P.W.
Fort Saint George
No. 641-
dated 17th Oct 71.
Recd 20
3-C-Rd

Ten. 4. 16 Sir
Submitting for
Sanction, Estimates for
certain Military works
at Trichinopoly - and
stating how Amounts
for the same may be
provided for.
No. 2803-6 Nov 71.

No 88

Clerks 21 Oct 71 D. 304

Trichinopoly District
Abstract Est No 1871/72 3

Work Reroofing the 26th Regiment N. I. Hospital at Trichinopoly

Quantity	Description of Work	Rate	Amount	Total
5241½	Supplg of old Roof removing ——— Sqs	" 8 "	26 3 3	
118⅛	Supplg of Teakwood Wrought & put up at	3 8 "	413 6 3	
97½	Supplg of Brick in Chunam work ——— Cft	" 2 "	12 3 "	
130	Supplg of Plastering with 1st Coat of Chunam ——— Sqs	1 8 "	1 15 2	
5016	Supplg of Reroofing with Palmyra Rafters Reepers Flat and pantiles tarring and Chunam borders complete ——— Sqs	25 " "	1254 " "	
225½	Supplg of Ridge Ventilators with Palmyrah Couples Collar pieces Reepers Flat and pantiles tarring & Chunam borders Complete ——— Sqs	18 " "	40 9 5	
	Scaffolding ———	" " "	8 " "	
	Sundries and Contingencies ———	— " "	83 10 11	
			Total Estimate Rupees	1840 " "

(Signed) James Vertue Capt RE
Executive Engineer Trichinopoly

Supg Engr Office Tanjore
31st August 1871

Brigade Office Trichinopoly 12th September 1871
No. 286
Brigade Major

H. F. Dalton Capt RE
Supg Engr

Tri Chinopoly District & Pay
Abstract Est N° 1871/72.

Work— Ventilating the Barrack Guard Room in occupation by 38th Regt N.I. at Tri chinopoly.

Quantity	Description of Work	Rate	Amount	Stat
160	C/ft of Demolishing wall for Ventilators ____ at	-- 6	5 --	
8	Weather boards procured from Range Stores belonging to Central Jail ____	each 10	-- 80 --	
8	___ Do ___ do ___ Repairing Fairing & Carting from stores ___	each 1	8 -- 12 --	
8	___ Do ___ do- fixing in Wall and plastering opening 9" ___	1	-- 8 --	
	Scaffolding Sundries Contingencies		7 --	
	Total Est Rupees		112 --	

/Signed/ James Vertue Capt RE
Exc. Engr Trichinopoly

Supd Engr Offices
for Dy
Tanjore 1st August 1871

Engr Office Trichy 2nd Aug 1871
/Entered/
Asst Engr
Engr Dept Dy

Capt RE
Supd Engr 4th Dy

Bldg No 908

Collection
Building Buildings Quarters
Fencing for Military
Abstract Estimate No — 87/72.
Work Carrying Out No 26
Rupees Thousand Hundred & Eighty
Rupees 1,88[illegible] 0 — —


P.W. 4986/71

6th Division Trichinopoly District


Plan and Section of a Dust Bin 3×3×3 to be built of Stone Masonry in rear of Staff Serjeants and Family Quarters Royal Artillery at Trichinopoly

Scale 8ft

Ground Plan

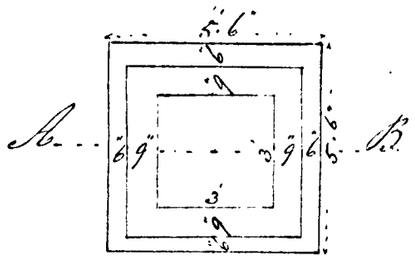

Section thro' A. B.



Supt Engineers Office
6th Divn Trichinopoly
4th October 1871
Offg Exve Engr

Military — 6th Divn — Allowance Estimate

Trichinopoly District

Est No 1871/72

Work — Constructing 4 Dust Bins to be built of Stone Masonry in rear of Staff Serjeants and Family Quarters Royal Artillery at Trichinopoly. each 3'+3'+3' interior

No	Measurements L	B	H	Contents	Particulars of Work	Rate	Amount	Total
1	2½	5½	1	12½	Foundation			
4	3½	3½	½	24½	Deduct Stone floors			
	Total			96½	Cft of Brick in Chunam at Super Structure	" 2 "	12 1 "	
64	1/10	3½		120	Side walls of 4 Arch Bins			
4	3½	3½	½	24½	Floor ditto — do — do —			
64	1	½		32	Coping of — do — do —			
	Total			176½	Cft of stone dressed & work in the inside such roughly on the out side	" 8 "	88 4 "	
					Pointing with fine Chunam in & out side of the stone Bins		7 " "	
					Excavating foundation		2 " "	
					Sundries and Contingencies		6 11 "	

Total Est Rs 116 " "

Pro 3/3
Trichinopoly 10th October 1871
(by order)
Major
Offg Brigade Major

Recommended
Capt RE
Offg Supt Engr 6th Divn

Public Works Department

No 2803 2803

Proceedings of the Madras Government

Read the following

From the Offg: Supdg: Engr 6th Division } No. 1641 dated 17 October 1871

The Estimates submitted with this letter are sanctioned.

As the Government are unable to allot the sum of Rs. 1840 required for repairing the hospital of the 26th Regiment N. I. at Trichinopoly during the current official year, the Superintg Engineer should apply for funds after the 1st April next. ——

A/T.

40
4

To The Supdg Engineer 6th Dn
5. Controller of P. W. Accts
15. Military Departt.

Recd 7/11/71

H.F.D.

24 Oct

Revised Estimate
Military Works
6th Division
Palamcottah Cantonment
Tinnevelly
Barracks

Constructing 4 Officers' Quarters & the Guard House at Fort in Barrack Square, 1 Sergeants' Quarters & Family Quarters for Artillery at Palamcottah

P. W. 4906/71.

Cl. 49 66

Govt. of {1871} Madras.

PUBLIC WORKS.

To The Superintending Engineer
6th Division

Dated

Recd. Encl. 4

G. O., 6th November 1871, No. 2803.

Nos. 88 & 89

Military Works in the Nilgiri.

Monopoly 5th Estimates amounting to Rs: 2068 for certain minor Works in the Nilgiri Monopoly 5th, sanctioned with Remarks.
