M.R.O. 1—77,006—8-6-37.

(1) Number of pages 16

(2) Date of repair

(3) Initials of the Referencer

MADRAS RECORD OFFICE.

Government of Madras.

PUBLIC WORKS DEPARTMENT.

G.O. No. 3100-01 Press / Mis.

139-144.

Dated 8-12-1891.

Not to be folded or roughly handled

No. 139. Read the following letter from the Acting Consulting Engineer for Railways, to the Secretary to Government, Public Works Department, dated Madras, 20th November 1871, No. 505 :—

I HAVE the honour to forward, for submission to the Government of India, the report of progress made in the construction of the Great Southern of India Railway for the quarter ended 30th September 1871.

2. As the extension works were not yet commenced, there is no separate report as called for by the Government of India in their letter of 23rd June 1871.

G. O., No. 1,773, dated 5th July 1871.

GREAT SOUTHERN OF INDIA RAILWAY.

General Progress Report of work in Erecting and Building Locomotive and Rolling Stock for quarter ending 30th September 1871.

—	Number sanctioned.	Number erected up to 30th June 1871.	Number erected during current year. During quarter.	Number erected during current year. To end of quarter.	Building or under erection at end of quarter.	Arrived at Shops during quarter.	Arrived at Port during quarter.	Balance to arrive in Port.
Locomotive Engines and Tenders	21	20	...	1	1	...	...	...
Composite Carriages ...	7	6	1	2	...	...	...	...
Second-class do. ...	2	2	...	...	...	...	...	...
Third-class do. ...	34	34	...	...	...	...	...	...
Passengers Brake Vans.	8	7	...	1	1	...	...	...
Horse Boxes	3	3	...	...	...	...	...	...
Carriage Trucks ...	1	1	...	...	...	...	...	...
Goods Brake Vans ...	4	4	...	...	...	...	...	...
Covered Goods Waggons.	166	144	4	23	18	...	...	...
Ballast Waggons ...	50	50	...	...	...	...	...	...
Open Goods do. ...	50	50	...	...	...	...	...	...
Timber Trucks	4	4	...	...	...	...	...	...
Gun-powder Vans ...	1	...	...	...	1	...	...	...
Salt Trucks	25	25	...	...	...	...	...	...
High Sided Open Trucks.	50	50	...	...	...	...	...	...
Sets of Iron work (Carriages)	Iron works drawn from General Stores in complete sets					...	...	...
Do. do. (Waggons)...								

NEGAPATAM,
14*th November* 1871.

(Signed) E. G. SHEWARD,
Locomotive and Carriage Superintendent.
(Signed) W. S. BETTS,
Agent.

Proceedings of the Madras Government, Public Works Department, 8th December 1871.

A.

OPEN LINE.

Progress Report for quarter ending 30th September 1871.

Reference to heads of Estimates.	Details.	Total Estimate. Indian Expenditure.	Total Estimate. Value of English Stores.	Actual Indian (Cash) Expenditure. During quarter.
				Rs. A. P.
I.	PRELIMINARY EXPENSES	...	...	.....
II.	LAND	...	...	.....
III.	CONSTRUCTION OF LINE	...	...	.....
	Earthwork	...	..	.....
	Small bridges	...	...	.....
	Large do.	...	...	.....
	Fencing	...	...	.....
	Other Items	...	...	.....
IV.	BALLAST AND PERMANENT-WAY	...	...	.....
	Ballast	...	...	.....
	Permanent-way	...	...	.....
V.	STATIONS AND BUILDINGS	...	...	.....
	Platform	...	...	147 8 0
	Passengers' buildings	...	...	.....
	Goods sheds	...	...	.....
	Watering arrangements	...	...	.....
	Staff Quarters	...	...	.....
	Engine Sheds, etc., Shops	...	...	.....
	Other Items	...	...	5 8 0
VI.	TELEGRAPH	...	...	142 0 0
VII.	PLANT	...	...	.....
VIII.	ROLLING STOCK	...	...	82 15 9
IX.	MAINTENANCE	...	...	692 8 5
X.	ESTABLISHMENT	...	...	.....
XI.	CONTINGENCIES...	...	...	13,379 10 4
		...	...	80 0 7

SOUTHERN EXTENSION.

Progress Report for quarter ending 30th September 1871.

Reference to heads of Estimates.	Details.	Total Estimate. Indian Expenditure.	Total Estimate. Value of English Stores.	Actual Indian (Cash) Expenditure. During quarter.
				Rs. A. P.
I.	PRELIMINARY EXPENSES	...	...	27,929 5 0
II.	LAND	...	...	.....
III.	CONSTRUCTION OF LINE	...	...	.....
	Earthwork	...	...	.....
	Small bridges	...	...	.....
	Large do.	...	...	.....
	Fencing	...	...	.....
	Other Items	...	...	.....
IV.	BALLAST AND PERMANENT-WAY	...	...	.....
	Ballast	...	...	.....
	Permanent-way	...	...	.....

Proceedings of the Madras Government, Public Works Department, 8th December 1871.

Progress Report for quarter ending 30th September 1871.—(Concluded.)

Reference to heads of Estimates.	Details.	Total Estimate. Indian Expenditure.	Total Estimate. Value of English Stores.	Actual Indian (Cash) Expenditure. During quarter.
V.	STATIONS AND BUILDINGS	...	...	.....
	Platform	...	...	.....
	Passengers' buildings	...	...	.....
	Goods Sheds	...	...	.....
	Watering arrangements	...	...	.....
	Staff Quarters	...	...	.....
	Engine Sheds, etc., Shops	...	...	.....
	Other Items	...	...	.....
VI.	TELEGRAPH	...	...	.....
VII.	PLANT	...	...	.....
VIII.	ROLLING STOCK...	...	...	.....
IX.	MAINTENANCE	...	...	.....
X.	ESTABLISHMENT	...	...	.....
XI.	CONTINGENCIES...	...	...	.....

(Signed) J. SMITH,
Chief Auditor.

(Signed) W. S. BETTS,
Agent and Traffic Manager.

(Signed) S. M. JOHNSON,
Assistant Controller.

NEGAPATAM,
27th October 1871.

No. 140. ORDER THEREON, 8th December 1871, No. 3,100.

RAILWAY, No. 25.

ORDERED that these papers be forwarded to the Government of India.

(True Extract.)

(Signed) J. CARPENDALE, Colonel, R.E.,
Secretary to Government.

No. 141. DOCKET No. 3,101, dated 8th December 1871.

COPY of the above forwarded to the Government of India.

(True Extract.)

Colonel, R.E.,
Secretary to Government.

Exd. E. C. Shunker.

CONSULTING ENGINEER'S OFFICE.

Railway Department.

No. 505

From Major A. L. Pendergast R.E.
C.R.E., Consulting Engineer for Railways,

To Colonel J. Basevi R.E.
Secretary to Government,
Public Works Department,
Fort Saint George.

Sir,

I have the honour to forward for submission to the Government of India, the Report of progress made in the construction of the Great Southern of India Railway for the quarter ended 30th September 1851.

2 As the extension works were not yet commenced, there is no separate Report, as called for by the Government of India in their letter

G.G. No. 1773
25 July 1851.

of

of 23 June 1891.

Madras 20 Nov 1891

Adam Che Seemanthaler,

Your Most Obedient

Humble Servant

Majesties

Agt Mens: Engr: Sur Ag

Form No. 233.)

GREAT SOUTHERN OF INDIA RAILWAY.

General Progress Report of work in Erecting and Building Locomotive and Rolling Stock for quarter ending 30th September 1871

	Number Sanctioned.	Number erected up to 31st Dec. 1870	Number erected during current year: During quarter.	Number erected during current year: To end of quarter.	Building or under erection at end of quarter.	Arrived at Shops during quarter.	Arrived at Port during quarter.	Balance to arrive in Port.	Remarks.
Locomotive Engines and Tenders	21	20	1	1	1				
Composite Carriages	1	1	1	2	"				
2nd Class do.	2	2	"	"	"				
3rd do. do.	34	34	"	"	"				
Passengers Brake Vans...	8	7	"	1	1				
Horse Boxes	3	3	"	"	"				
Carriage Trucks	1	1	"	"	"				
Goods Brake Vans	4	4	"	"	"				
Covered Goods Waggons	166	142	14	23	18				
Ballast Waggons	51	50	"	1	"				
Open Goods do.	50	50	"	1	"				
Timber Trucks	4	4	"	"	"				
Gunpowder Vans	1	"	"	"	1				
Salt Trucks	25	25	"	"	"				
High Sided Open Trucks	50	50	"	"	1				
Sets of Iron work (Carriages)	Iron work delivered from General Stores in Negapatam					None			
Do. (Waggons)									

Loco. and Car. Supt's. Office,
Negapatam 4th Oct. 1871.

William Bell.
Agent

Edgd/ Chas. P. Sherwood
Loco. and Car. Supt.

Great Southern of India Railway

Open Line — Progress Report for the quarter ending 30th September 1871

Reference to heads of Estimate	Details	Total Estimate: Indian expenditure	Total Estimate: £ Value of Compensations	Actual Indian (Cash) expenditure: During Quarter		
I	Preliminary Expenses			"	"	"
II	Land			"	"	"
III	Construction of Line			"	"	"
	Earthworks					
	Small Bridges					
	Large do					
	Fencing					
	Other Items					
IV	Ballast and Permanent Way			"	"	"
	Ballast					
	Permanent Way					
V	Stations and Buildings			1427	8	"
	Platforms					
	Passengers' Buildings					
	Goods Sheds					
	Weaderma Arrangements					
	Cattle Sheds					
	Engine Sheds & Shops			5	8	"
	Other Items			142	"	"
VI	Telegraphs			"	"	"
VII	Plant			82	15	9
VIII	Rolling Stock			692	8	6
IX	Maintenance			"	"	"
X	Establishment			13379	10	4
XI	Contingencies			86	"	7

James Smith
Chief Auditor

Alexander Betts
Agent and Traffic Manager

Negapatam
Chief Auditors Office
5th October 71
P. T.

Wm. Johnson.
Assistant Controller

A.

Great Southern of India Railway

Southern Extension — Progress Report for quarter ending 30th September 1871

References to Headings in Estimate	Details	Estimate: Indian Expenditure	Estimate: Value of English Stores	Actual Cost (Cash Disbursements): Current Quarter
I	Preliminary Expenses			27929 0 0
II	Land			" " "
III	Construction of Line			" " "
	Earthworks			
	Small Bridges			
	Large do			
	Tunnels			
	Other Items			
IV	Ballast and Permanent Way			" " "
	Ballast			
	Permanent Way			
V	Stations and Buildings			" " "
	Platforms			
	Passengers Buildings			
	Do.			
	Watering Arrangements			
	Staff Quarters			
	Engine Sheds & Shops			
	Other Items			
VI	Telegraph			" " "
VII	Plant			" " "
VIII	Rolling Stock			" " "
IX	Maintenance			" " "
X	Establishment			" " "
XI	Contingencies			" " "


James Smith
Chief Auditor

Agent and Traffic Manager

Negapatam
Chief Auditors office
24th October 71
Comptd

W. Thomson.
Assistant Controller

P.P. 557/71

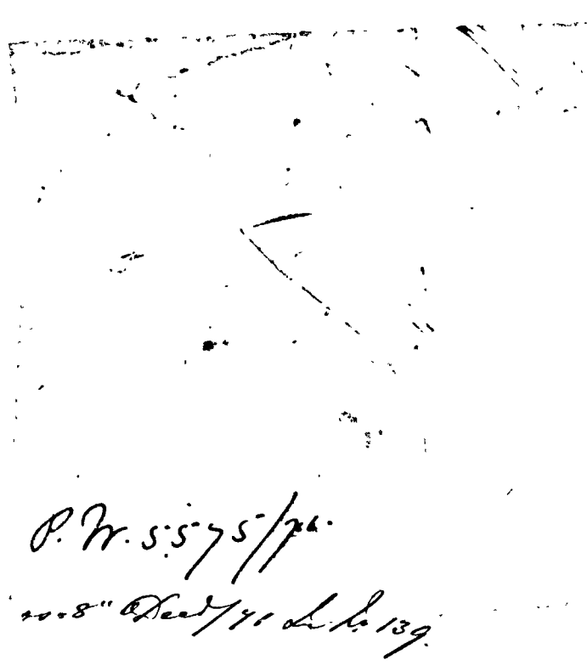

P. W. S. S. 75/76.
no. 8" Deed 41 Lib. 139

Public Works ~~Public~~ 1871 Department.

No. 85-5575

From

The Consulting Engineer
for Railways,

To

The Secretary to Government,
P. W. Department,
Fort St. George.

Dated 20th November 1871.
Received 23rd November 1871.

No. 505

Encl: 3 N
Nos 3100-3101-8th Nov 71.

Forwarding the report of progress made in the construction of the G.S of I. Ry for the quarter ended 30th September 1871

Madras 20th November 1871.

Sir,

I have the honor to forward herewith, for the information of Government, the report of progress made in the construction of the Great Southern of India Railway during the quarter ended 30th September 1871.

2. I also forward herewith, for the information of Government, a Return of the Rolling Stock of the Railway on the 30th September 1871.

3. I have the honor to be,
Sir,
Your most obedient servant,
[illegible]
Consulting Engineer for Railways.

Forwarding report of progress made in the construction of the S.I.R. for Quarter ended 30th Sept 71.

Rolling Stock as on 30th September 71.

To the Govt of India
Pub. Wks Dept
Rlys

Copy of the above forwarded to the Govt of India
Pub. Wks Dept
Rlys

Nos 3100-3101 dt 8th December 71.

Copy of the above forwarded to the Govt of India
Pub. Wks Dept
Rlys

Nos 3100-3101 dt 8th December 71.

Returns of Rolling Stock as on 30th September 71 forwarded.

Nos 3100-3101 dt 8th December 71.

Copy of the above forwarded to the Govt of India
Pub. Wks Dept
Rlys

Nos 3100-3101 dt 8th December 71.

Nos 3100-3101 dt 8th December 71.

Nos 3100-3101 dt 8th December 71.

C/25575

Bolt of 1871 Stat. s.

PUBLIC WORKS.

Lieut Donnelly Corps
for Pittsburgh
&
The Secretary to the Govt
of India &c

Sir

I am directed by the Secretary of State for War to transmit to you, for the information of the Secretary to the Government of India in Public Works Department, the accompanying Copy of a Report from Captain Scott, R.E. dated 1st October 1871, No. 3100-3117.

Nos. 139-1214 1214

Respectfully. Passing orders
on the letter from Captain Scott
for the submitting Abstract
Estimate made in the
Corps Indian Office 4 Sept 1871
for Quarter ending
30 Sept 71.
