MRO 1—77,006—8 6-37.

(1) Number of pages_____

(2) Date of repair_____

(3) Initials of the Referencer_____

MADRAS RECORD OFFICE.

Government of Madras.

Public Works DEPARTMENT.

G.O. No. 3211-12 Press / Mis.

360-66

Dated 20-12-1871.

Not to be folded or roughly handled

Proceedings of the Madras Government, Public Works Department, 20th December 1871.

No. 364. Read the following letter from the Acting Consulting Engineer for Railways, to the Secretary to Government, Public Works Department, dated Madras, 8th December 1871, No. 540:—

I HAVE the honour to forward, for submission to the Government of India, the report of progress of the Carnatic Railway Company for the quarter ended 30th September 1871, with a brief report of the progress of the survey operations by the Chief Engineer

---

Extract from Report by Chief Engineer, dated 2nd December, as to progress of survey for quarter ending 30th September 1871

MR JAMES and his party had completed, at the end of September last, the field-work of his part of the survey, with the exception of a very short distance, to the town of old Cuddalore, had completed the boring of the Pannar river, and had commenced that of the Guddalum where it is proposed to cross them for the railway.

2 Mr Devonshire-Scott and his party were within 11 miles of Chingleput, having surveyed and finally staked out and levelled about 55 miles from the commencement, in addition to many miles of preliminary examination where alternative lines from the trial survey were thought advisable

3 Mr Whitlock and his party had advanced nearly to Godvancherry, a distance of 12 miles from Chingleput, which was the starting point The permission to proceed with the working survey for this length had only been received on the 19th of August, and although more work remains to be done than on the other portions, the progress of the work has, I think, been satisfactory

(True Extract)

(Signed) J T. FISHER,
Agent and Manager

General Progress Report of Carnatic Railway Company (Limited) for quarter ending 30th September 1871

References to heads of Estimate	Details	Total Estimate		Actual Indian Expenditure	
		Indian Expenditure	Value of English Stores.	During quarter	Total from commencement to end of quarter.
		RS	RS	RS A P	RS. A. P
1	Preliminary Expenses	1,64,991	...	24,555 2 3	*a* 1,36,760 11 6

	RS	A	P
a Cash	1,36,760	11	6
Stores	7,371	10	1
Home Expenditure	37,529	11	3
Total...	1,81,662	0	10

MADRAS,
28th November 1871.

(Signed) J T FISHER,
Agent and Manager.

(Signed) G R WALKER, Lieutenant, R E,
Offg Examiner of Railway Accounts.

Proceedings of the Madras Government, Public Works Department,
20th December 1871.

No. 365. ORDER THEREON, 20th December 1871, No 3,211.

RAILWAY, No. 58.

ORDERED that this report be forwarded to the Government of India

(True Extract)
(Signed) J. CARPENDALE, Colonel, R E,
Secretary to Government.

No. 366 DOCKET No. 3,212, dated 20th December 1871.

COPY of the above forwarded to the Government of India.

(True Extract)

Colonel, R E,
Secretary to Government.

Ed E. C. Shanker.

3

Extract from Report by Chief Engineer dated 2d December as to progress of Survey for Quarter ending 30th September 1871.

Mr James and his party had completed at the end of September last, the field work of his part of the Survey, with the exception of a very short distance, to the Town of old Cuddalore; had completed the Boring of the Pannar River and had commenced that of the Guddelum were it is proposed to cross them for the Railway.

Mr Devonshire Scott and his party were within 11 Miles of Chingleput, having surveyed and finally staked out and leveled about 55 miles from the commencement, in addition to many miles of preliminary examination where alternative lines from the trial survey were thought advisable.

Mr Whitlock and his party had advanced nearly to Godvancherry a distance of 12 miles from Chingleput which was the starting point. The permission to proceed with the working survey for this length had only been received on the 19th of August, and although more work remains to be done than on the other portions, the progress of the work has I think been satisfactory.

/Sd/ F. L. Dibdin.
Chief Engineer.

/True Extract/

Jos. T. Fisher
Agent Manager

5

General Progress Report of Carnatic Ry Co/Limited/ for Quarter ending 30th September 1871.

References to heads of estimate	Details	Total Estimate: Indian expenditure	Total Estimate: Value of English Stores	Actual Indian expenditure: during quarter	Actual Indian expenditure: Total from Commencement to end of quarter
1	Preliminary expences.	64.991 - -	- - -	24.555 2 3	a 136760 11 6

W. A. Thompson
Head Keeper

a Cash _____ 136.760 - 11.6
Stores _____ 7371 - 10 - 1
Home expenditure _____ 37529 - 11 - 3
181.662 - 0 - 10

Madras
28th November 1871

G. F. Walker Jr. R.E.
Offg. Govt. Carnatic Ry Accts.

Jos. T. Fisher
Agent & Manager

8 Dr. 15-874/71
Trans. 20 Rly Statistics

CONSULTING ENGINEER'S OFFICE

Railway Department.

No 546

From Major H. L. Pendergast R.E.

Offg: Consulting Engineer for Railways,

To Colonel C. J. Caldecott R.E.

Secretary to Government,

Public Works Department,

Fort Saint George.

Sir,

I have the honour to forward herewith, for submission to Government, the Report of progress of the Carnatic Railway Company for the quarter ended 30th September 1851, with a Sketch Report of the progress of the Company expenditure up the Abstract Compared.

I have the honour to be

Sir

Your most Obedient

Humble Servant


H. L. Pendergast Major R.E.

Offg: Consulting Engr for Rlys.

P.W. 587 4/11/51

Rec'd Dept. 4th Inst.



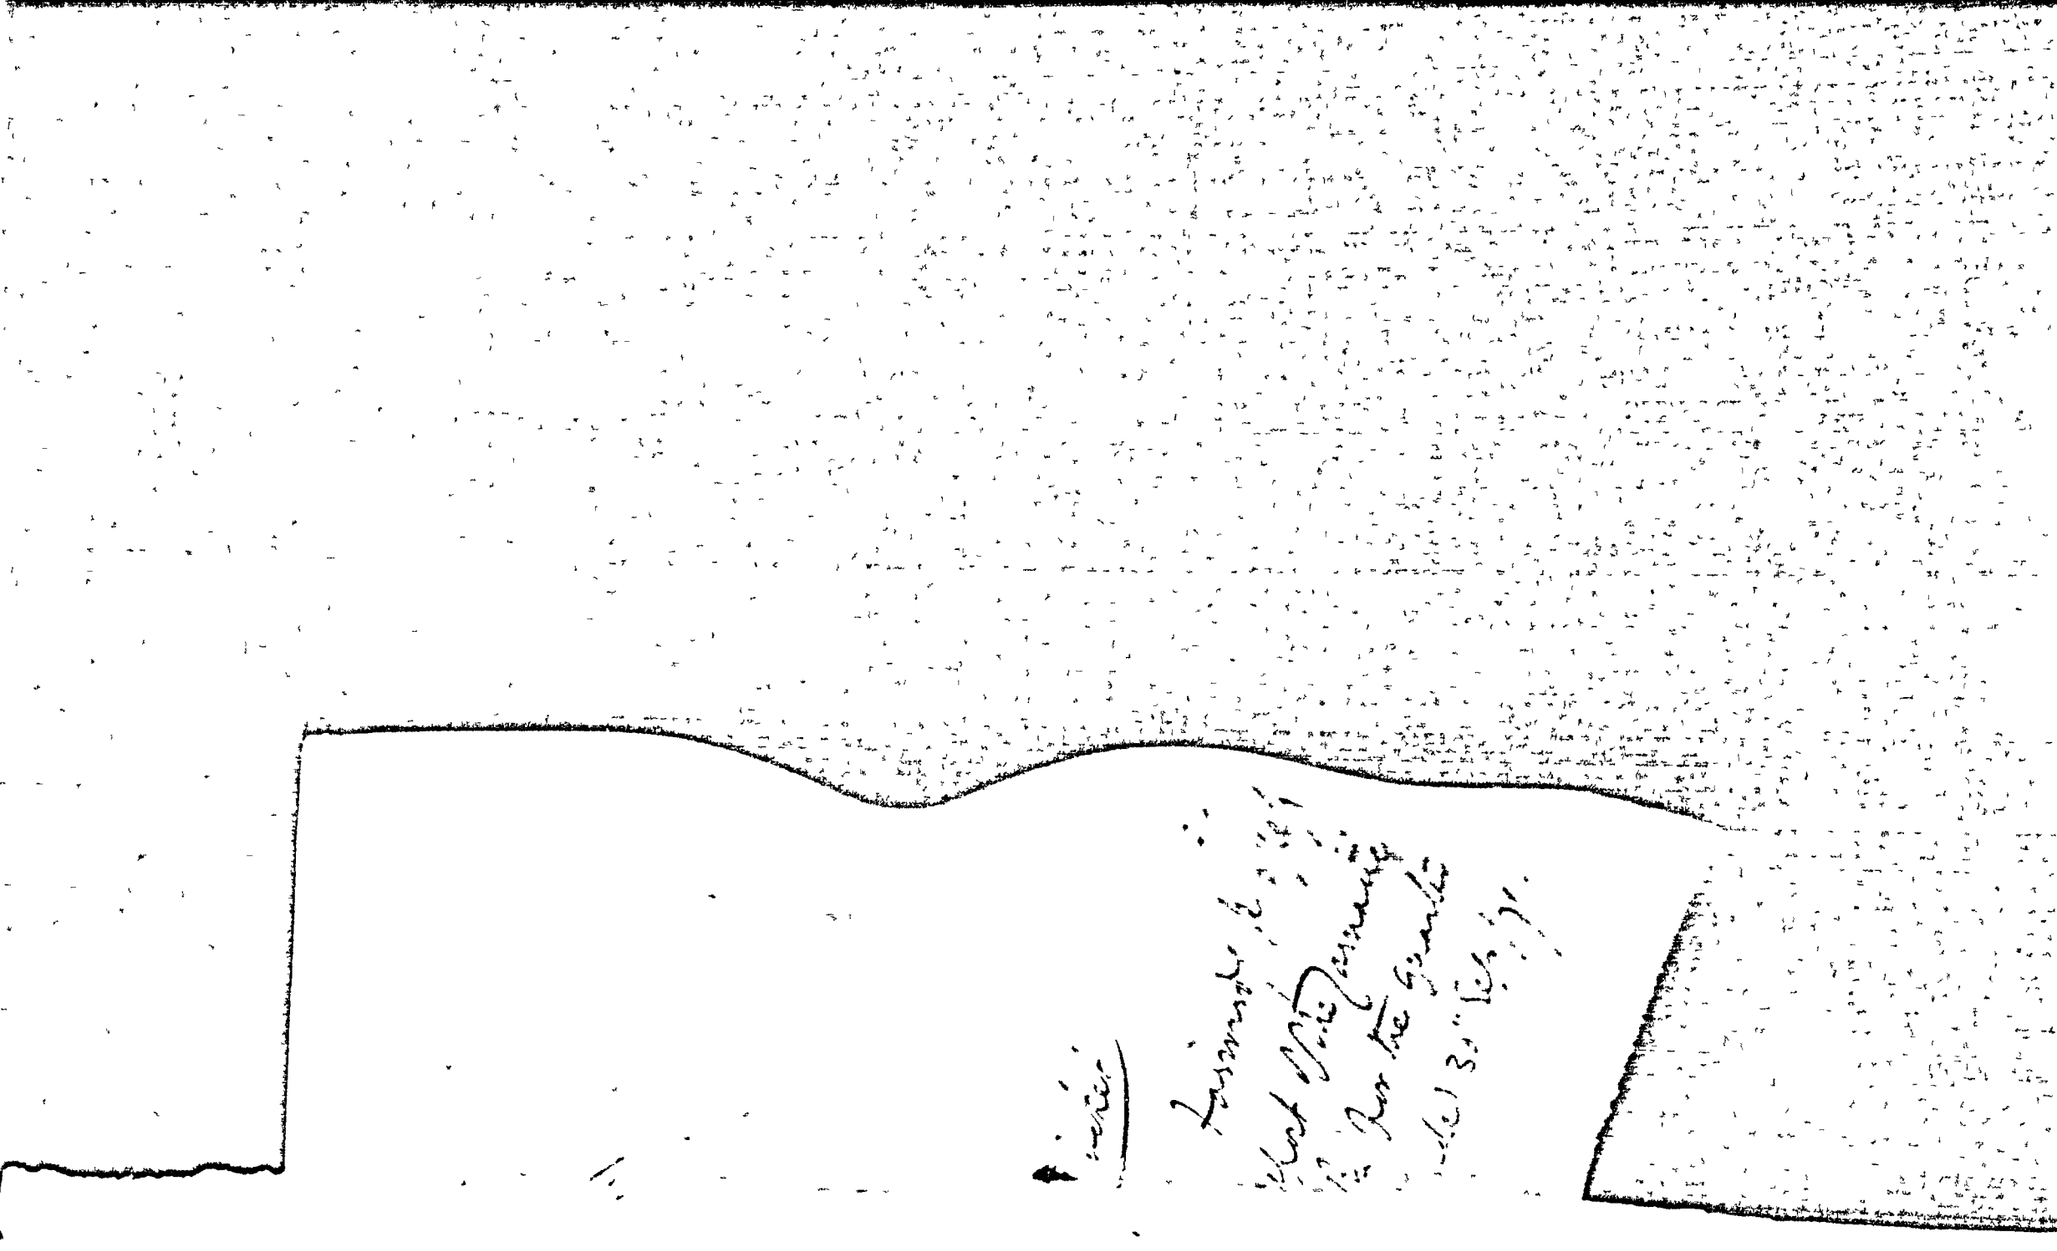

Railway Department.

No 5874

From

The Consulting Engineer
for Railways.

To

The Secretary to Government,
P W Department,
Fort St George

Dated 8th December 1871.
Received 11th December 1871.

No 5740

Recommending Plan &
Report of the East I/G Railway
The Greater Godavari Rte
&c &c &c

Dec 2 1871

No 3211-3212-20 Allowed
11th Dec 1871

No 3211

Ordered that this report be forwarded to the Govt of India.

To The Consulting Engineer for Railways

Docket No 3212 dt 20th Decr 71

Dated 22/12/71

Copy of the above forwarded to the Govt of India

Dated 22/12/71

Ch. 5874.

Cobl of 1857-8 Madras.

PUBLIC WORKS.

To Chief Consulting Engr for Railways and
The Secretary to the Govt of India
Dated 1st
Rec'd 20th Decr 32/1/3212
Order
Nos. 364-366 & 411
Forwarding Report
Noted the Letter from the Govt Secy for Pubc Works submitting Progress Report of the Carnatic Ry for the Quarter ended 30th Sept/71.
