4

(1) பக்கங்களின் எண்ணிக்கை 8.

(2) புதுக்கித் திருப்பிய நாள் March 90

(3) ஆதாரங்குறிப்பவர் கருக்கொப்பம்

தமிழ்நாடு ஆவணக் காப்பகம்.

தமிழ்நாடு அரசு

P.W.D. துறை

அரசாணை எண். 3159 W. அச்சகம்
மு. கோப்புத் தாள் எண். பலவகை

நாள் : 26.11.1890

மடிக்கவோ கண்டபடி கையாளவோ கூடாது

ஆவண. எச-1—18,000—15-8-87.

Chingleput Division Office.

No. 2828

Saint Thomas Mount

30th September 1890

3159/1

From

C.H.B. Burillon Esquire

Executive Engineer

Chingleput Division

To,

The Superintending Engineer


5th Circle.

Madras.

Sir,

With reference to your No. 2259 dated 11th August 1890 I have the honor to forward herewith for your information and early return, two measurement books regarding the Vayalur Salt Factory Flood Bank, from which it will be seen that the excess of 7246 c yards of earthwork in excess of the estimated quantity is not due as you seem to think to an incorrect estimate or to incorrect measurement.

2. From the diagram in the margin it will be seen, that pits had to be dug in the high ground opposite the Bank and earth had to be carried through the trench between the high ground and the salt pans. The foot paths were therefore essentially necessary and bunds had therefore to be construc-

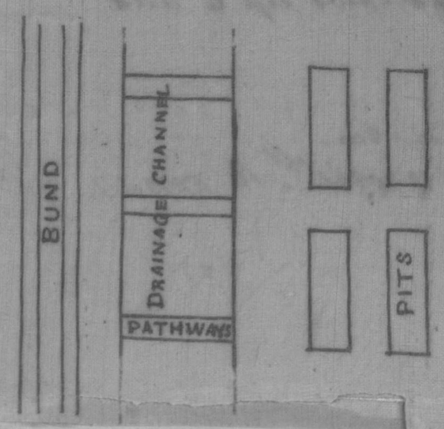

ted

Constructed for the purpose of carrying the excavated soil across the trench to the embankment. When preparing the estimate the necessity for these paths was not foreseen as however might have been done.

These small bunds had, after they had served their purpose, to be removed so that the trench might be open to receive drainage for which it is intended. This entailed extra expence.

Complete information, I beg to submit has already been given in the Comparative statement of differences and in the Calculation sheets I would beg to point out from these that the earthwork required for the Bank proper has been reduced from 1,052,284 cft to 9,63,481 cft in the revised estimate and that therefore the excess is due to what was required for pathways and also a ring bund which had to be constructed at the Northern end of the tank to keep out water

Five piece workers were employed on the work and they were paid as follows up to and for 31st August 1890.

(1) Earthwork including pathways &c.
12,20,861 cft. Rs. 5799-1-4

(2)

(2) Tamping lifting and sprinkling pear } Rs 5799-1-4 / 776-6-9
(3) Petty supervision &c. 147-3-0
3159 / 2 Rs. 6722-11-1

excluding a sum of Rs 346-15-1 withheld for them as security.

The above work was all check measured by the Sub Divisional Officer and myself. I think, I have given complete explanation on the several points, and I hope that the present revised estimate may now meet with your approval and sanction. The Original papers are herewith returned.

I have &c.

(Signed) C.H.B Burllon
Executive Engineer
Chengleput Division

W.H. Buetow
Colonel R.E
Superintending Engineer S. Circle

12th Nov. 1890.

SUPERINTENDING ENGINEER'S OFFICE,
V CIRCLE, MADRAS,
Chepâk, 8th November 1890.

No. 3720

3159/3

From Colonel W. H. Burton R.E.
SUPERINTENDING ENGINEER,
V CIRCLE,

To
THE Chief Engineer
P.W. Department.

SIR,

I have the honor to report that since the submission of the statement of requirements for incomplete repair of the Voyalur Salt Factory flood bunks in this office No 974 dated 29th May last, a revised estimate amounting to Rs 8,870 has been sanctioned by me for the same work. The necessity for the revision of the original Estimate of Rs 7416 is fully explained in the enclosed Copy of letter No 2828 dated 30th September last from the Executive Engineer Chingleput Division.

I request therefore that funds to the extent of Rs 3,277 may be sanctioned for the work instead of Rs 1,623 applied for in the statement.

I have the honor to be
Sir,
Your most obedient Servant
W. H. Burton Colonel R.E.
Superintending Engineer V Circle

Enclosure.
1 Copy of letter No 2828 dated 30 September 1890.

W Cdc 10828

No. 1986-37 dy 17-7-90

From

THE SUPERINTENDING ENGINEER,

V CIRCLE,

To

THE Chief Engineer
P. W. Deptt.

Dated 8
Recd. 11 } November 1890.

ENCLOSURES. 1

No. 3720.

Voyalur Salt-Factory.
flood banks.

Requests that funds
to the extent of Rs 3077
may be sanctioned for
the completion repairs to ——

No. 3159 dy 26 Nov 1890.

PUBLIC WORKS DEPARTMENT.

3159
4

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following

From the S. E. V Circle No 3720. dt 8th Nov 90

The allotment of Rs 1,623 applied for by the Subg Engineer V Circle in his No. 774, dated 29th May 1890, for repairs to the Salt Factory at Voyalur, having already been allotted by the Govt of India, that Govt will be requested to sanction the additional allotment of Rs 1,454 now required.

J.H.T. 23/11/90

* vide G. O. No. 3128 W dy 24 November 1890.
+ Estimate No. 1967

No. 3160 dy 26 Nov 1890

To
The Secy to the Govt of India
P. W. Department

Sir,

In forwarding
copy

S. E. V Circle
Ex: P. W. Accts

Home

Copy of the accompanying Proceedings of the Government No 3159 W. dated 26th Nov 1890. I am directed to request that an allotment of Rs* 1,454 be sanctioned for repairs to the salt factory bund at Vayalur in addition to the sum of Rs 1,623 allotted for the work by the Government of India in its letter No 283 ACW dated 10th November 1890

I have &c

* Rs 1,810 including Establt and Tools & Plant percentages.

5 Dept

No 3159 Govt dated 26 Nov 1890

Secretary
14.11.90

W

Sy...

Despatch note
to Govt No 3159 W dated 26-11-90
26/11/90

Cir

Mail Rec'd 14.XI.90
S.C. 27.11.

27/11.
