(1) Number of [illegible]

(2) Date of [illegible]

(3) Subject of the Reference

MADRAS RECORD OFFICE.

Government of Madras.

[illegible] DEPARTMENT.

G.O. No.	1473	Press Mis.
97-98		97-98
Dated	12-7-	1897.

5/6

Not to be folded or roughly handled

Government House.

No. 97. Read the following Proceedings of Government in the Public Works Department, dated 6th July 1875, No. 1929 :—

ABSTRACT.—Estimate of Rupees 4,500 for the construction of a wrought-iron cistern and the fitting up of new pipes, &c., for supplying water to the bath-rooms in Government House, Madras, sanctioned for immediate execution. The question of an allotment for the work remitted for consideration in the Financial Department.

No. 98. ORDER THEREON, 13th July 1875, No. 1473.

The attention of the Public Works Department will be drawn to G.O., No. 1010, dated 8th May 1875.


2. The work should be carried out without delay, the charge being met either from savings or transfers from other allotments later in the year.

(True Extract.)

Officiating Chief Secretary.

To the Public Works Department.
,, Accountant-General.

Ex'd. T. O'Connor.

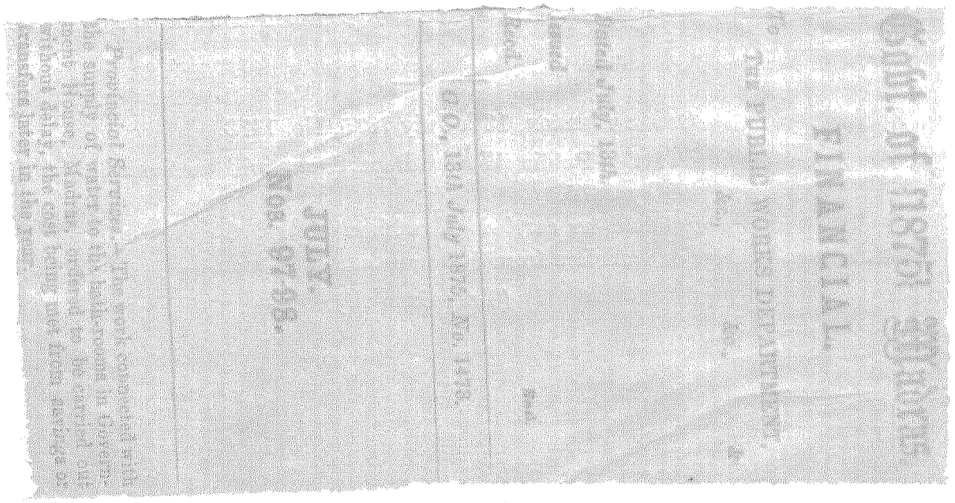

Proceedings of the Madras Government, Public Works Department,
6th July 1875.

Read the following papers :—

No. 233. Memorandum from Chief Engineer, dated 17th April 1875, No. 417.

No. 233-A. From Captain ROSS THOMPSON, R.E., District Engineer, Presidency, to Lieut.-Colonel J. MULLINS, R.E., Officiating Secretary to Government, Public Works Department, dated Fort St. George, 10th May 1875, No. 672 :—

WITH reference to your Memorandum, No. 417, dated 17th April 1875, I have the honor to submit, for sanction of Government, a specification report, plan, and estimate, amounting to Rupees 4,500, for constructing a wrought iron cistern and fitting up new piping, &c., for supplying water to bath-rooms in Government House, Madras.

2. The estimate provides everything necessary. The rates are reasonable and sufficient, and no supplementary works will be hereafter required.

No. 28 OF 1875-76.

Detailed Estimate of the probable cost of constructing a Wrought Iron Cistern 18′ × 15′ × 3′ 6″ *and fitting up new piping for use in the Government House—Vide District Engineer's No.* 6,914, *dated* 30*th March* 1875.

No.	Description of Work.	Rate.	Per	Amount.	Total.
		RS. A. P.		RS. A. P.	RS. A. P.
10,081	lbs. iron work for cistern ...	0 3 0	lbs.	1,890 3 0	
1,500	„ rivets	0 6 0	„	562 8 0	
82½	Cubic feet teakwood	4 0 0	C. ft.	330 0 0	
	Fitting up and rivetting charges at Government House	.....	...	250 0 0	
10	Squares red lead paint, 1 coat ...	1 8 0	Sqr.	15 0 0	
7	„ white lead paint, 2 coats.	2 0 0	„	14 0 0	
5	„ do. 1 coat...	1 4 0	„	6 4 0	
5	Tar painting, 1 coat	1 0 0	„	5 0 0	
	Cart-hire, &c.	.....	...	30 0 0	
	Contingencies	.....	...	155 1 0	
	Total of cistern ...	.....	...	.....	3,258 0 0
300	R. feet wrought iron pipes 2 inches	1 2 0	R. ft.	337 8 0	
400	R. feet wrought iron pipes 1½ inches	0 14 0	„	350 0 0	
3	Cast-iron stand pipes 6 inch diameter	18 6 0	Each.	55 2 0	
7	Brass cocks 1½ inch diameter ...	12 0 0	„	84 0 0	
4	Do. do. 1 inch „ ...	8 0 0	„	32 0 0	
	Cost of removing old piping and setting up the new piping, &c...	.....	...	200 0 0	
	Removing and re-setting the existing pump, &c., in another position as per plan	.....	...	100 0 0	
	Cart-hire to Government House.	.....	...	25 0 0	
	Contingencies	.....	...	58 6 0	
	Total of piping ...	.....	...	.....	1,242 0 0
	Grand Total ...	... ...	...	.....	4,500 0 0

CHEPAUK,
21*st April* 1875.

(Signed) J. N. GRAINGER,
Genl. Supt., Public Works Workshops and Stores.
(Signed) ROSS THOMPSON, Captain, R.E.,
District Engineer, Presidency.

Proceedings of the Madras Government, Public Works Department,
6th July 1875.

No. 234. From the District Engineer, Presidency, dated 14th June 1875, No. 1,225.

No. 235. ORDER THEREON, 6th July 1875, No. 1,929.

CIVIL WORKS, No. 17.

THE estimate, amounting to Rs. 4,500, is sanctioned for immediate execution. There being no funds at the disposal of the Public Works Department, the question of an allotment for the work is remitted for consideration in the Financial Department.

(True Extract.)

Major, R.E.,
Offg. Joint Secretary to Government.

To the District Engineer, Presidency.
„ Financial Department.
„ Controller of Public Works Accounts.

Exd. A. Grubert.
6 Spare Copies

Financial Department

Govt. of {1875} Madras.

PUBLIC WORKS.

To

THE DISTRICT ENGINEER,

PRESIDENCY,

&c., &c., &c.

Dated July 6th.

Issued

Read 10/7/75.

Read G.O.

G. O., 6th July 1875, No. 1,929.

JULY.

Nos. 233-235

Construction of a wrought iron cistern and the fitting up of new pipes, &c., for supplying water to the bath-rooms in Government House, Madras.—Estimate of Rupees 4,500 for the —, sanctioned for immediate execution. The question of an allotment for the work remitted for consideration in the Financial Department.

Read order.

Forwarded 13 July 1875 No 11,738

Re attention of the Public Works Department with his Memo No 1010-98 dated 8th May 1875.

Re work ordered should be carried out without delay, the charge of the payment of which from Savings, or transfer from other allotments duly in the year.

2

Re Public Works Department. Memorandum of proposal

Resp 21/7

10/7/75

12/7

Petn

Govt. of {1874} Madras.

Financial

G.O. 13 July 1875. No. 1473

Nos. 972 9

Provincial Services.

The work connected with the supply of water to the bath rooms in Government House, has been considered to be carried out without delay, the cost being met from Savings on Transfers later in the year.
