1. Number of pages 14
2. Date of repair. 4-9-2
3. Initials of Reference.

M.R.O. 1—39,000—16-10-29.

MADRAS RECORD OFFICE.

Government of Madras.

Public Works DEPARTMENT.

Cons. 24-11-57

G.O. No. 2154 Press Mis.

12728

Dated 23—11— 1957

Not to be folded or roughly handled

Fort Saint George, Public Works Consultation of 24th November 1857.

No. 127. Read the following Extract from the Minutes of Consultation in the Ecclesiastical Department, dated 10th November 1857, No. 382.

Read the following Extract Minutes Consultation Public Works Department.

Referring for consideration, an estimate submitted by the Chief Engineer, amounting to Rupees 470, for constructing a wall to enclose the Burial Ground at Itchapore in the Ganjam District. } (Here enter 28th October 1857, No. 2020.)

The Right Honorable the Governor in Council sanctions the estimate for the work proposed, amounting to Rupees (470) four hundred and seventy, to be entered in the Budget for 1858-59.

(True Extract.)

(Signed) T. PYCROFT,
Chief Secretary.

No. 128. ORDER THEREON, No. 2154; dated 23rd November 1857.

Ordered to be communicated to the Chief Engineer with reference to his report dated 19th October last, No. 4530.

(Signed) H. FORBES,
Acting Secretary to Government.

Ecclesiastical Department.

No. 382.

Extract from the Minutes of Consultation under date the 10*th November* 1857.

Read the following Extract Minutes Consultation, Ecclesiastical Department.

Referring, for consideration, an Estimate submitted by the Chief Engineer, amounting to Rupees 470, for constructing a wall to enclose the Burial Ground at Itchapore in the Ganjam District. (Here enter 28th October 1857, No. 2020.)

The Right Honorable the Governor in Council sanctions the Estimate for the Work proposed, amounting to Rupees (470) Four hundred and seventy, to be entered in the Budget for 1858-59.

(True Extract.)

Chief Secretary

To the Department of Public Works,
with 2 Enclosures.
" Venerable the Archdeacon,
with copy of Extract Minutes of Consultation recorded above.
" Accountant General.
" Civil Auditor.

Exd. J. A. Wilson.

Buildings ( ) (New Work)

Abstract of Estimate № of 185 /5

District Ganjam

Work Constructing a Compound wall of Brick in clay 5 feet high with 1 foot of coping in Brick in chunam to enclose the Burial Ground at Itchapoor

Quantities	Description of Work	Rates			Amount	Amount of each part
C. Yds.		Rs.	As.	P.	Rupees.	Rupees.
5516	Cft. Brick work in clay 76ft.	"	"	9	259	
710	Cyd. Brick work in chunam 76 by.	1	12	"	116	
5775	Sufft. Plastering in chunam 759ft.	1	8	"	87	
	2 Urns complete	"	"	"	3	
160	Cyd. Earth work for foundation 76yd.	"	1	"	10	
	Gate with Padlocks 18ea.	"	"	"	25	
	Sundries and Superintendance	"	"	"	40	
					Total company's Rupees	470

Central Office of P.W.
Fort Saint George.
19th October 1857.

W.H. Sadar Colonel
Chief Engineer D.P.W.

Quantities.	Description of Work	Rates.			Amount.	Amount of each part.
C. Yds.		Rs	As	P	Rupees	Rupees

Enclosure
In a Report

From
The Chief Engineer
D. F. H

To
The Secretary to Govt
D. F. H

Dated 19th Oct 57
Received 21st Oct 57

2257
D.O. No. 2257

No. 4530

Abstract Estimate for constructing a Compound wall of Brick in clay 5 feet high with 1 foot of coping in Brick in chunam to enclose the Burial Ground at Ittchapoor in the District of Ganjam.
Amounting to Cs. Rs. 470-0-0

£. 57.0.0
In No. 390.

129

Fe Gen. 19 Oct 57 No. 4530

EDS 21 Oct 57

Revised Plan and Section of a Wall to enclose the Burial ground at Ittchapoor.-

D.O. No. 2257

D.O. No. 2257/57


£. 57.0.0
In No. 390


Revised Plan and Section of a Wall

to enclose the Burial Ground

at


ITCHAPOOR

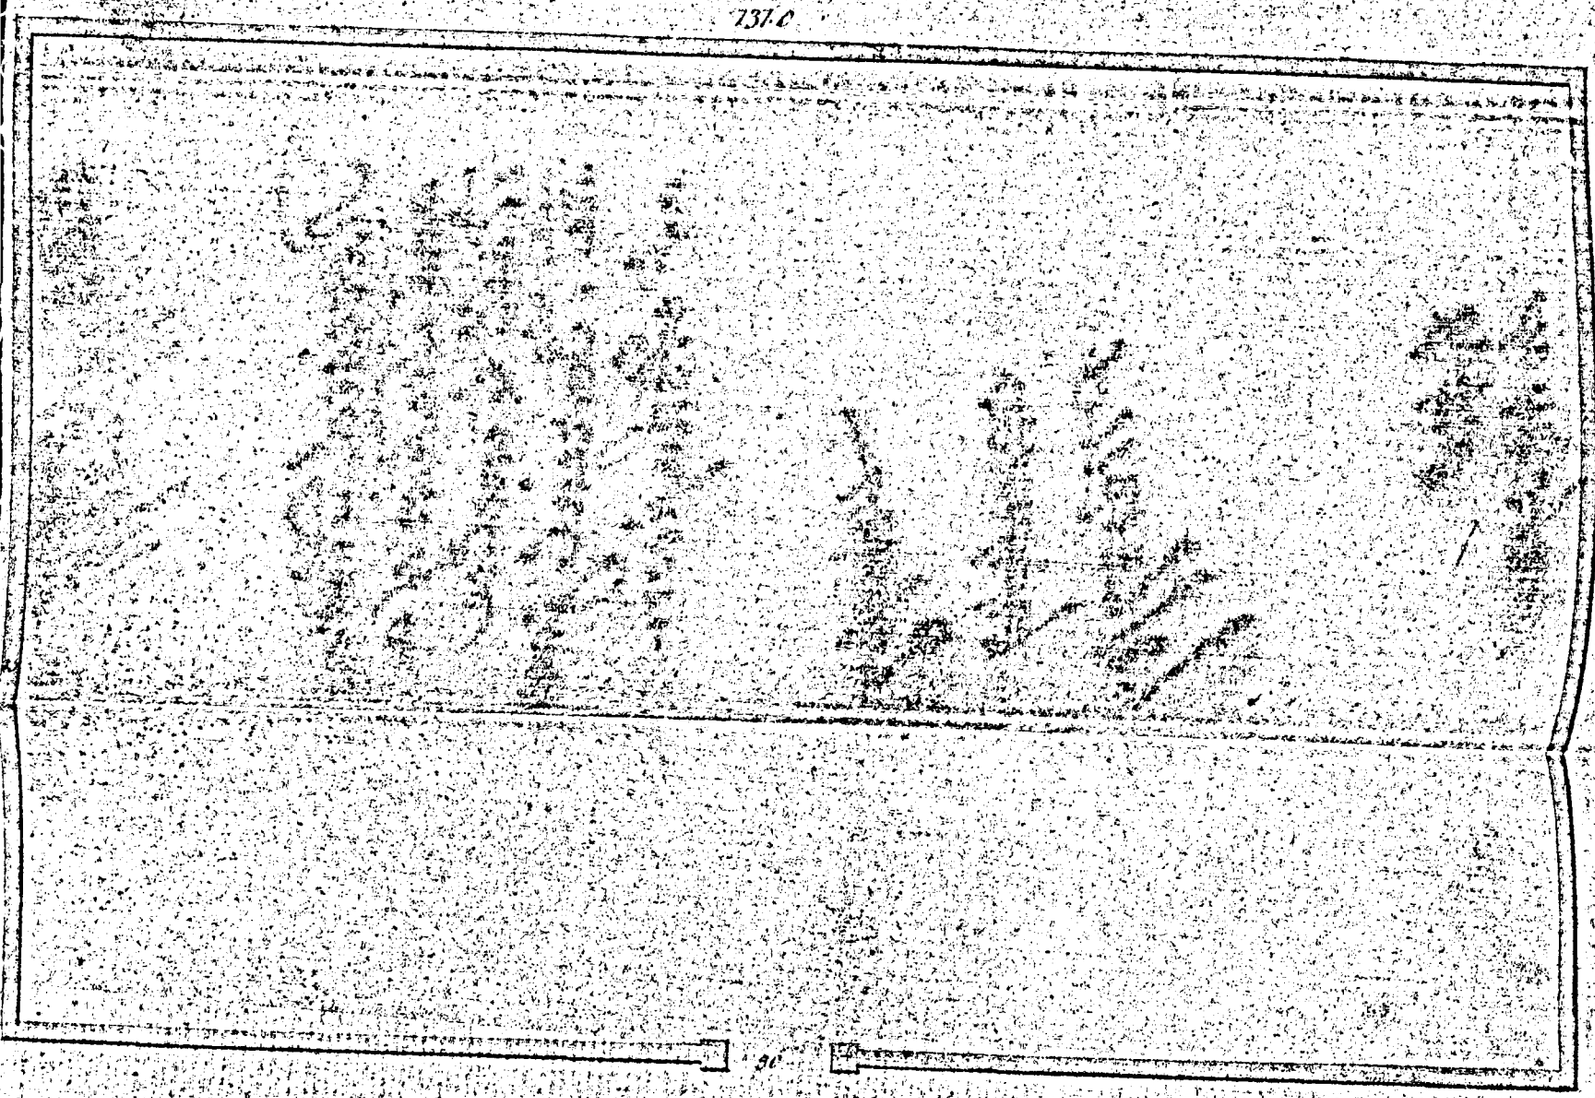

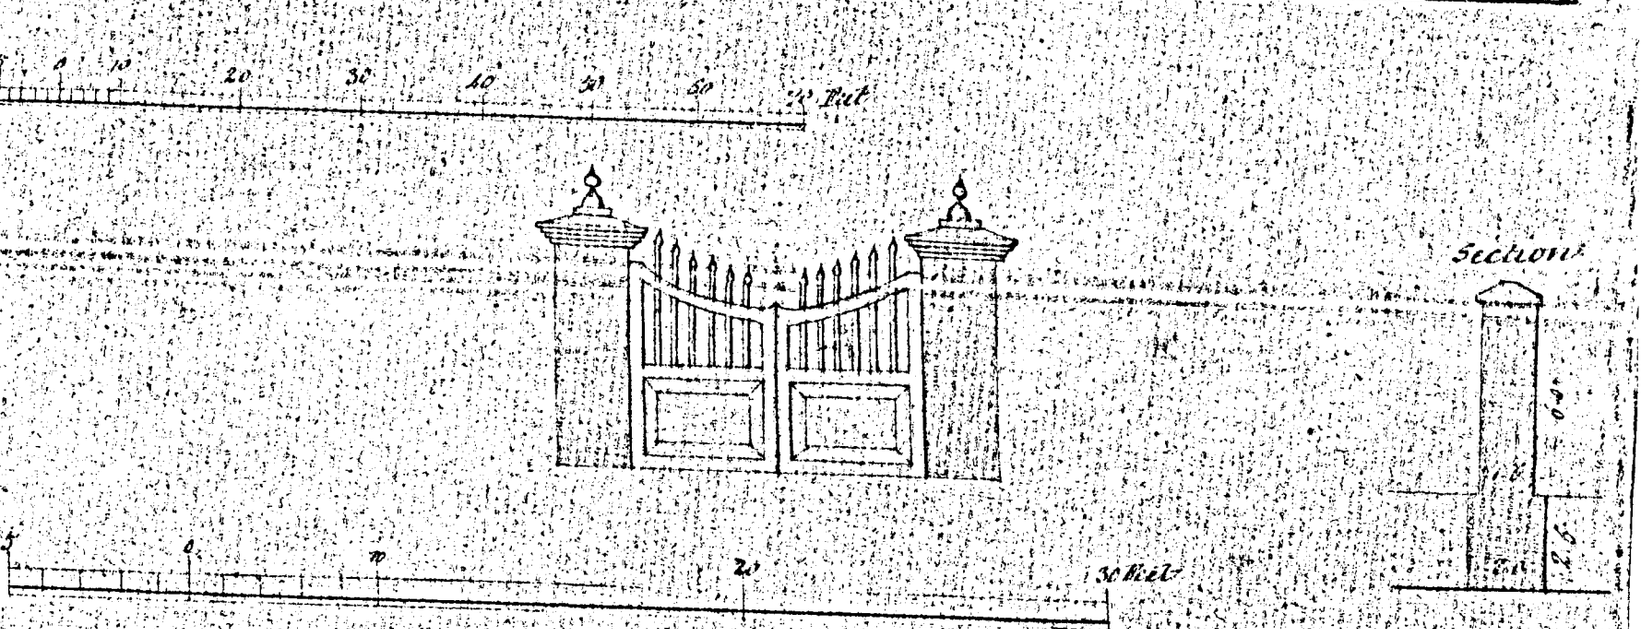

Fort St George
Sept^mber Engr^s Office
19^th September 1834

Alex^r Mottat Captain
Act^g Sup^t^g Engineer
Northern Circle NEIL

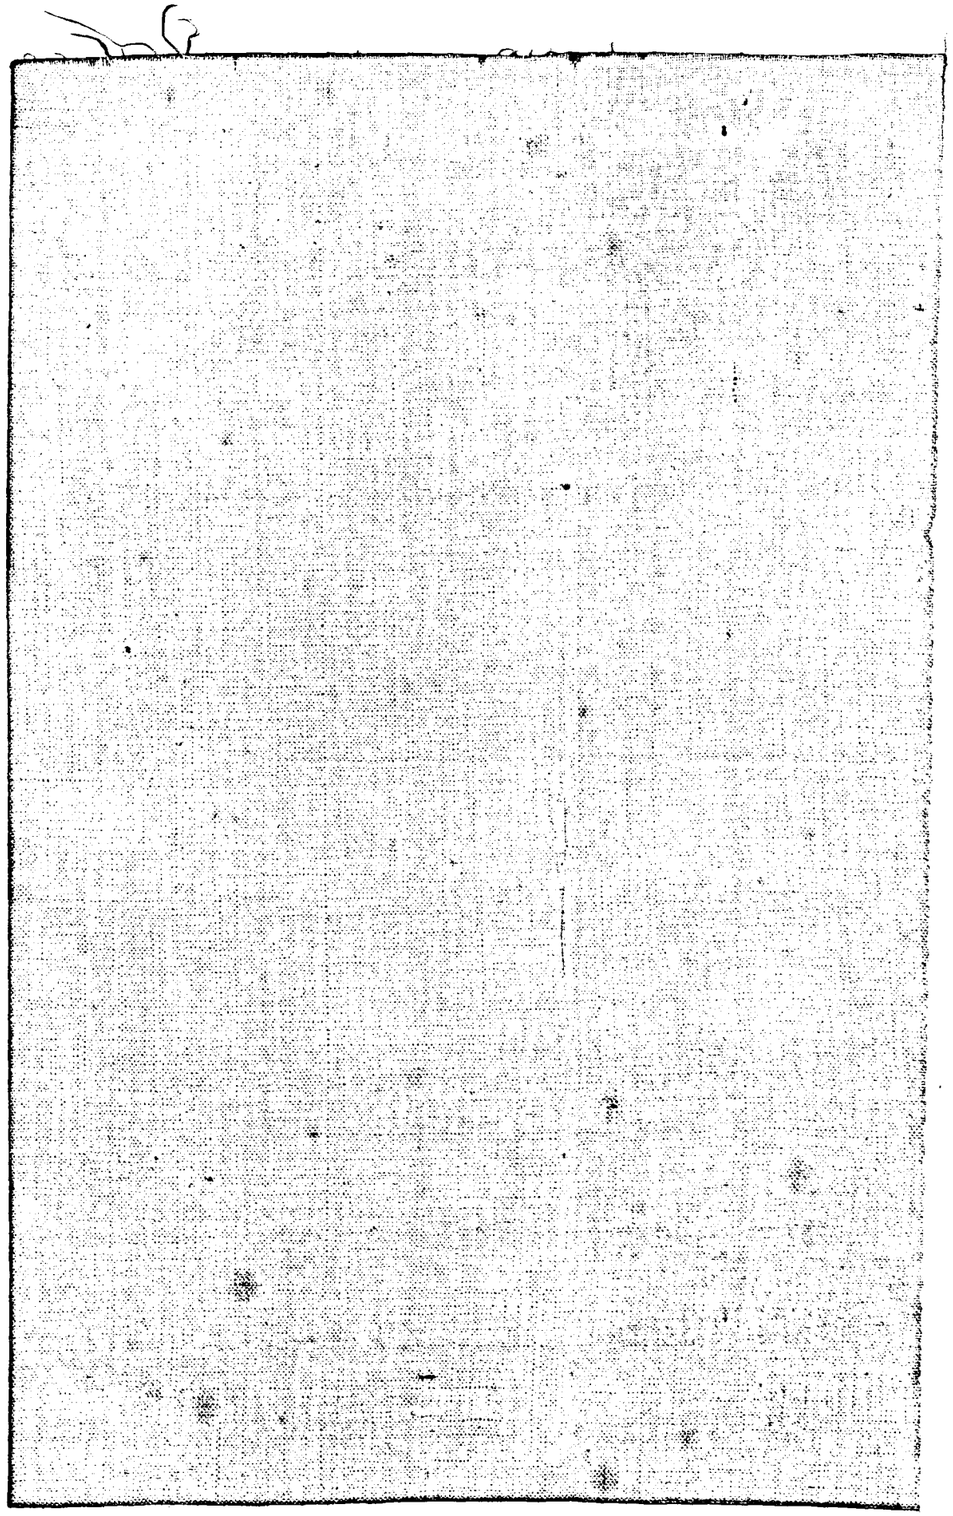

Comm: 29th Octr 57 No: 89.
90

Public Works 1857 No 1154
Dated Town 24th Novr
No 2257.

Submit Prim. Comm.
in the Subordinate Dept

Dated 16th December
Received 17th "

Encls: 2 Returned Encl
Plan
4-1-58.

Sanctg for entry
in the Budget of 1858/59
an Estimate of Rs 470
for the construction
of a wall to enclose
the Burial Ground
at Ichapore in
Ganjam District.

Mr 2/428

Mr Allen order
No 2154. 28 Novr

No 2154

Ordered to be com-
municated to the Chief Engi-
neer with reference to his
Report dated 19 October last
No 4330.

Fort St George
23d Novr 57

9 Copies to the Chief Engr Dept 24
