No. 6189

Gobt. of {1894} Madras.
PUBLIC WORKS.

Pro
5/9/94

Dated

Recd. Encl.

G.O., 3/9 1894 No. 2176W

Students Hostel
at Chepâk

[illegible] orders describing the area proposed to be made over for the directing the Consg: Archt: ~~[illegible]~~ to prepare the necessary plans ~~taking care to~~ allowing plenty of space for future extensions.

80/LX

4/9

J.C.C.
4/9

19—2,000—93.

4

1W/16 10/76

GOVERNMENT OF MADRAS.

PUBLIC WORKS DEPARTMENT.

Buildings and Roads.
Civil Works.

Read—the following paper :—

From H. IRWIN, Esq., C.I.E., Consulting Architect to the Government of Madras, to the Chief Engineer, Public Works Department, dated Chepâk, 18th August 1894, No. 1403.

With reference to G.O., No. 1735 W., dated 11th July 1894, I have the honour to forward a plan of the Chepâk ground showing the proposed site for the Victoria Students' Hostel. From G.O., No. 1280 W., dated 22nd May 1894, it would appear that the triangular spot cross hatched red in the enclosed plan is intended, but, judging from the accommodation required, I consider that the whole area up to the southern boundary wall and the road on the west side will be required.

2. Soliciting the orders of Government as to the extent of ground to be made over to the committee, I have, &c.

Order—dated 3rd September 1894, No. 2176 W., Public Works.

The area intended to be made over for the Students' Hostel is the whole of the space between the boundary wall, the canal and the road, and not merely the small triangle at the northern end of this space.

2. Plans should be prepared on this ground, care being taken to allow plenty of space for future extensions, what is not built over being used as a garden or for tennis courts, and the tank near the southern boundary being filled up if necessary.

(True Extract.)

Under Secy. to Govt., P.W.D.

To the Consulting Architect to Government.
,, Educational Department.
,, Honorary Secretaries, Victoria Students' Hostel Committee.

Exd. C. A. Munisawmy.
Spare Copies

BUILDINGS AND ROADS.
CIVIL WORKS.

Govt. of {1894} Madras.

PUBLIC WORKS.

Dated September, 3rd.

Recd. *Encl.*

G.O., 3rd Sept. 1894, No. 2176 W.

SEPTEMBER.

Students' Hostel at Chepak

Orders describing the area proposed to be made over for the — and directing the Consulting Architect to prepare the necessary plans allowing plenty of space for future extensions.

C. A.
1.

C. No. 6189

P. W. Department.

Read the following:—

Letter from the Consulting to Govt - Madras } H. E. No 1403 d/18 August 1894

FOR ORDERS.

I always understood that the portion of ground to be given for the Students' Hostel at Chepak was as described in Mr. Irwin's letter of Aug. 18. 1894 No. 1403 - and certainly not only the miserable little corner cross hatched red. The Con. Architect I think should be instructed to make designs for the Hostel on the whole of the ground he alludes to - wherever it appears to him to come in best, taking care to leave plenty of space in his plans for future extensions. What is not built on shd. be made into a garden, and there wd. be no objection to filling in the tank - Tennis courts too might be shown.

Cir.

225

W

CMM
22/8/94

The tank could be turned into an A1 swimming bath, I should say. ~~But that may be left to the management of the Hostel~~

JD
29/8/94

JG
31/8

Cm

43—500-6-3-94.

FOR ORDERS.

Site for the Students Hostel, Chepauk.

2176 W

G.O. No. 2176 W. dy 3rd September 1894.

E. 22/8

C. A. / 1. 500—20-1-94.

Office of the Consulting Architect to Govt.,
Chepauk, Madras,

No. 1403

18th August 1894.

From
Henry Irwin, Esq., C.I.E.,
Consulting Architect
to the Government of Madras,

To
The Chief Engineer
Public Works Department.

Sir,

1 Enclosures

With reference to G.O. No. 1735 W dated 11th July 1894, I have the honor to forward a plan of the Chepak ground shewing the proposed site for the Victoria Students Hostel. From G.O. No. 1280 W dated 22nd May 1894 it would appear that the triangular spot cross hatched red in the enclosed plan is intended, but judging from the accommodation required, I consider that the whole area up to the Southern boundary wall & the Road on the West side will be required.

2. Soliciting the orders of Government as to the extent of ground to be

made

No. 3.

CHEPAUK COMPOUND IN 1893

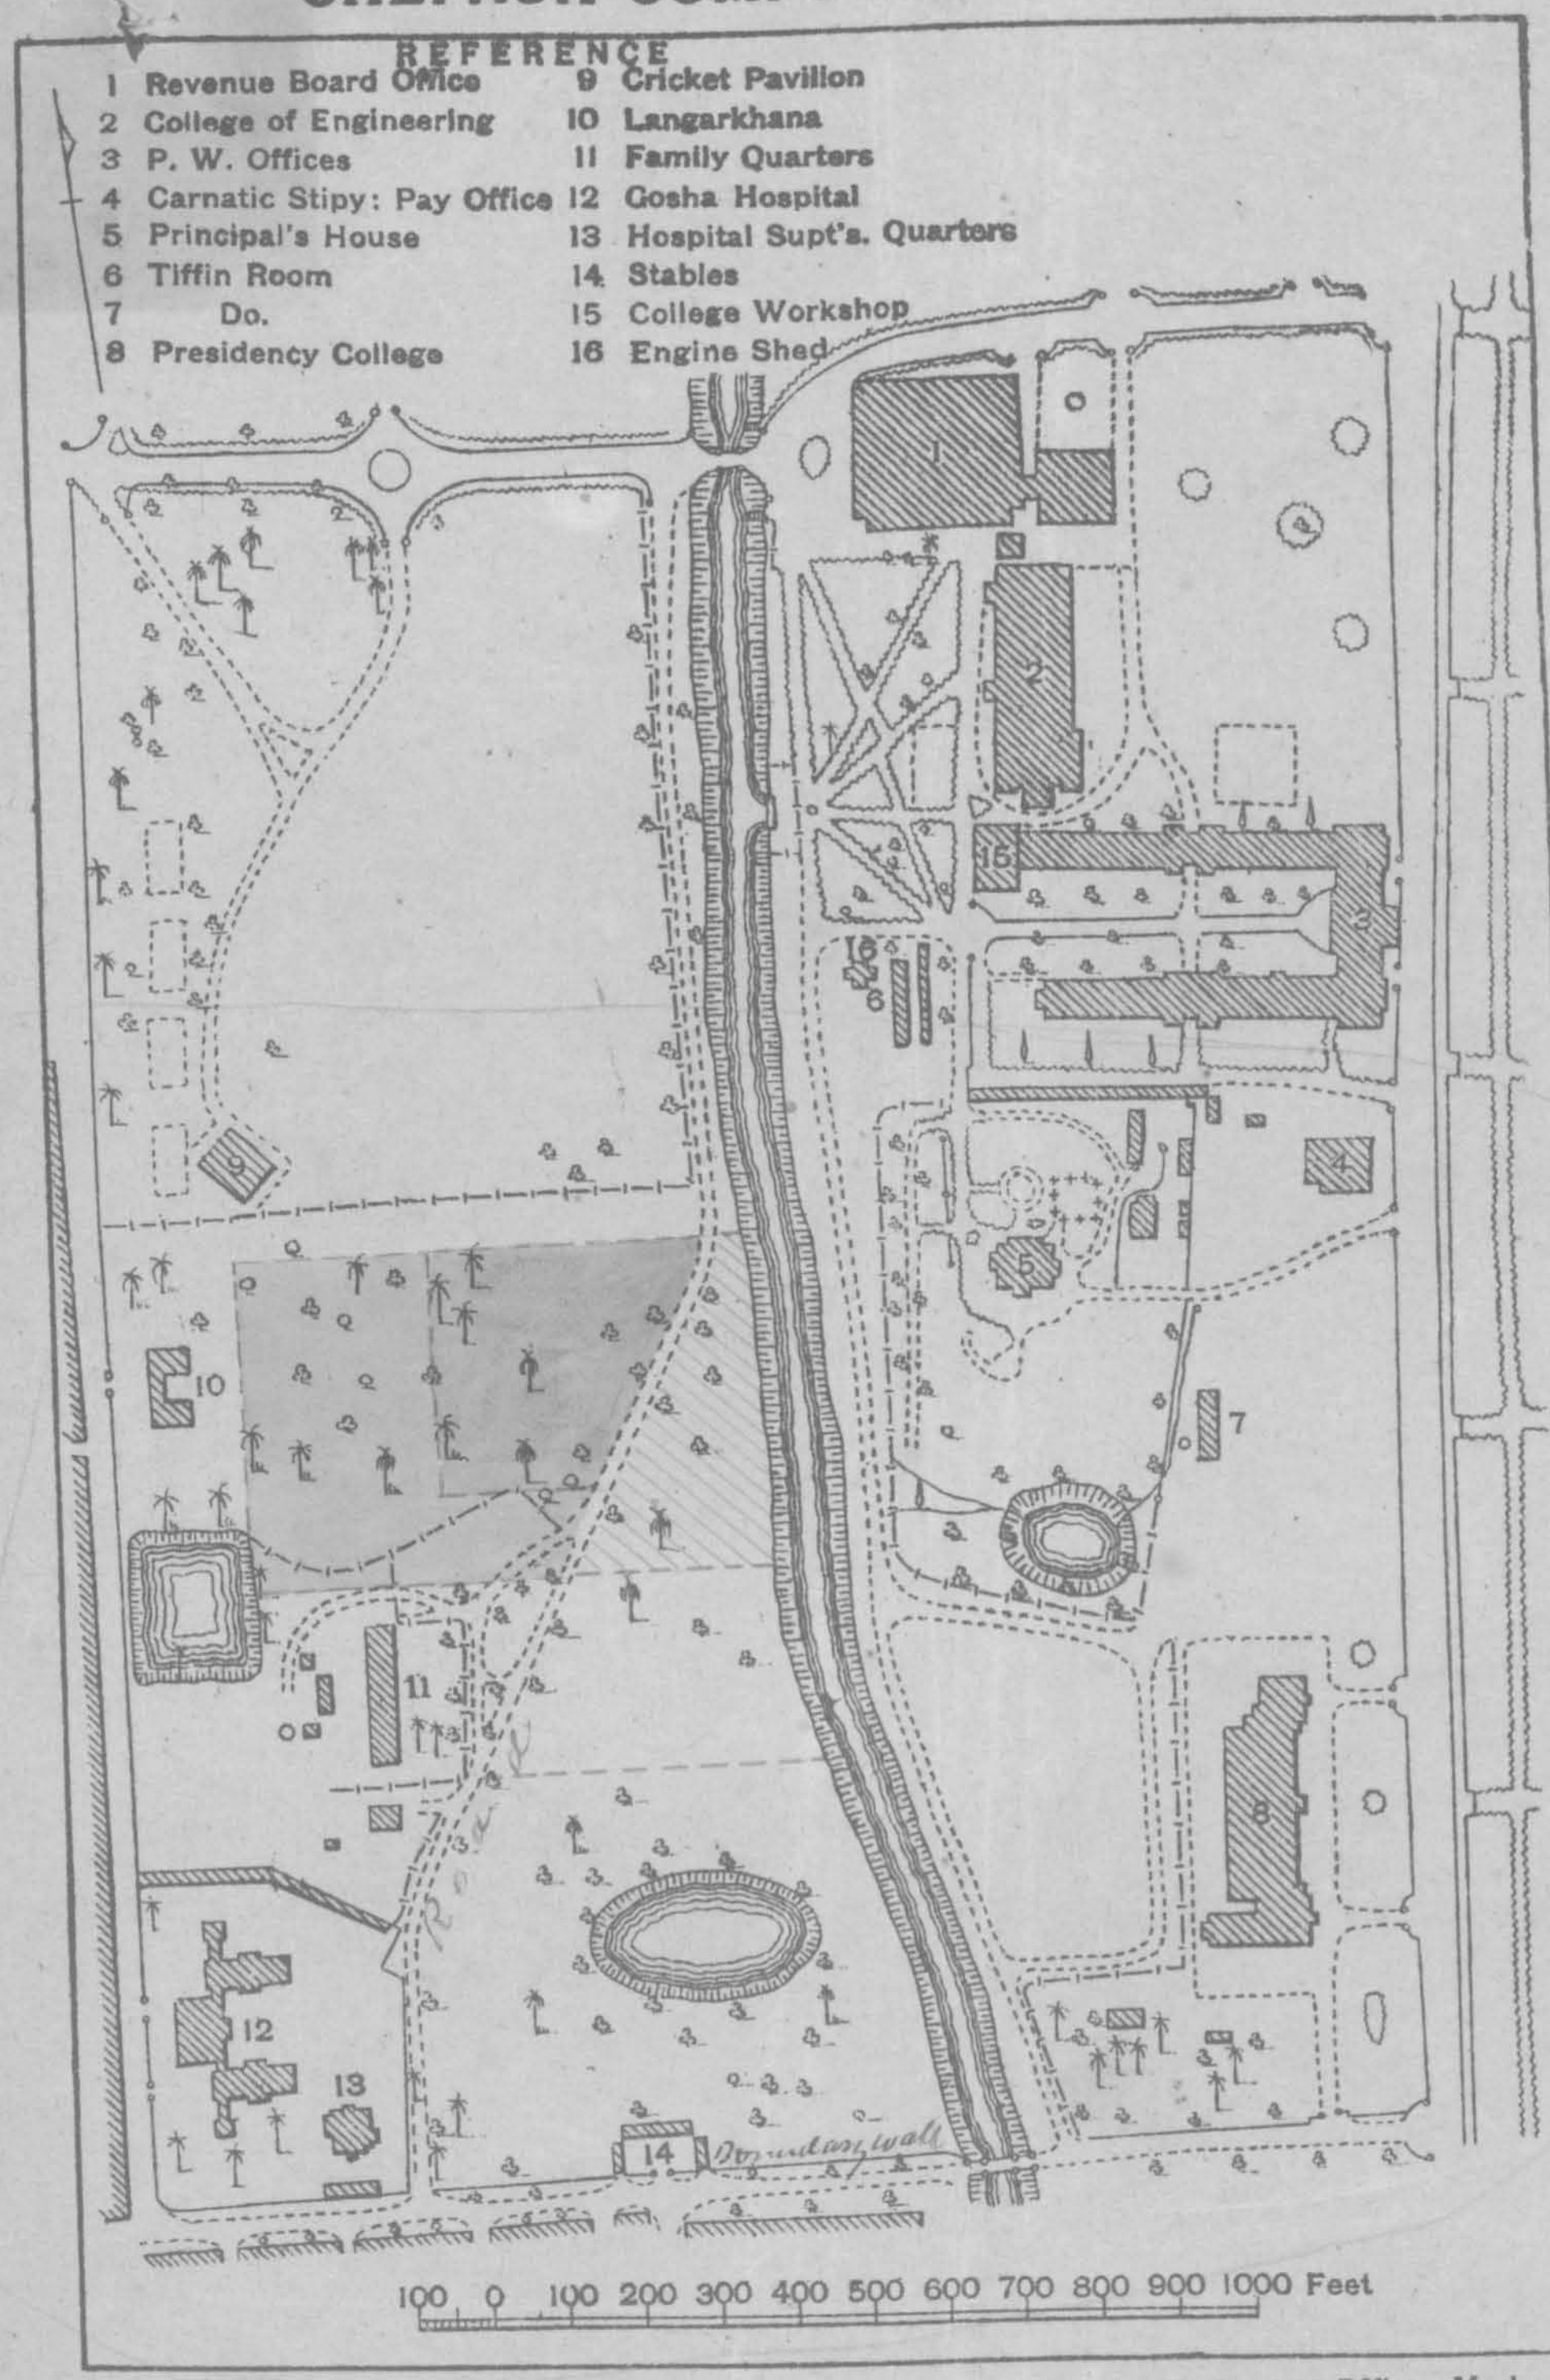

REFERENCE

1 Revenue Board Office	9 Cricket Pavilion
2 College of Engineering	10 Langarkhana
3 P. W. Offices	11 Family Quarters
4 Carnatic Stipy: Pay Office	12 Gosha Hospital
5 Principal's House	13 Hospital Supt's. Quarters
6 Tiffin Room	14 Stables
7 Do.	15 College Workshop
8 Presidency College	16 Engine Shed

Reg: No. 679: Copies 500

Photo-Zinco., Survey Office, Madras.
1893.

Present ground coloured .... blue.
Additional ground proposed by Consulting Architect -- red.
Further portion asked for by Principal, cross hatched red.

---

made over to the Committee

I have the honor to be
Sir
Your Most Obedient Servant
Henry Irwin
Consulting Architect
to Government.

No. 7. 6189

No. 1280 w d/ 22-5-94
1735 w d/ 11-7-94

Public Works Department.

From

The Consulting Architect
to the Government of Madras.

To

The Chief Engineer
P. W. D.

No. 1403

Dated 18th
Despatched
Received 20th
August 1894.

No. of Enclosures. 1

Subject.

Requesting the orders of Govt: for the extent of ground to be made over to the Victoria Students Hostel Committee, in the Chepak Park.

0.L.S. 298 R3/4

No. 2176 w d/ 3rd September 1894

PARTMEN

PROCEEDINGS OF THE MADRAS GOVERNMENT.

Read the following

Letter from the Consg: Architect —— (A. E. No. 1403 d/ 18.8.94)

3 Pun

W.J.
29/8/94

The area intended to be made over for the Students' Hostel is the whole of the space between the boundary wall, the canal and the road, and not merely the small triangle at the northern end of this space.

2. Plans should be prepared on this ground care being taken to allow plenty of space for future extensions,

(40—1,000—22-2-94.)

No. 1280 W dt -3-94

~~[illegible]~~ d/ 11-7-94

Public

what is not built
over being used as
a garden or for tennis
courts, and the tank near
the southern boundary,
being filled up if
necessary

J 28.8

~~[illegible]~~
and initialed on the Cover

N.S.
15 Sep 94

Site for the Students'
Hostel — Chepak

Copy 28/8

DESPATCHED
12 SEP. 94

Consg. Architect
Educational Dept.

Hony Secretaries,
Victoria Students Hostel
Comtee.

3rd September 1894, No. 2177 W., Public Works.

GOVERNMENT OF MADRAS.

PUBLIC WORKS DEPARTMENT.

Buildings and Roads.
Civil Works.

Read—the following papers :—

From the Presidency Port officer, Madras, dated 21st July 1894, No. 137/145 P.M.

G.O., dated 4th August 1894, R. No. 138, Marine.

Read—the following letter from the Presidency Port officer, Madras, dated 21st July 1894, No. 137/278 G. :—

Three estimates.	RS.
1. Constructing Port officer's office at Pámban, Madura district ...	1,800
2. Constructing two godowns for Port officer's office at Pámban, Madura district	2,020
3. Removing and reconstructing Deputy Telegraph Master's quarters with out-houses at Pámban, Madura district	1,380
Total ...	5,200

I have the honour to request that a sum of Rs. 5,200, together with the usual percentage for establishment and tools and plant, may be placed at the disposal of the Public Works Department for carrying out the works noted marginally.

2. The estimates for the same have been duly countersigned and forwarded to the Chief Engineer, Public Works Department.

Order—dated 4th August 1894, R. No. 138, Marine.

The receipt of the estimates from the Public Works Department will be awaited.

(True Extract.)

(Signed) J. F. PRICE,
Chief Secretary.

G.O., dated 20th August 1894, No. 337, Marine.

Read—endorsement of the Public Works Department, dated 14th August 1894, No. 771 D., on letter (through the Presidency Port officer) from the Superintending Engineer, VI Circle, dated 6th July 1894, No. 421.

Order—dated 20th August 1894, No. 337, Marine.

The estimates are approved and returned to the Public Works Department.

G.O., dated 4th August 1894, No. 138, will now be communicated to the Financial Department for early orders.

(True Extract.)

(Signed) J. F. PRICE,
Chief Secretary.

ORDER—dated 3rd September 1894, No. 2177 W., Public Works.

The following estimates are returned to the Superintending Engineer, VI Circle, for sanction:—

	RS.
Constructing an office for the Port officer at Pámban	1,800
Constructing two godowns for the Port office at Pámban	2,020
Reconstructing the Deputy Telegraph Master's quarters at Pámban...	1,380

2. The works will be carried out on funds, as shown below, being made available by the Financial Department:—

	RS.
Works	5,200
Establishment	1,196
Tools and plant	78
Total ...	6,474

(True Extract.)

Under Secy. to Govt., P.W.D.

To the Superintending Engineer, VI Circle, with enclosures.
„ Examiner, Public Works Accounts.
„ Marine Department.
„ Financial „

Exd. C. A. Munisawmy.
Spare Copies

BUILDINGS AND ROADS.
CIVIL WORKS.

Govt of {1894} Madras.

PUBLIC WORKS.

Dated September, 3rd.

Recd. *Encl.*

G.O., 3rd Sept. 1894, No. 2177 W.

SEPTEMBER.

Estimates

Certain — for the construction of an office, with two godowns, for the Port officer at Pámban, and the reconstruction of the Deputy Telegraph Master's quarters at that station, returned to the Superintending Engineer, VI Circle, for sanction and for execution when funds are made available by the Financial Department.

[G./53]
500—26-6-94.

Marine Department.

CHIEF SECRETARIAT, MADRAS.

Read — the following paper

G O dated 4' Aug. 1894, No 138 - Marine

2 Paper

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following paper :—

From the Presidency Port Officer, Madras, dated 21st July 1894, No $\frac{137}{278}$ G.:-

I have the honour to request that a sum of Rs (5,200) five thousand and two hundred, together with the usual per centage for establishment and tools and plant may be placed at the disposal of the Public Works Department for carrying out the works noted marginally.

2. The Estimates for the same have been duly countersigned× and forwarded to the Chief Engineer, Public Works Department.

3 Estimates

1. Constructing Port Officer's office at Pamban Madura District	Rs 1800
2. Do 2 Godowns for Do at Do	" 2020
3. Removing and reconstructing Deputy Telegraph Master's quarters without out houses at Do	" 1380
Total	Rs 5200

× Not received at Ootacamund

Order, dated 4th August 1894, R No 138

The receipt of the Estimates from the Public Works Department will be awaited.

(True Extract)

J Francis

Ag. Asst. Secretary
for Chief Secretary

Copy to,
the Public Works Department.

[G./53,]
500—23-11-93.

Department.

CHIEF SECRETARIAT, MADRAS.

PROCEEDINGS OF THE MADRAS GOVERNMENT.

Read the following paper:—

3

Govt. of {1894} Madras.

P. W. CURRENT No. 5921

No. 772 D dy 14-8-94

To

The Public Works Depts.

Remanded with reference to endt. No. 771 D dy 14th August 1894.

Regtd. 9. 8. 94

Recd 6/8/94

C 3/8/94

Proceedings, dated 4th Augt 1894.
R No. 138.

Subject.

Awaiting receipt of Estimate of Rs 5200 for Constructing Port Officer's Office &c at Paumban, Madura Dt.

+ Rs 5480 -

Re

0/9/8

Os Ba/8

[G/53.]
500--16-8-94.

Marine Department.

CHIEF SECRETARIAT, MADRAS.

Read the following paper G O dated 4 Aug 1894 No 138, Marine

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following ~~paper~~ :—

Endorsement of the Public Works Department, dated 14th August 1894, No. 771 D on letter from the Superintending Engineer, 6th Circle, d/ 16th July 1894 No. 421,

× through the Presidency Port Officer

Order: 20th August 1894, No. 337.

The estimates are approved and returned to the Public Works Department.

G. O. d/ 4. 8. 94, No. 138 will now be communicated to the Financial department for early orders.

× Vide No. 772 D 14-8-94

(True Extract)

A. D. G. Shelley
Capt RE
Under Secretary W. D.
for Chief Secy

To

The Public Works Depts with Plans & Estimates
" " Financial Depts
" " Presidency Port Officer.

P. W. CURRENT No. 6376

No. 71 W d/ 11-1-94
72 W d/ 11-1-94
625 W d/ 6-3-94

Govt. of {189 } Madras.

To

The Public Works Dept.

Encls 1 St (2 plans)

Recd. 27. 8. 94

Proceedings, dated 20 August 1894
No. 337.

Subject.

Approving & returning to the P.W.D. estimates for constructing an office for the Port-officer and Pamban &c. and Communicating to the Fin'l Dept. for early orders G.O. d/ 4th August 1894 No. 138 on the P.P.O's request that a sum of Rs. 5200 may be placed at the disposal of the P.W.D. for carrying out the works.

CAW 27-8-94

O.L.S. 314-R1/9

No. 771 Dy 14-8-94

Public Works Department.

Current No. 5480
Letter No. 137/145 P.W.
Dated 21st July 1894
From the Presidency Port Officer.

NOTE BY TECHNICAL SECTION.

Name of work. Constructing Port officers office & godowns & Dy. Telegraph Masters Quarters at Pamban in the Madura District.

Amount of Estimate Rs 5200

The estimates under review have been framed with reference to G.O. No. 71 W dated 11th Jany. 1894 & provide for the following works:—

(a)	Constructing Port officers Office Rs	1800
(b)	— do — do — 2 godowns —	2020
(c)	Dismantling & reconstructing Deputy Telegraph Masters Qrs. with out houses	1380
	Total estimate Rs	520

Port officers Office. In the report accompanying this estimate it is stated that the Port officer was consulted regarding the accommo-dation required for his office & that officer wanted the following viz. an office room 32'×16', record room 18'×12' & a centre room for the Public 18'×12', as the area pro-posed by the Port officer was consider-ed too large & as the cost to the hitherto very heavy, the S.E. has ed 2 rooms, one measuring for the Port officer and another 16'×14' for his clerk & records together with a front verandah 6 feet wide, which accommodation the S E considers to be quite sufficient for the Port Officers office.

The walls of this office are to be raised 10 feet high over a basement of 1'6" & built of brick in clay except around doors & windows for a depth of 9 inches & on top of walls for a depth of 18 inches which are to be of brick in chunam. The basement & foundations are to be of brick in chunam. The roof is to be gabled & covered with Mangalore tiles laid over teak reepers & teak couples, (couples placed 18" apart from centre to centre). The floor is to be of 6" concrete & plastered with ¼" cement & the walls plastered with 2 coats of chunam.

The scantlings allowed for roof timber are correct.

Port Officers office godowns: The Port officer requested provision to be made for 3 godowns, one for warps & anchors 27'×12' another for paints & oils 18'×12' & the third for storm signals 16'×12' but provision has been made for only two godowns each 20'×12' one for paint, oil & storm signals & the other for warps & anchors.

The walls of these godowns are to be raised 10 feet high over a basement of one foot & built of brick in clay except around doors
ws & top of walls which are
brick in chunam. The floor
downs are to be of ½" asphalt laid over a bed of concrete 4" thick. The roof is to be of corrugated iron laid over teak purlins supported on a wooden truss. The walls are to be plastered throughout with 2 coats of chunam.

The scantlings for roof timber are correct.

Deputy Telegraph Masters Quarters

This estimate provides for demolishing the existing thatched shed with outhouses and rebuilding the same in the compound of the Telegraph office.

The building is to be consist of 2 end rooms each 14'×12'6" & two centre rooms each 10'6"×12'6" with front & rear verandahs 8 feet wide. The outhouse accommodation is to be similar to those that are to be demolished, viz. cook room 12'6"×9 godown 9'×9' latrine 7'6"×4'0" & fowl house 3'6"×7'6" as per tracing plan.

The walls of the main rooms are to be raised 11'3" high over a basement of 2 feet & to be built of stone in mud throughout from stones available from the existing building. The floor is to be of concrete 4" thick & the roof of cocoanut leaves laid over old palmyrah couples & new cocoanut reepers. The walls are to be plastered with clay & whitewash all useful materials from the existing building are to be utilized in the construction of the new quarters.

The rates are fair except for the following which are slightly in excess of the Divisional schedule. These excess rates have been passed in the estimate for Port Officer's quarters sanctioned in G.O. No. 625 W dated 6th March 1,894.

Concrete ——	14....	against	12....
Brick in mud —	14....	-do-	13....
Cut stone work —	1-8..	-do-	1-...
Teakwood work	3.10..	-do-	3-8..

Nature of surface soil is reported to be sand 3 feet & the sub soil soft rock 2 feet.

The foundations are proposed to be laid of brick in chunam & concrete if concrete be provided throughout to ground level, for the office & godowns the excess will be Rs 35-

The roof of the godowns are proposed to be carried on a truss placed 10 feet apart & as the span is only 12 feet it is submitted that the corrugated iron may be carried on purlins & couples, couples placed 4 feet apart & the truss be done away with. There would be more head way & the roof much neater.

The estimates have been countersigned by the Presidency Port Officer. The original approximate estimates have been approved in

The Marine Dept. in its order No. 404 dated 17th Novr. 1893. embodied in G.O. No. 91 W dated 11th Jany. 1894.

8.viii.94

Building
Civil Wor

No: 2177 W. d/ 3rd September 1894 **PUBLIC WORKS DEPARTMEN**

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following

From the Presy: Port Officer, Madras. (H.E. No. 137/145 P.M. d/21.7.94)

Do: Marine dept —— (" " 138 d/4.8.94)

Do: Marine dept —— (" " 337 d/20.8.94)

5 Prev

The following estimates are returned to the Supdg Engineer VI Circle for sanction:—

Constructing an office for the Port officer at Pamben .... Rs 1800

Constructing two godowns for the Port office at Pamben ..... " 2,020

Reconstructing the Dy Telegraph Master's quarters at Pamben ... " 1,380

(40—1,000—23-2-94.)

the Port Officer and another 18'x14'

the works will be carried
out on funds as shewn
below being made
available by the Financial
department:—

Works ..	Rs.	5,200
Establishment ..		1,196
Tools & Plant ..		78
Total Rupees		6,474

CHMS
30/8 94

205

M 30/8

DESPATCHED
14 SEP. 94

T/thu
B G M

S. E. VI Circle with enclos. (15)
(4 places)

E. P.W. Accts,

Marine dept

Financial dept

My only [illegible] two
77' D sep [illegible] first give
attention arrangement
for sending [illegible]
14/9

6/11

CNo. 6[illegible]76

24-10-57 [illegible]

Govt. of {189 } Madras.
PUBLIC WORKS.

Pass 5-9-94

Dated

Recd. Encl.

G.O., 3/9 1894 No. 2177 W

Estimates

ertain — For the ~~con~~
d construction of an
ffice, with two godowns,
r the Port officer
t Pámban, & ~~the~~
construction of the Dy.
elegraph master's quarters
f that station, returned
the S.E. VI Circle
r sanction, and for
ecution when ~~in~~ funds are
~~ing provided~~ made
vailable by the Finl.
ept:

12/5

4/9 - 2.c.c 4/9

No. 6189

Govt. of (1894) Madras.
PUBLIC WORKS.

Pres
5/9/94

Dated

Recd. Encl.

G.O., 3/9 1894 No. 2176W

Students Hostel

at Chepâk

Orders describing the area proposed to be made over for the — & directing the Cons: Archt: ~~directed~~ to prepare the necessary plans ~~taking care to~~ allowing plenty of space for future extension.

80/IX

4/9

J.C.C.
4/9

1W/16 80/76

R 27/8

3rd September 1894, No. 2176 W., Public Works.

GOVERNMENT OF MADRAS.

PUBLIC WORKS DEPARTMENT.

Buildings and Roads.
Civil Works.

Read—the following paper :—

From H. IRWIN, Esq., C.I.E., Consulting Architect to the Government of Madras, to the Chief Engineer, Public Works Department, dated Chepâk, 18th August 1894, No. 1403.

With reference to G.O., No. 1735 W., dated 11th July 1894, I have the honour to forward a plan of the Chepâk ground showing the proposed site for the Victoria Students' Hostel. From G.O., No. 1280 W., dated 22nd May 1894, it would appear that the triangular spot cross hatched red in the enclosed plan is intended, but, judging from the accommodation required, I consider that the whole area up to the southern boundary wall and the road on the west side will be required.

2. Soliciting the orders of Government as to the extent of ground to be made over to the committee, I have, &c.

Order—dated 3rd September 1894, No. 2176 W., Public Works.

The area intended to be made over for the Students' Hostel is the whole of the space between the boundary wall, the canal and the road, and not merely the small triangle at the northern end of this space.

2. Plans should be prepared on this ground, care being taken to allow plenty of space for future extensions, what is not built over being used as a garden or for tennis courts, and the tank near the southern boundary being filled up if necessary.

(True Extract.)

Under Secy. to Govt., P.W.D.

To the Consulting Architect to Government.
,, Educational Department.
,, Honorary Secretaries, Victoria Students' Hostel Committee.

Exd. C. A. Munisawmy.
Spare Copies

BUILDINGS AND ROADS.
CIVIL WORKS.

Govt. of {1894} Madras.

PUBLIC WORKS.

Dated September, 3rd.

Recd. *Encl.*

G.O., 3rd Sept. 1894, No. 2176 W.

SEPTEMBER.

Students' Hostel at Chepak

Orders describing the area proposed to be made over for the — and directing the Consulting Architect to prepare the necessary plans allowing plenty of space for future extensions.

P. W. DEPARTMENT.

READ the following :—

Letter from the Consulting to Govt - Madras } H.E. No 1403 d/18 August 1894

FOR ORDERS.

225

W

CMM 22/8/94

I always understood that the portion of ground to be given for the Students' Hostel at Chepak was as described in Mr. Irwin's letter of Aug. 18. 1894 No. 1403 - and certainly not only the miserable little corner cross hatched red. The Consg. Architect I think should be instructed to make designs for the Hostel on the whole of the ground he alludes to - wherever it appears to him to come in best, taking care to leave plenty of space in his plans for future extensions. What is not built on shd. be made into a garden, and there wd. be no objection to filling in the tank - tennis courts too might be shown.

Circ.

The tank could be turned into an A1 swimming bath, I should say. But that may be left to the management of the Hostel

29/8/94

31/8

FOR ORDERS.

Site for the Students'
Hostel, Chepauk.

2176 W

No. 2176 W. d/ 3rd September 1894

R. 22/8

W

No. 265 W d/ 3-2-80
W d/ 5-5-81
91

No. 2176 W. d/ 3rd September 1894

PARTMEN

No. 3.

CHEPAUK COMPOUND IN 1893

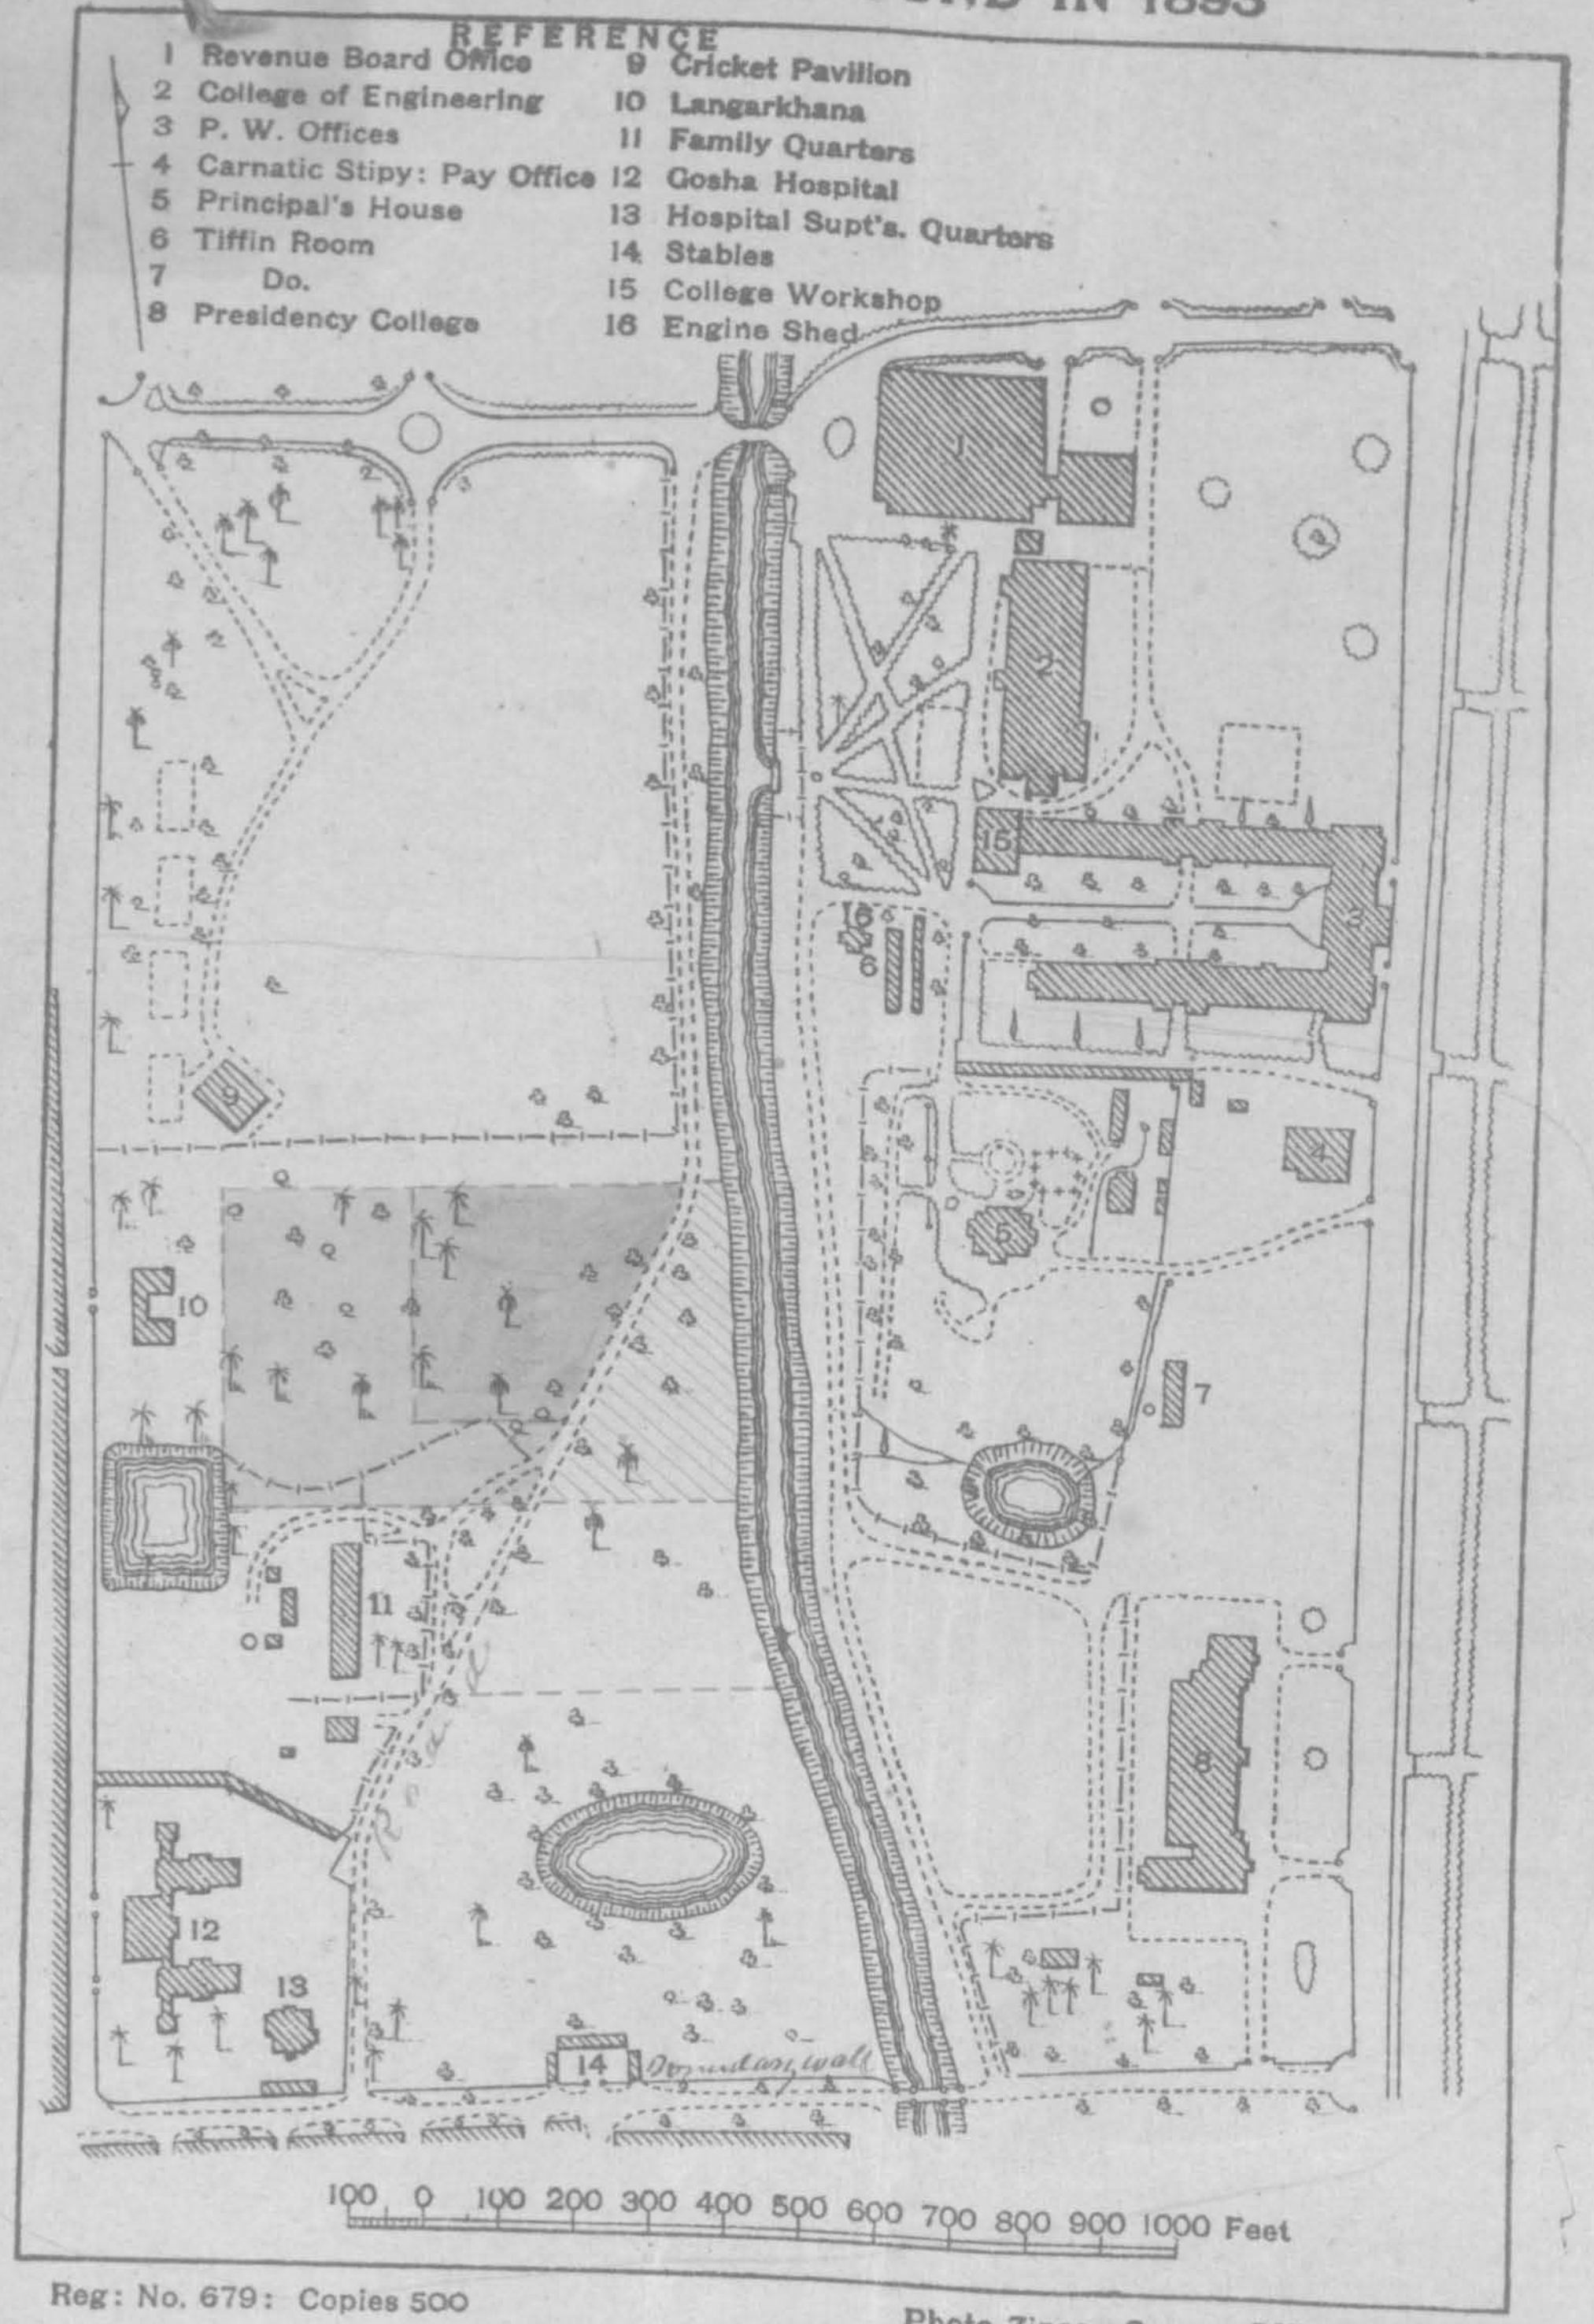

Reg: No. 679: Copies 500

Photo-Zinco., Survey Office, Madras.
1893.

Present ground coloured - - - - - - - - - - - - - - blue.
Additional ground proposed by Consulting Architect - - red.
Further portion asked for by Principal, cross hatched red.

FOR ORDERS.

1280 W

P.W. 5.2-1
28647/94
6189

4
Edl.
2
394

R. 22/8

W

R 27/8

No. 265 W d/ 5-5-81

No: 2176 W d/ 3rd September 1894.

C. A. / 1. 500 -29-1-94.

No. 1403

Office of the Consulting Architect to Govt.,
Chepauk, Madras,
18th August 1894.

From
Henry Irwin, Esq., C.I.E.,
Consulting Architect
to the Government of Madras,

To
The Chief Engineer
Public Works Department.

Sir,

1 Enclosures

With reference to G.O. No. 1735 W dated 11th July 1894, I have the honor to forward a plan of the Chepak ground shewing the proposed site for the Victoria Students Hostel. From G.O. No. 1280 W dated 22nd May 1894 it would appear that the triangular spot cross hatched red in the enclosed plan is intended, but judging from the accommodation required, I consider that the whole area up to the Southern boundary wall & the Road on the West side will be required.

2. Soliciting the orders of Government as to the extent of ground to be

made

d/ 5-5-81

No. 2176 lr d/ 3rd September 189

made over to the Committee

I have the honor to be
Sir
Your most obedient servant

Henry Irwin

Consulting Architect
to Government.

No. 7. 6189

No. 1280 w d/ 2-5-94
1735 w d/ 11-7-94

Public Works Department.

From

The Consulting Architect
to the Government of Madras.

To

The Chief Engineer
P. W. D.

No. 1403

Dated 18th
Despatched
Received 20th
August 1894.

No. of Enclosures. 1

Subject.

Requesting the orders of Govt: for the extent of ground to be made over to the Victoria Students Hostel Committee, in the Chepak Park.

O.L.S. 298 R3/4.

No. 2176 w d/ 3d September 1894.

PROCEEDINGS OF THE MADRAS GOVERNMENT.

Read the following

Letter from the Consg: Architect ——— (H. E. No. 1403 d/ 18.8.94)

3 Pair

W.A. 29/8/94

The area intended to be made over for the Students' Hostel is the whole of the space between the boundary wall, the canal and the road, and not merely the small triangle at the northern end of this space.

2. Plans should be prepared on this ground care being taken to allow plenty of space for future extensions,

(40—1,000—22-2-94.)

No. 1. 6189

No. 1280 W d/ 22-5-94
1735 W d/ 11-7-94

Public Works Department

what is not built over being used as a garden or for tennis courts, and the tanks near the southern boundary, being filled up if necessary

D 28. 8

~~The Hon. Mr. J. Grose~~ ... and initialed on the Cover

N. S.
18 Sep 94

Site for the Students' Hostel - Chepauk

Copy 23/8

T. Has
B. Cy

DESPATCHED
12 SEP. 94

Consg. Architect
Educational Dept.
Hony Secretaries,
Victoria Students Hostel
Comtee.

---

265 W d/ 3-2-80
W d/ 5-5-81

3rd September 1894, No. 2177 W., Public Works.

GOVERNMENT OF MADRAS.

PUBLIC WORKS DEPARTMENT.

Buildings and Roads.
Civil Works.

Read—the following papers :—

From the Presidency Port officer, Madras, dated 21st July 1894, No. 137/145 P.M.

G.O., dated 4th August 1894, R. No. 138, Marine.

Read—the following letter from the Presidency Port officer, Madras, dated 21st July 1894, No. 137/278 G. :—

I have the honour to request that a sum of Rs. 5,200, together with the usual percentage for establishment and tools and plant, may be placed at the disposal of the Public Works Department for carrying out the works noted marginally.

2. The estimates for the same have been duly countersigned and forwarded to the Chief Engineer, Public Works Department.

Three estimates.	RS.
1. Constructing Port officer's office at Pámban, Madura district ...	1,800
2. Constructing two godowns for Port officer's office at Pámban, Madura district	2,020
3. Removing and reconstructing Deputy Telegraph Master's quarters with out-houses at Pámban, Madura district	1,380
Total ...	5,200

Order—dated 4th August 1894, R. No. 138, Marine.

The receipt of the estimates from the Public Works Department will be awaited.

(True Extract.)

(Signed) J. F. PRICE,
Chief Secretary.

G.O., dated 20th August 1894, No. 337, Marine.

Read—endorsement of the Public Works Department, dated 14th August 1894, No. 771 D., on letter (through the Presidency Port officer) from the Superintending Engineer, VI Circle, dated 6th July 1894, No. 421.

Order—dated 20th August 1894, No. 337, Marine.

The estimates are approved and returned to the Public Works Department.

G.O., dated 4th August 1894, No. 138, will now be communicated to the Financial Department for early orders.

(True Extract.)

(Signed) J. F. PRICE,
Chief Secretary.

ORDER—dated 3rd September 1894, No. 2177 W., Public Works.

The following estimates are returned to the Superintending Engineer, VI Circle, for sanction:—

	RS.
Constructing an office for the Port officer at Pámban	1,800
Constructing two godowns for the Port office at Pámban	2,020
Reconstructing the Deputy Telegraph Master's quarters at Pámban...	1,380

2. The works will be carried out on funds, as shown below, being made available by the Financial Department:—

	RS.
Works	5,200
Establishment	1,196
Tools and plant	78
Total ...	6,474

(True Extract.)

Under Secy. to Govt., P.W.D.

To the Superintending Engineer, VI Circle, with enclosures.
„ Examiner, Public Works Accounts.
„ Marine Department.
„ Financial „

Exd. C. A. Munisawmy.
Spare Copies

Copy to,
the Public Works Department.

For Chief Secretary

BUILDINGS AND ROADS.
CIVIL WORKS.

Govt of {1894} Madras.

PUBLIC WORKS.

Dated September, 3rd.

Recd. *Encl.*

G.O., 3rd Sept. 1894, No. 2177 W.

SEPTEMBER.

Estimates

Certain — for the construction of an office, with two godowns, for the Port officer at Pámban, and the reconstruction of the Deputy Telegraph Master's quarters at that station, returned to the Superintending Engineer, VI Circle, for sanction and for execution when funds are made available by the Financial Department.

[G./53]
00—26-6-94.

Marine Department.

CHIEF SECRETARIAT, MADRAS.

Read the following paper
G O dated 4 Aug. 1894, No 138 Marine

2 Par

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following paper :—

From the Presidency Port Officer, Madras, dated 21st July 1894, No $\frac{137}{278}$ G.:-

I have the honour to request that a sum of Rs (5,200) five thousand and two hundred, together with the usual percentage for establishment and tools and plant may be placed at the disposal of the Public Works Department for carrying out the works noted marginally.-

2. The Estimates for the same have been duly countersigned and forwarded[×] to the Chief Engineer, Public Works Department.

3 Estimates

1.	Constructing Port Officer's office at Pamban Madura District	Rs 1800
2.	Do 2 Godowns for do at do	" 2020
3.	Removing and reconstructing Deputy Telegraph Master's quarters with out houses at do	" 1380
	Total	Rs 5200

× Not received at Act as amended

Order, dated 4th August 1894, R No 138

The receipt of the Estimates from the Public Works Department will be awaited.

(True Extract)
J Francis
Ag. Asst Secretary
for Chief Secretary

Copy to,
the Public Works Department.

265 W d/ 3-2-90

d/ 5-5-87

[G./53.]
500—23-11-93.

Department.

CHIEF SECRETARIAT, MADRAS.

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following paper:—

3

Govt. of {1894} Madras.

P. W. CURRENT No. 5921

To

The Public Works Depts.

No. 772 D dy 14-8-'94

D

Recorded with reference to endt. No. 771 D dy 14th August 1894.

Regtd. 9-8-94

Recd 6/8/94

Proceedings, dated 4th Augt. 1894.
R No. 138

CMB 13/8/94

Subject.

Awaiting receipt of Estimate of Rs. 5200 for Constructing Port Officer's Office &c at Paumban, Madura Dt.

+ Amt. 5480.

Re

0/9/8

Os Ba/8s

No. 265 W dt 3-2-80
W dt 5-5-81
-91

500—16-8-94.

Marine Department.

Read the following paper
G.O. dated 4 Aug 1894 No. 138, Mar

LP

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following ~~paper~~:—

Endorsement of the Public Works Department, dated 14th August 1894, No. 771 D on letter from the Superintending Engineer, 6th Circle, dt 16th July 1894 No. 421,

× through the Presidency Port Officer

Order: 20th August 1894, No. 337.

The estimates are approved and returned to the Public Works Department.

× Vide No. 772 D 14-8-94

G.O. dt 4.8.94, No. 138 will now be communicated to the Financial department for early orders.

(True Extract.)

A. D. G. Shelley
Capt. RE
Under Secretary P.W.D.
for Chief Secy

To

The Public Works Dept. with Plans & Estimate
" " Financial Dept.
" " Presidency Port Officer.

P. W. CURRENT No. 6376

Govt. of {189 } Madras.

No. 71 W d/ 11-1-94
72 W d/ 11-1-94
625 W d/ 6-3-94

To

The Public Works Dept.

Entd. 15 (J. Mano)
Recd: 27. 8. 94

Proceedings, dated 20 August 1894
No. 337.

Subject.

Approving & returning to the P. W. D. estimates for constructing an office for the Port-Office and Pamban &c. and Communicating to the Finl. Dept. for early orders G.O. d/ 4th August 1894 No 138 on the P. P. O's request that a sum of Rs. 5200 may be placed at the disposal of the P. W. D. for carrying out the works.

CAW
27. 8. 94.

O.L.S. 314. R1/9

---

265 W d/ 3-2-80
54 W d/ 5-5-81
12-4-91

No. 771 Dd 14-8-94

Public Works Department.

Current No. 5480
Letter No. 137/145 P. W.
Dated 21st July 1894
From the Presidency Port officer.

NOTE BY TECHNICAL SECTION.

Name of work. Constructing Port officers office & godowns & Dy. Telegraph Masters Quarters at Pamban in the Madura District.

Amount of estimate Rs 5200
[illegible]

The estimates under review have been framed with reference to G.O. No 71 W dated 11th Jany. 1894 & provide for the following works:-

(a) Constructing Port officers office Rs 1800
(b) - do - do - 2 godowns - 2020
(c) Dismantling & reconstructing Deputy Telegraph Masters Qrs. with out houses 1380
Total estimate Rs 5200

Port officers office: In the report accompanying this estimate it is stated that the Port officer was consulted regarding the accommodation required for his office & that officer wanted the following viz. an office room 32'×16', record room 18'×12' & a centre room for the public 18'×12', as the area proposed by the Port officer was considered too large & as the cost would be very heavy, the E. E. has only provided 2 rooms, one measuring 14'×1

RRENT No 6376

No 71 W of 11-1-94

for the Port Officer and another 16'x14' for his clerk & records together with a front verandah 6 feet wide, which accommodation the S E considers to be quite sufficient for the Port Officer's office.

The walls of this office are to be raised 10 feet high over a basement of 1'6" & built of brick in clay except around doors & windows for a depth of 9 inches & on top of walls for a depth of 18 inches which are to be of brick in chunam. The basement & foundations are to be of brick in chunam. The roof is to be gabled & covered with Mangalore tiles laid over teak reepers & teak couples, (couples placed 18" apart from centre to centre). The floor is to be of 6" concrete & plastered with ¼" cement & the walls plastered with 2 coats of chunam.

The scantlings allowed for roof timbers are correct.

Port Officer's Office godowns: The Port Officer requested provision to be made for 3 godowns, one for warps & anchors 27'x12' another for paints & oils 18'x12' & the third for store signals 16'x12' but provision has been made for only two godowns each 20'x12' one for paint, oil & store signals & the other for warps & anchors.

The walls of these godowns are to be raised 10 feet high over a basement of one foot & built of brick in clay except around doors [illegible] & top of walls which are [illegible] in chunam. The floors are to be of ½" asphalte laid over a bed of concrete 4" thick. The roof is to be of corrugated iron laid over teak purlins supported on a wooden truss. The walls are to be plastered throughout with 2 coats of chunam.

The scantlings for roof timber are correct.

Deputy Telegraph Masters Quarters

This estimate provides for demolishing the existing thatched shed with outhouses and rebuilding the same in the compound of the Telegraph office.

The building is to be consist of 2 end rooms each 14'x12'6" & two center rooms each 10'6"x12'6" with front & rear verandahs 8 feet wide. The outhouse accommodation is to be similar to those that are to be demolished, viz. cook room 12'6"x9 godown 9'x9' latrine 7'6"x4'0" & fowl house 3'6"x7'6" as per tracing plan.

The walls of the main rooms are to be raised 11'3" high over a basement of 2 feet & to be built ~~with~~ of stone in mud throughout from stones available from the existing building. The floor is to be of concrete 4" thick & the roof of cocoanut leaves laid over old palmyrah couples & new cocoanut reepers. The walls are to be plastered with clay & whitewash

All useful materials from the existing building are to be utilized in the construction of the new quarters.

The rates are fair except for the following which are slightly in excess of the Divisional schedule. These excess rates have been passed in the estimate for Port Officers quarters sanctioned in G.O. No. 625 W dated 6th March 1894.

Concrete ——	14....	against	12....
Brick in mud —	14....	-do-	13....
Cut stone work —	1-8..	-do-	1....
Teakwood work	3-10..	-do-	3-8..

Nature of surface soil is reported to be sand 3 feet & the sub soil soft rock 2 feet.

The foundations are proposed to be laid of brick in chunam & concrete. If concrete be provided throughout to ground level for the office & godowns the excess will be Rs 35/-

The roof of the godowns are proposed to be carried on a trusses placed 10 feet apart & as the span is only 12 feet it is submitted that the corrugated iron may be carried on purlins & couples, couples placed 4 feet apart & the trusses be done away with. There would be more head way & the roof much neater.

The estimates have been countersigned by the Presidency Port Officer. The original approximate estimates have been approved in

the Marine Dept. in its order No. 404 dated 17th Nov. 1893. embodied in G.O. No 71 W dated 11th Jany 1894.

Jno.
