

752
Public Works (1896) Department.

G.O., No 2750

DATED 25 September
1896

25/9

[Despatch Abstract.]

Sub Registrar's Office at Chettiikulam: Re-
vised estimate of Rs. 2950 for constructing a
— in Trichinopoly D^y Sanctioned.

==

10
4

25/9 27/1

Revised estimate of Rs. 2,950 for constructing a —, in Trichinopoly district, sanctioned.

GOVERNMENT OF MADRAS.
PUBLIC WORKS DEPARTMENT.

Buildings and Roads.
Civil Works.

Read—the following paper:—

G.O., No. 1307, Judicial, dated 14th August 1896.

Read—the following letter from the Superintending Engineer, VI Circle, dated 18th July 1896, No. 1134 T.C.:—

I have the honour to inform you that the Executive Engineer, Trichinopoly, has submitted a revised estimate amounting to Rs. 2,950 for the marginally-noted work. The original estimate of Rs. 2,440 for the work was approved by you in No. 2679, dated 28th June 1894, and sanctioned by me in Register No. 9 of 1894-95. In the present estimate, provision has been made for certain extra works not originally provided, but since found necessary for reasons given in the report. They are compensation for a portion of the land taken up for the building, erection of mud walls all round the compound, with a small gate and construction of a culvert, &c.

2. As regards the provision for compensation, for which no explanation has been given in the estimate and report, I enclose a copy of the Executive Engineer's letter, No. 608 S.E., dated 4th February 1896, from which it would appear that the amount provided is admissible.

3. The Executive Engineer recommends the substitution of cement concrete flooring for square bricks, as the latter cannot be obtained of good quality; he has accordingly revised the estimate. Under the circumstances, the revised estimate is accepted and it is herewith forwarded for your countersignature and submission to Government for sanction.

Endorsement of the Inspector-General of Registration, dated 23rd July 1896, G. No. 4610.

Submitted for the sanction of Government.

2. The construction of a Sub-Registrar's office at Chettikulam, in the Trichinopoly district, was sanctioned in G.O., No. 2088, Judicial, dated 7th October 1893.

Order—No. 1307, Judicial, dated 14th August 1896.

The revised estimate, aggregating Rs. 2,950, is approved and will be transferred to the Public Works Department.

(True Extract.)

(Signed)

F. J. WILSON,
for Chief Secretary.

No. 2750 W., 25TH SEPTEMBER 1896.

ORDER—No. 2750 W., dated 25th September 1896.

The revised estimate, amounting to Rs. 2,950, for constructing a Sub-Registrar's office at Chettikulam, in the Trichinopoly district, is sanctioned in supersession of the estimate of Rs. 2,440 sanctioned by the Superintending Engineer, VI Circle.

2. This sanction has been registered as Provincial No. 82 W. of 1896-97, and classified as Civil Buildings—Original Works.

(True Extract.)

Under Secretary to Government.

To the Superintending Engineer, VI Circle, with nine enclosures.
" Examiner, Public Works Accounts.
" Judicial Department.

Exd. T. K. Narayana Aiyangar.

PROCEEDINGS OF THE MADRAS GOVERNMENT.

READ the following

Proceedings of Govt in the Judicial Dept. No. 130742, August 1896

The revised estimate amounting to Rs. 2,950, for constructing a Sub-Registrar's office at Chettikulam in the Trichinopoly District is sanctioned in supersession of the estimate of Rs. 2,440 sanctioned by the Suptg. Engineer, VI Circle.

2. This sanction has been registered as Provincial No. 82 W of 1896-97 and classified as Civil Buildings, Original Works.

To the S.E. VI Circle with enclosures.
" Exar. P.W. Accts.
" Judicial Dept.

Current No. 1652
Letter No. 1309
Dated 14 August 1896
From the District Engineer

NOTE BY TECHNICAL SECTION.


Name of work Constructing Sub-Registrars Office at Chettikulam, Trichinopoly Dist.
Amount of estimate Rs 2950.

The S.E. VI Circle, submits a revised estimate, amounting to Rs 2950, for constructing a Sub-Registrars Office at Chettikulam in the Trichinopoly Dist. which, in lieu of the original estimate, amounting to Rs 2440, sanctioned by himself in 1894-5 together with a deviation statement in 1896, for compensation of land originally omitted under the notification in 1896, for that the land was Govt. property, making total sanction for the work Rs 2508.

The excess of Rs 442 or 18.1% over the original sanction is due to the following causes:-

- (1) To the provision of certain new items since found absolutely necessary, such as, (a) Constructing mud compound wall to the gate & pipe Rs 248, (b) Constructing masonry gate pillars with wooden gate Rs 48 and (c) for constructing a road culvert.

Two sections for the compound wall for the culvert have been submitted. The foundations for the compound wall have been provided for in the estimate, with detail quantities marked in green pencil. The section is thus:-

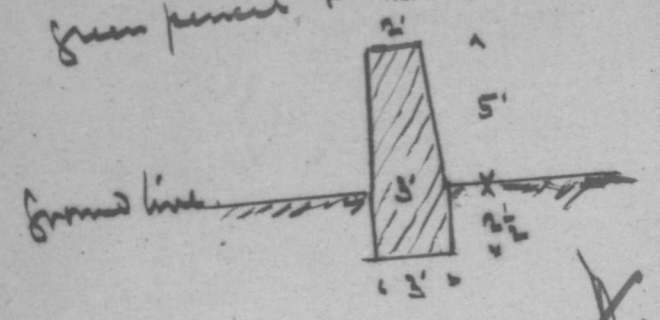

Is there no section for the compound wall or for the culvert? And for the former then seem to be no foundations provided.


* This is not clear provided in the original estimate.

copy 10.9.96

Sanctioned 18.9.96

In the original estimate, amounting to Rs 2440, sanctioned by the S.E. VI, no provision had been made for compensation for land, vide original estimate attached. Since this estimate was sanctioned a deviation statement was submitted by the S.E. VI vide his letter W. 608 SE dated 4.12.1896 in which provision was made for Rs 57.8 + 10.8 for compensation hence the estimate.

How compound wall of masonry at Chettikulam was made at 1894-5. How compound wall of masonry at Chettikulam was made at 1894-5. How compound wall of masonry at Chettikulam was made at 1894-5.

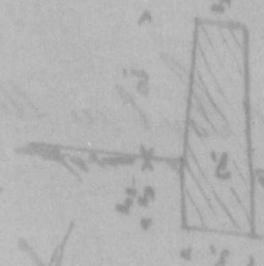

T.K. B.M.

How compound wall of masonry at Chettikulam was made at 1894-5. How compound wall of masonry at Chettikulam was made at 1894-5. How compound wall of masonry at Chettikulam was made at 1894-5.

Culvert Rs 90, making in all Rs 386,

(2) To increase in rates in the items of earth filling and cement plaster 42.

(3) To derivation in the rate head of flooring and in the provision of cutlery edging to verandah & steps 41.

(4) To the omission of wall flats in original estimate & for setting wood also blocking 20.

Total Purposes 489.

Deduct savings in the items of contingencies 47

Total excess requiring sanction 442.

The following rates have been increased:-

Earth filling Rs 7.8.3 against Rs 2.8.
Cement plaster 8.0.0 - do - 5.0.0

These high rates are reported to be due to carriage of cement for 26 miles from Trichinopoly & to the cost of good earth from a distance.

The revised estimate has been countersigned by the D.C. of the District.

5.9.96

...

Public Works (1896) Department.

CURRENT No. 7652

Order

From The Judicial Department.

No. 1507.

Dated 14th
Received 24th } August 1896.
Enclosures 9
Spare copies -

SUBJECT.

Approving and transferring to the P.W.D. the revised estimate aggregating Rs. 2,950 for constructing an Office building for the Sub-Registrar of Chettikulam, Trichy Dist.:

O.L.S. 384 Sent again
R12/9 14/9 R25/9

READ the following paper :—

From the Superintending Engineer, 6th Circle, dated
18th July 1896, No. 1134 T.C.

I have the honour to inform you that the Executive Engineer, Trichinopoly, has submitted a revised estimate amounting to Rs. 2,950 for the marginally noted work. The original

Constructing an office building for the Sub-Registrar at Chettikulam, Musiri Taluk. estimate of Rs. 2,440 for the work was approved by you in No. 2679, dated 28th June 1894, and sanctioned by me in Register No. 9 of 94-95. In

the present estimate, provision has been made for certain extra works not originally provided, but since found necessary for reasons given in the report. They are compensation for a portion of the land taken up for the building, erection of mud walls all round the compound, with a small gate and construction of a culvert &c.

2. As regards the provision for compensation, for which no explanation has been given in the estimate and report, I enclose a copy of the Executive Engineer's letter, No. 608, S.E., dated 4th February 1896, from which it will appear that the amount provided is admissible.

3. The Executive Engineer recommends the substitution of cement concrete flooring for square bricks, as the latter cannot be obtained of good quality; he has accordingly revised the estimate. Under the circumstances, the revised estimate is

is accepted and it is herewith forwarded for your counter-
signature and submission to Government for sanction.

Endorsement of the Inspector-General of Registration,
dated 23rd July 1896, GNo. 4610, on the above.

Submitted for the sanction of Government.

2. The construction of a Sub-Registrar's office at
Chettikulam, in the Trichinopoly district, was sanctioned in G.O.
No. 2088, Judicial, dated 7th October 1893.

O R D E R:-No. 1307, dated 14th August 1896..

The revised estimate aggregating Rs. 2,950 is
approved and will be transferred to the Public Works Department.

(True Extract)

Thulm
for Chief Secretary.

To
The Inspector-General of Registration.
,, Public Works Department. (with enclos. in original) ✓

8.4
